

Job Stamp 04-0120F4 SFOBB SAS
-------------------------------------

Construction Calendar	385			
Project working days no.	595			
Date	01/02/2008			
Inspectors	Start	9:30	Stop	15:00
Hours				
Shift Hours	Start	6:30	Stop	15:00

**Description of Operation:**

- See Lalit Mathur's diary for ABF labor, equipment, materials, weather, and comments.
- Daily activity of Regional Steel (R.S.) and ABF
  - R.S. continued to place B1 and B2 transverse bars at west corners

Fig. 1



- Jason and Kurt torqued 26 couplers at B1 layer, which were marked with a red paint. The wrench number is 2007/253582. They started it from north west region to south west region.

Fig. 2

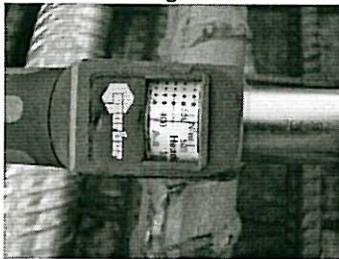


Fig. 3



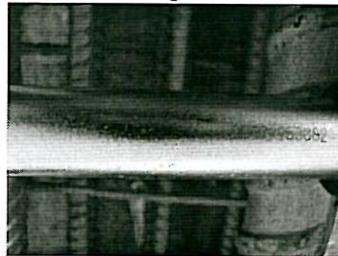


Fig. 4

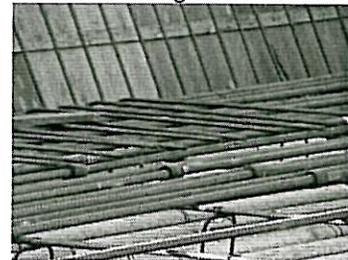

- R.S. placed supporting bars for B1 transverse bars around W2E.
- Formwork at north side for concrete pouring from ABF

Fig. 5

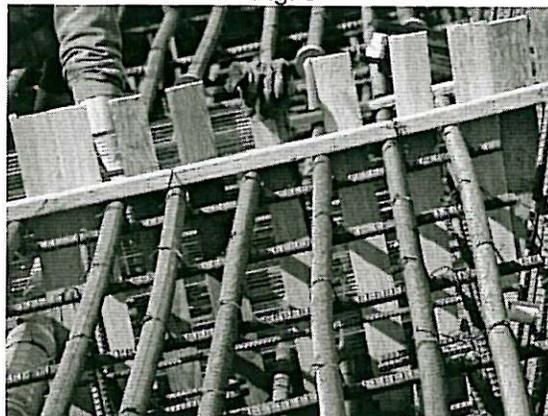

➤ Note


- Attend the internal staff and TTW meeting from 7:30 to 9:00.
- Robert Wong and Frances Maroni visited the job site around 10:30.
- Informed John, a foreman, that B2 transverse bars need to be pulled up (see punch list).
- See Matt Bruce's diary for detailed activities and comments related to post-tensioning and other issues.
- See Pamela Gagnier's diary for additional comments.

➤ Punch list

- 3 full-length transverse bars (B2) need to be pulled up. Each bar has 3 couplers.
- 6 short transverse bars (B2) need to be pulled up.

Inspector:

SeongHyeok Song



Trans Engineer (C)/Asst. Struct. Rep
