

Job Stamp

04-0120F4

SFOBB SAS

Construction Calendar

399

Project working days no.

609

Date

01/16/2008

Inspectors

Start

10:00

Stop

15:00

Hours

Shift Hours

Start

6:30


Stop

15:00

Description of Operation:

- See Lalit Mathur's diary for ABF labor, equipment, materials, weather, and comments.
- Daily activity of Regional Steel (R.S.) and ABF
 - R.S. started to place hair-pins.

Fig. 1

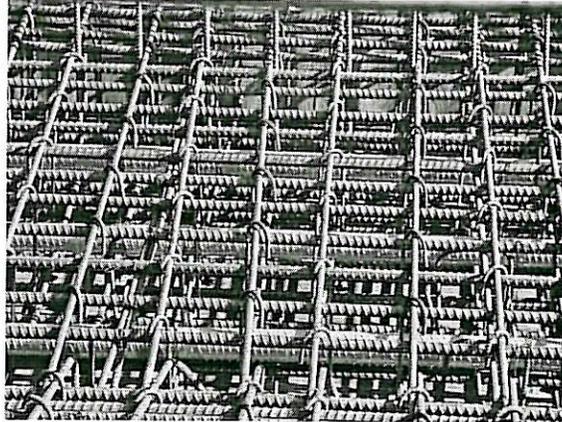


- R.S. started to place flexi-ducts at both sides.

Fig. 2



➤ Note

- Counted the total number of hoops placed today and compared them with the plan (see below the figure).

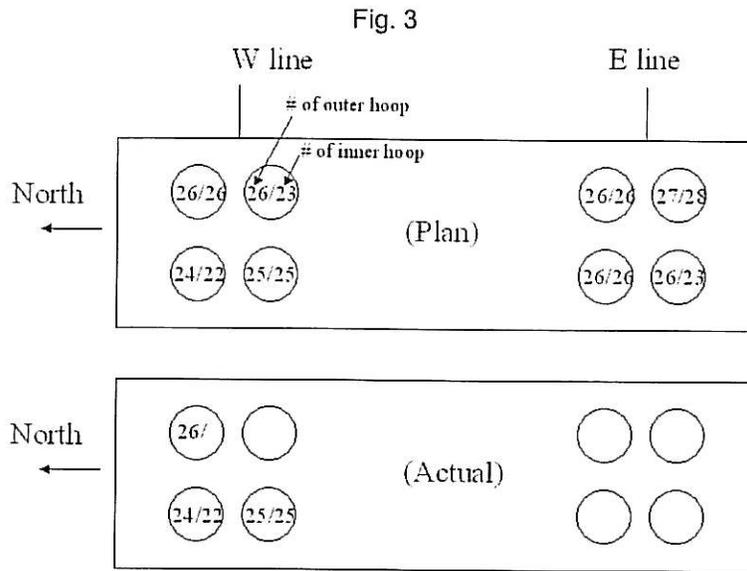

- Had a conversation with Pam and Ron regarding the spacing of the vertical bars which will be placed at solid areas (see plan 497S18).
- ABF contractor visited the job-site for the quality control of the couplers torqued.

Fig. 4

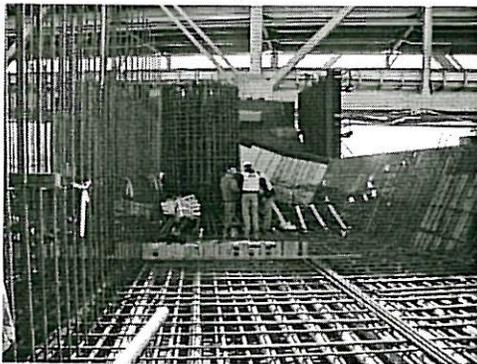


Fig. 5



- See Matt Bruce's diary for detailed activities and comments related to post-tensioning and other issues.
- See Pamela Gagnier's diary for detailed conversation with the contractors and decision made.

➤ Punch list

- 3 full-length transverse bars (B2) need to be pulled up.
- B2 full-length transverse bars need to be torqued. Each bar has 2 couplers.
- 6 short transverse bars (B2) need to be pulled up.
- 1 full-length transverse bar (B3) at west corner needs to be pulled up.
- The B1 transverse bar at east corner need to be replaced due to the malfunction of a mechanical coupler.
- The spacing of the hoops at ESW column.

Inspector:

SeongHyeok Song

A handwritten signature in blue ink, appearing to be 'SeongHyeok Song'.

Trans Engineer (C)/Asst. Struct. Rep
