

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. **46.B**
Date the Shift Began: **3/7/08**
 NIGHTWORK **FRIDAY**
Shift Hrs Start **6:30** Stop **15:00**
Inspector's Hrs Start **6:30** Stop **15:00**

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT



Location: W2 Cap Beam	7-day const. cal.: 450	Weather: partly cloudy
Remark: scaffold/minor formwork	Project work day: 660	High 62F/Lo 41F

Description of Operation:
Up above:
- continue to sandblast/clean concrete (north side)
- continue to build scaffolding (east face)
below:
- no work observed on Hinge K assembly
- begin minor formwork for pour 2

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.					IDLE OR DOWN	REMARKS		
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)						Name	Classification	Prime / Sub

For equipment and personnel hours, please see LALIT MATHUR'S diaries.

Matt Bruce (Caltrans) states that cracks are very obvious for the south side of pour 1. I checked the limits of pour 2 (for the intermediate diaphragm) marked by X's engraved into the concrete. They are correct - as measured off center of the longitudinal diaphragm. Scaffolding continued for the east side of W2. A timber panel was being mobilized back and forth between the ground to above for proper measurements and fabrication. Attached pictures show the extent of the drilling for the HS rods in the formwork thus far.

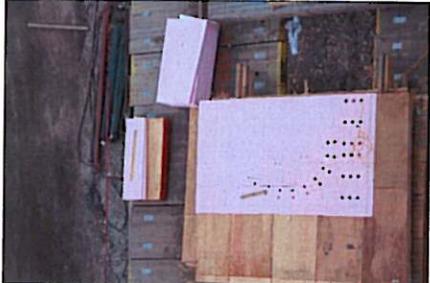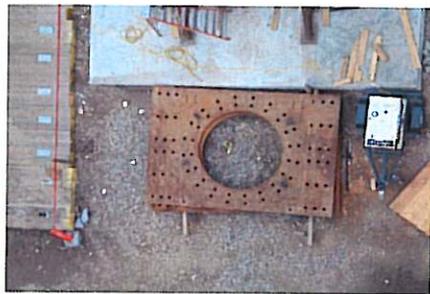

Materials:

Insp. Hrs.	
REG:	INTERMITTENT
OT:	INSPECTION

David Chung
DAVID CHUNG
REC'D ON MAR 22 10:03:07

TE/CT
Title
