

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	457			
Project Work Day No.:	667			
Date	03/14/2008			
Inspectors	Start	12:00	Stop	13:10
Hours				
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

Weather: Partly overcast with mild temperature - Hi 57 F Lo 45 F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Erected vertical HP and double channel strongbacks for the east forms and worked on connections.
- Diaphragm, east and west vertical face gang form construction continues.
- Fabrication of continuity tendon blockout forms.
- Sandblasting and cleaning construction joint on the north side.
- Began chipping excess concrete on the L and T-bars near W2E with a impact hammer.

RPS

- Were not onsite today and they are scheduled to return mid March.

Office Work:

- Assisted Lalit with writing the letter regarding the coring samples taken yesterday.
- Rick Morrow, Lalit Mathur, Pamela Gagnier, Ron Matin, David Chung and myself met with Jim Davidson at the Caltrans Burma Road office to discuss coring samples taken yesterday.
- Wrote todays diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow




File Name:	DSC00963
Date:	03-14-08
By Int:	M Bruce

Description: Impact hammer used to remove excess concrete on L and T-bars near W2E.

File Name:	DSC00968
Date:	03-14-08
By Int:	M Bruce

Description: Formwork construction for miscellaneous locations in the W2 cap beam.

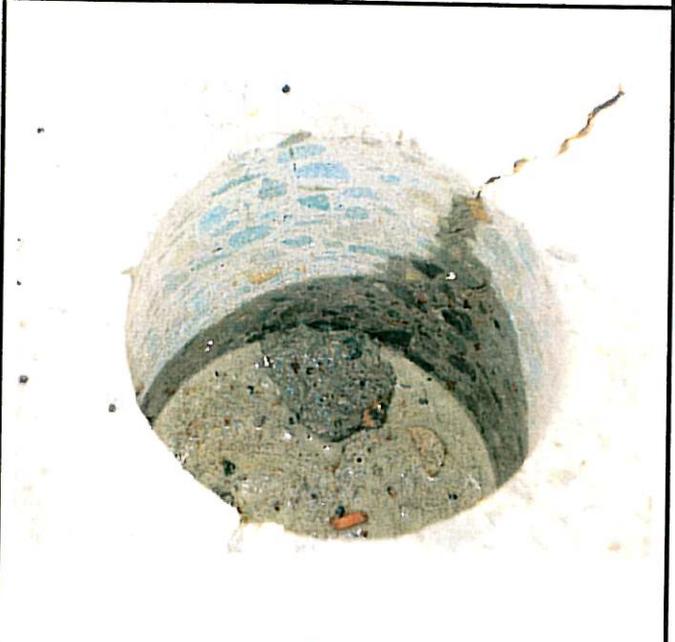

File Name:	DSC00972
Date:	03-14-08
By Int:	M Bruce

Description: Work on east face strongback connections.

File Name:	DSC00982
Date:	03-14-08
By Int:	D Chung

Description: Water that was left in the hole the previous day was removed from the coring hole today.
