

Job Stamp 04-0120F4 SFOBB SAS
-------------------------------------

Const. Calendar:	499			
Project Work Day No.:	709			
Date	04/25/2008			
Inspectors	Start	08:00	Stop	12:00
Hours		12:30		14:30
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

Weather: Sunny with mild temperature - Hi 74F Lo 52F (per weather.com forecast)

**Description of Operations @ W2 Cap Beam:**

**ABF**

- Continued assembling/building water cooling system for pour number 2.
- Continued installing form ties, plates, washers, and nuts for the northwest wall.
- Finished placing cooling pipes in the northwest wall.
- Continued blockout for the northwest wall with shear keys.
- Placed the west face(north side) of the jacking saddle support block form.
- Erected/closed vertical southwest wall forms.
- Installed dehumidification support bolts in the northwest wall which need to be leveled, see RFI 1249 for additional details.

**RPS**

- Continued to to place 29JL bars in the north jacking saddle support block, see sheet 497S7R1. The couplers shipped to the jobsite were too short. TY-Lin verbally approved splicing the couplers with #29 straight bars (full length) with the short couplers to achieve proper development length.
- Completed placement of the #32HV rebar in the south east section of the jacking saddle support block. The spacing of the 23-25HT01 bars doesn't follow the pattern on sheet 497S6R1 per RPS shop drawings. Also the bar spacing doesn't follow the angle of the forms.
- Placed 25L5L01 to 25L5L07 spliced bars the southeast wall, see sheets 478R1, 480R1, and 481R1 for details.
- Completed placing #25 T-Headed horizontal ties in the northwest wall in the vertical section of the wall, see sheet 495R2 for details.

**Office Work:**

- Wrote todays diary.

**Inspector:**

Matt Bruce Matt Bruce Transportation Engineer (D)

REC'D '08 MAY-31 #004891

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow




File Name:	DSC01534		
Date:	04-25-08	By Int:	D Chung

Description: Assembling/building water cooling system for pour number 2. The main pipes are being placed in the center of the W2 falsework on the west column.

File Name:	DSC01538		
Date:	04-25-08	By Int:	D Chung

Description: Miscellaneous work on the northwest wall.

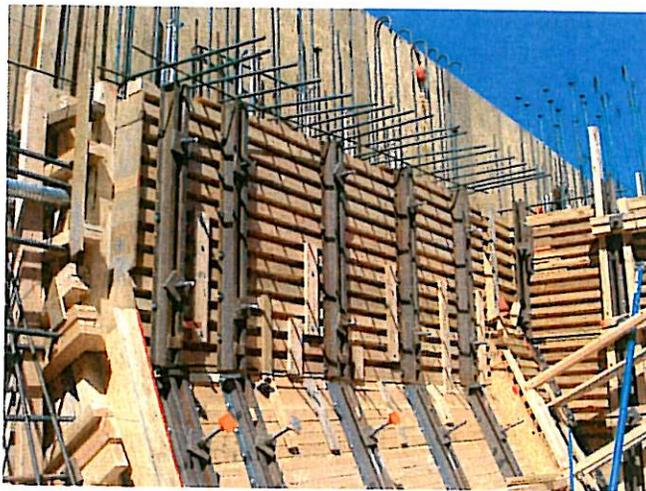

File Name:	DSC01541		
Date:	04-25-08	By Int:	D Chung

Description: Southwest wall construction to date.

File Name:	DSC01543		
Date:	04-25-08	By Int:	D Chung

Description: Placement of the #32HV rebar in the south east section of the jacking saddle support block.
