

2/1/08

| |
|-------------------------------------|
| Job Stamp 04-0120F4 SFOBB SAS |
|-------------------------------------|

| | | | | |
|-----------------------|------------|-------|------|-------|
| Const. Calendar: | 574 | | | |
| Project Work Day No.: | 784 | | | |
| Date | 07/09/2008 | | | |
| Inspectors | Start | 09:20 | Stop | 11:20 |
| Hours | | 12:40 | | 14:30 |
| Shift Hours | | 07:00 | | 15:30 |

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

Weather: Hazy with warm to hot temperature - Hi 95F Lo 65F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Continued to install plywood for the void area falsework in the northeast quadrant, see photo below.
- Continued to work on access opening for pour 3, and 5 on the west side of W2 near the stairtowers sitting on the soffit.
- Mobilized falsework bents for the west quadrants on the Hinge K working slab, see photo below.
- Began fabricating west wall sloped forms on the ground, see photo below.
- Installed one HP vertical waler in between the W2E Hinge K assemblies.
- Installed falsework removal rods in the northwest void area.

RPS

- Continued placing L-bars through the south W2E column cages and began placing T-bars through the center section of the pier column cages, see Pamela's diary for details.
- Miscellaneous work in the W2E cages such as profiling continuity tendons E-30B and E-31B, tying L-bars and T-bars, tying #43 vertical bars, etc.
- Began layout of L-bars and T-bars at pier W2W column cages.

Surveying Work:

- Set elevations on rebar adjacent to continuity tendons W-20B through W-37B on both the west and east sides of the W2W column cages with David Chung.

Office Work:


- Attended weekly Team Concrete meeting with TY-Lin and ABF at 8:00am.
- Reviewed extra work bills for CCO#46 (Macalloy rod thread testing) done June 16,17, and 18.
- Wrote today's diary.

Inspector:

Matt Bruce *Matt Bruce* Transportation Engineer (D)

REC'D *08 JUL-22 #005814

| | |
|----------------|----------------------------|
| EA | 04-0120F4 |
| Co-Rte-KP (PM) | SF-080-13.2/13.9 (8.2/8.7) |
| Structure Rep. | Rick Morrow |

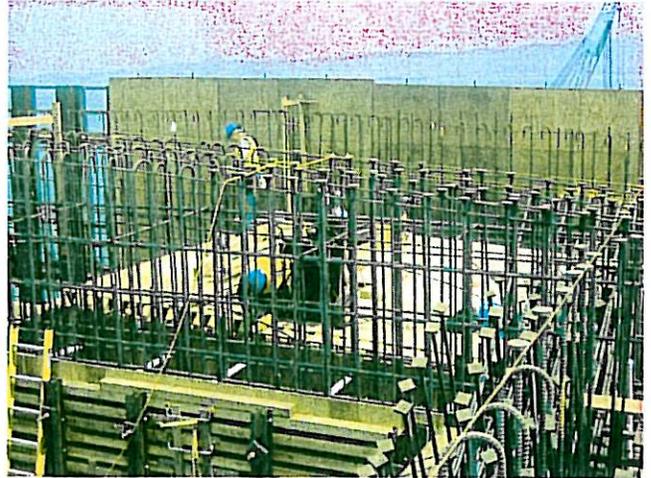


| | |
|------------|-------------------------|
| File Name: | July-09-2008 W2 Cap 001 |
| Date: | 07-09-08 |
| By Int: | M Bruce |

Description: L and T-bar placement to date at W2E.

| | |
|------------|-------------------------|
| File Name: | July-09-2008 W2 Cap 002 |
| Date: | 07-09-08 |
| By Int: | M Bruce |

Description: Installing plywood for the void area falsework in the northeast quadrant.

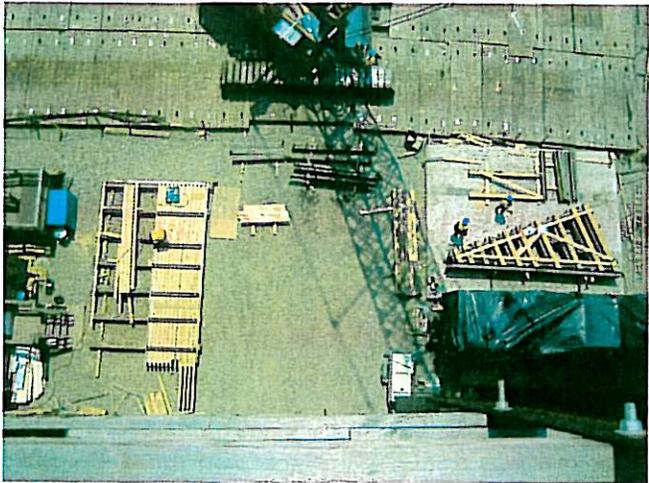

| | |
|------------|-------------------------|
| File Name: | July-09-2008 W2 Cap 003 |
| Date: | 07-09-08 |
| By Int: | M Bruce |

Description: Photo taken of the void area formwork construction on the west side of the W2 cap beam.
