

dkm

Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar:	575			
Project Work Day No.:	785			
Date	07/10/2008			
Inspectors	Start	10:10	Stop	11:30
Hours		12:20		16:40
Shift Hours		06:40		17:10

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

Weather: Sunny with warm temperature - Hi 88F Lo 60F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Continued to work on access opening for pour 3, 4, and 5 on the west side of W2 near the stairtowers sitting on the soffit.
- Finished installing plywood for the void area falsework in the northeast quadrant, and placed ledger for the pour 3 blockout in the northeast quadrant.
- Continued to mobilize falsework bents for the west quadrants on the Hinge K working slab.
- Continued fabrication on the west wall sloped forms.
- Installed form ties in the southwest wall and closed the access opening, see photo below.
- Installed W36x232 (based on field measurements) beams adjacent to the jacking saddle as there is no submittal or RFI to my knowledge for placing these beams, see photo below.
- ABF surveyors assisted RPS with layout of transverse and longitudinal tendons at W2W.
Note: David Chung and myself worked overtime due to the fact that ABF is now working 10hr shifts. See Lalit Mathur's diary for details regarding personel and equipment.

RPS

- Began profiling transverse and longitudinal tendons at W2W with the assistance of ABF surveyors, which included placement of the x-strong pipe for W-30B, W-31B, W-32B, W-33B and W-34B.
- Continued layout of L-bars and T-bars at pier W2W column cages.
- Placed #25 double T-head horizontal ties in the sloped portion of the northeast wall, see photo below.

Surveying Work:

- Set elevations on rebar and 2"x4" templates adjacent to stringlines set by ABF surveyors to measure the cover on the vertical rebar in pour 2 with David Chung.

Office Work:

- Attended biweekly Safety Tailgate meeting at 8:00am.
- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

REC'D *08 JUL-22 #005819


EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow



File Name:	July-10-2008 W2 Cap 001		
Date:	07-10-08	By Int:	M Bruce
Description: Placement of #25 double T-head horizontal ties in the sloped portion of the northeast wall. The formwork was erected prior to the ironworkers installing the reinforcement.			



File Name:	July-10-2008 W2 Cap 002		
Date:	07-10-08	By Int:	M Bruce
Description: Photo of ironworkers placing x-strong pipe at pier W2W with the assistance of ABF surveyors.			

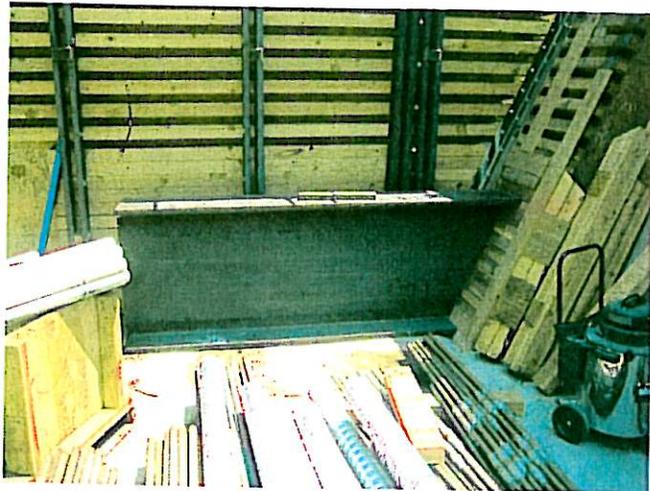

File Name:	July-10-2008 W2 Cap 007		
Date:	07-10-08	By Int:	M Bruce
Description: Installation of a W36 beam adjacent to the jacking saddle on the north side of the longitudinal diaphragm looking south.			



File Name:	July-10-2008 W2 Cap 008		
Date:	07-10-08	By Int:	M Bruce
Description: Form tie installation in the southwest wall and the closed access opening.			
