

*afm*

Job Stamp  
**04-0120F4**  
**SFOBB SAS**

Const. Calendar:	579			
Project Work Day No.:	789			
Date	07/14/2008			
Inspectors	Start	09:20	Stop	10:40
Hours		12:20		16:40
Shift Hours		06:40		17:10

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

**HOURS - ITEM NO.**

Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	#48 Bar Reinf. Steel (Bridge)	HOURS - ITEM NO.										IDLE OR DOWN	REMARKS	
															Name	Contractor
1	1	General Foreman	8												Bob Bognaes	RPS
2	1	Ironworker Foreman	8												Tim Greenlee	RPS
3	1	Ironworker	8												Victor Quiroz	RPS
4	1	Ironworker	8												Lucino Ortiz	RPS
5	1	Ironworker	8												Alejandro Garnita	RPS
6	1	Ironworker	8												Jose Franco	RPS
7	1	Ironworker	8												Jose Enriques	RPS

**Weather:** Partly overcast with mild temperature - Hi 80F Lo 59F (per weather.com forecast)

**Description of Operations @ W2 Cap Beam:**

**ABF**

- Erected falsework bents in the southwest quadrant for pour 3, see photo below for details.
- Continued to place ledger for the pour 3 blackout in the southeast quadrant.
- Erected southwest sloped forms for pour 5, see photo below for details.
- Continued prep work for the northwest quadrant pour 4 joint at the west wall.

Notes: 1.) ABF is continuing 10hr shifts and today I switched with Pamela to observe operations and check grades for pour 3 with David Chung, see Lalit's diary for ABF personel and equipment.

**RPS**

- Continued to place L&T-bars in pier W2W column cages.
- Began to raise the #25 hooked bars in the south portion of the transverse diaphragm, see photo below.
- Miscellaneous work in the southwest wall before the forms were closed today, myself and David Chung looked at the rebar before the forms closed. No. 25 horizontal ties still need to be installed in the upper portion of the wall. The ironworkers informed ABF that they still have enough access to place these bars.
- Shipped #43 vertical bars that were cut in the column cages offsite.


**Office Work:**

- Attended weekly staff (Temp. Towers and Caps) meeting at 8:00am.
- Wrote today's diary.

**Inspector:**

Matt Bruce *Matt Bruce* Transportation Engineer (EIT) \*08 JUL-22 #005829

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

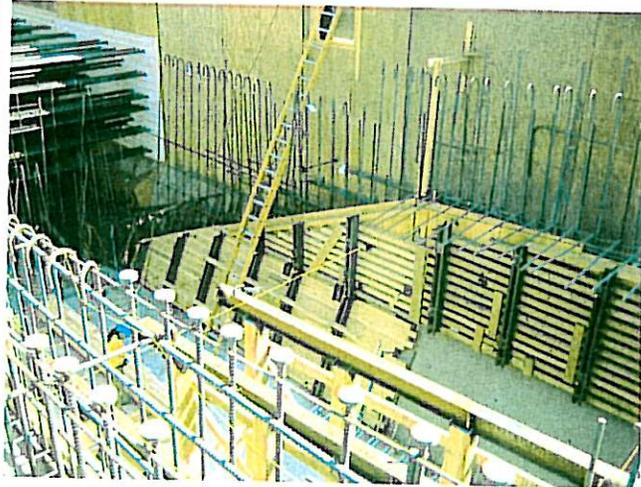

File Name: July-14-2008 W2 Cap 003

Date: 07-14-08 By Int: M Bruce

Description: Ironworkers raising the #25 hooked bars in the south portion of the transverse diaphragm.

File Name: July-14-2008 W2 Cap 004

Date: 07-14-08 By Int: M Bruce

Description: Formwork erection completed today in the southwest quadrant.
