

JK

Job Stamp	
04-0120F4	
SFOBB SAS	

Const. Calendar:	580			
Project Work Day No.:	790			
Date	07/15/2008			
Inspectors	Start	10:00	Stop	10:40
Hours		12:40		16:40
Shift Hours		06:40		17:10

ASSISTANT RESIDENT ENGINEER'S CONTRACTOR – ABFJV, Sub RPS

Weather: Partly overcast in the morning, sunny with mild temperature in the afternoon and slight breezes from the west - Hi 77F Lo 57F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Continued to erect falsework bents in the southwest quadrant for pour 3 and 4, see photo below for details.
- Continued pour 3 joint prep work in the northwest quadrant.
- ABF surveyors set control points on top of the cable tie-down pipes at piers W2E & W2W, see photo below.
- Installed grout tubes the previous day for CBT-24, 30, 31, 32, 33, 34, 35 at pier W2W.

Notes: 1.) ABF is continuing 10hr shifts and today I worked overtime with Pamela to observe operations and check post-tensioning duct placement at pier W2W. The ironworkers need to still need to adjust the CBT tendons prior to additional L&T-bar placement.

RPS

- Continued to place L&T-bars in pier W2W column cages.
- Began to raise the #25 hooked bars in the north portion of the transverse diaphragm.

Office Work:


- Reviewed W2 post-tensioning plans and details.
- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

REC'D *08 JUL-22 #005832

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

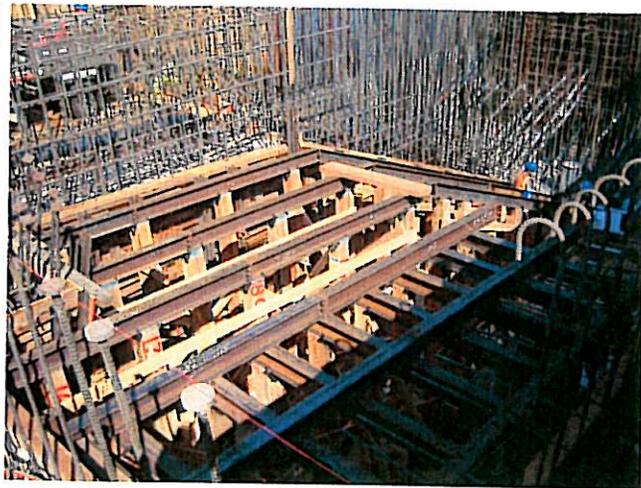

File Name: July-15-2008 W2 Cap 001

Date: 07-15-08 By Int: M Bruce

Description: Control points being set on top of the cable tie-down pipes at pier W2E.

File Name: July-15-2008 W2 Cap 004

Date: 07-15-08 By Int: M Bruce

Description: Falsework bents erected in the southwest quadrant for pour 3 and 4.
