

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SAS SFOBB
Larry Gustafson – Senior Scheduler

Week Ending 08-16-2008

Monday August 8, 2008 Approximately 11 AM: Clear, Windy, Cool

- TT “D” – Pile Driver returns to “re-tap” Northern Piles – foundation welding is approaching completion



- E2 – Southerly Soffit form complete – Cleaning of Northerly Vertical rebar nearing completion



REC'D 08 AUG 15 #006098

- TT “C” Area – Rock Fill essentially complete – Note caissons in place for CIDH –SWWP protection in place



- TT “AE” Assembling first deliveries



- W2 – Northerly Pour 3 Bulkhead (Rebar templates and supports)



South Pour 3 Bulkhead form




Top Rebar Mat Pour 3



Tuesday August 12, 2008 Approximately 11:00 AM: Clear, Cool, Calm

- E2 – Shelter had been moved to Southerly End (EB) for sand blasting the vertical rebar

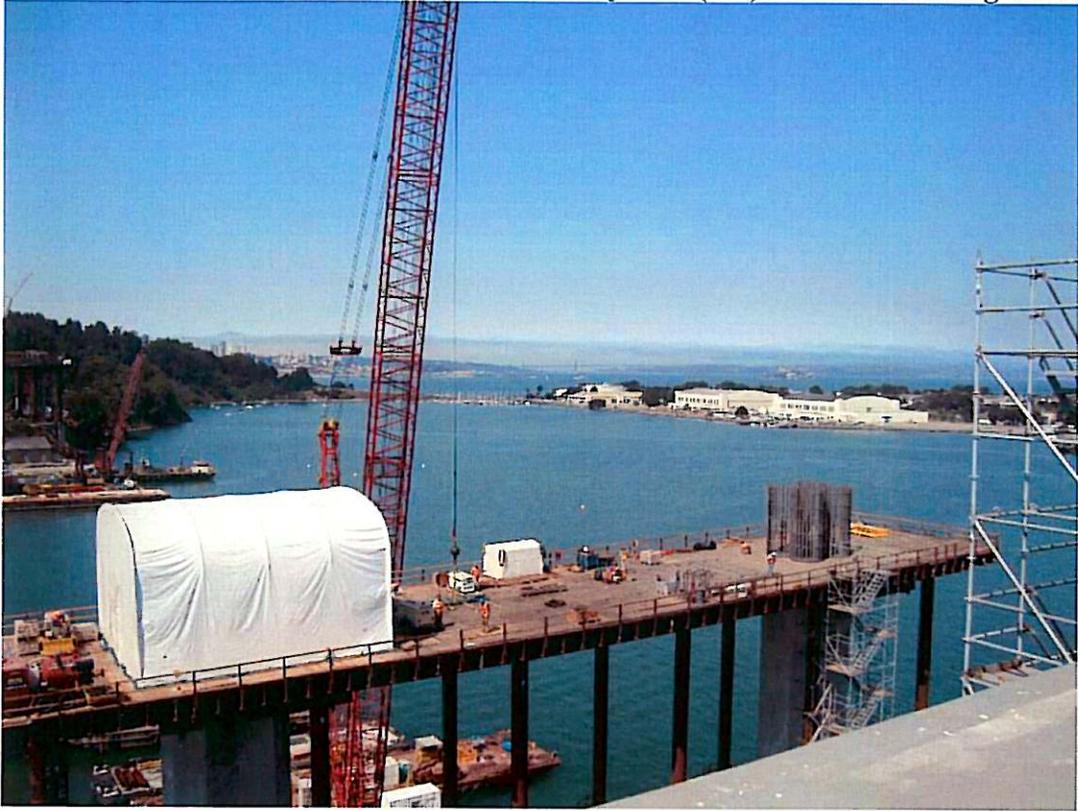

Northerly (WB) Vertical Rebars had been cleaned



- **TT “D” – Apparently Northern Piles have been “re-tapped”**



TT “C” Area – Note that Support Barge & Rock Fill Barge are gone



Thursday August 14, 2008 Approximately 1:00 PM Clear, Warming, Calm at sea level, Windy @ Top of W2

- **TT “D” Note that 4 Northerly Piles have been cut off**



- **E2 – Note that a portion of Easterly vertical edge form is in place**



- TT “C” Area – Awaiting CIDH activity




- TT “AE” being erected





TT "BE" Lower portion has been erected

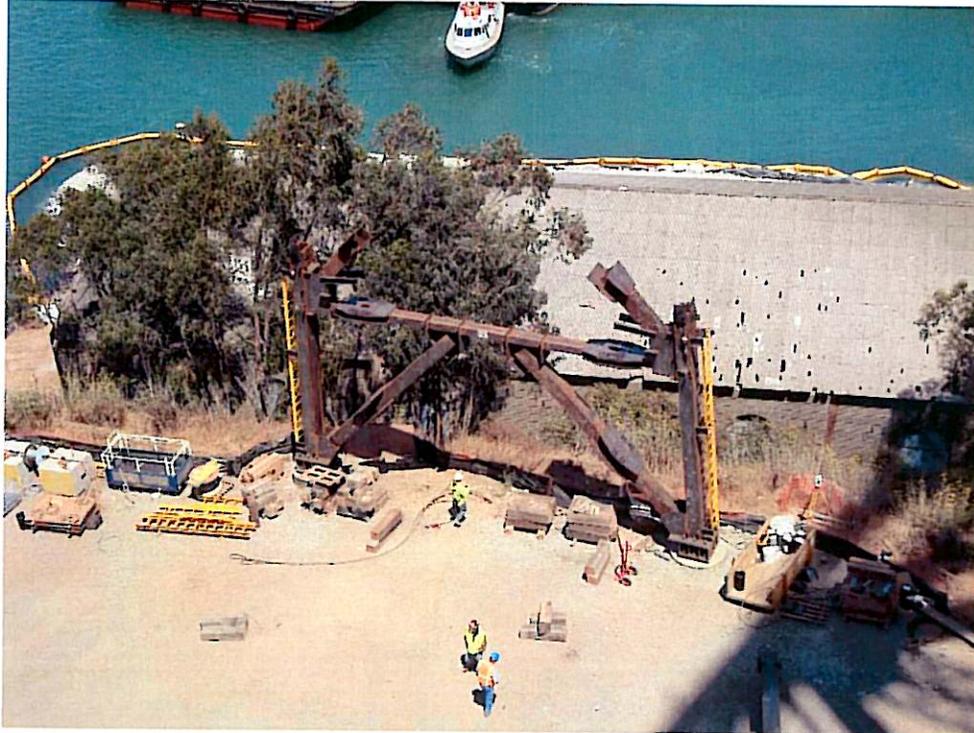

- W2 – Pour 3 Upper rebar mat



View from southern bulkhead



View from Northerly Bulkhead – Pour 3 set for Thursday August 21st, one week from today.

