

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	589			
Project Work Day No.:	799			
Date	07/24/2008			
Inspectors	Start	12:00	Stop	13:20
Hours		14:30		16:10
Shift Hours		06:40		17:10

ASSISTANT RESIDENT ENGINEER'S CONTRACTOR – ABFJV, Sub RPS

Weather: Sunny with mild temperature, westerly breezes - Hi 78F Lo 56F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Continued to work on the chamfer of the pour 3 soffit/ceiling in the northwest quadrant.
- Continued to erect void area falsework bents for the sloped portion of the northwest quadrant.
- Continued to prepare water cooling system pipes for pour 3 near the stairtowers sitting on the west soffit, see photo below.

Notes: 1.) ABF is continuing 10hr shifts and today David Chung and myself are working overtime to observe operations.

RPS

- Were not on the jobsite today and are scheduled to be back onsite Monday July 28th.

Surveying Work:

- Shot the elevations of the marks set on the 21 falsework pipe columns to determine elastic shortening/settlement (if any) before pour 3 with David Chung.

Office Work:



- Attended Confined Space training at 7:30am.
- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

REC'D '08 SEP-06 #006504

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

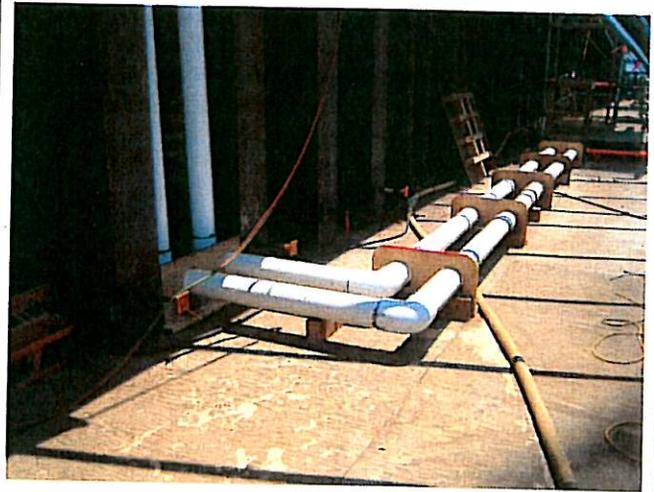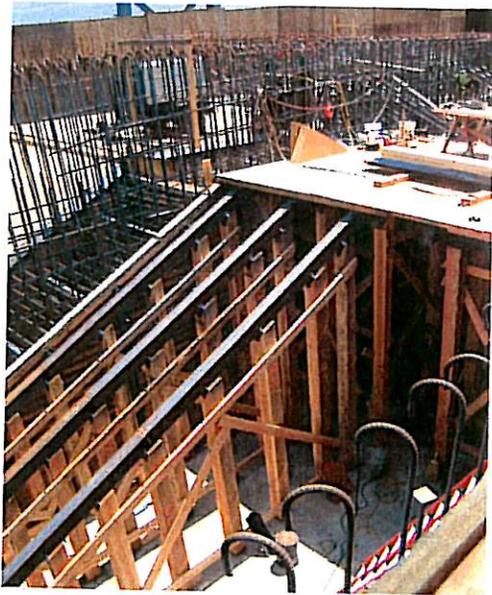

File Name:	July-24-2008 W2 Cap 003		
Date:	07-24-08	By Int:	M Bruce

Description: Erection void area falsework bents for the sloped portion of the northwest quadrant.

File Name:	July-24-2008 W2 Cap 006		
Date:	07-24-08	By Int:	M Bruce

Description: Water cooling system intake and out-take pipes for pour 3 near the stairtowers sitting on the west soffit.
