

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	600			
Project Work Day No.:	810			
Date	08/04/2008			
Inspectors	Start	09:20	Stop	10:30
Hours		12:30		14:10
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS**

Weather: Overcast with cool temperature in the morning, sunny with mild to warm temperature in the afternoon - Hi 77F Lo 57F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Completed installation of ladder rungs inside the corrugated pipe blockout for the south manhole or access opening.
- Began to install form ties in the east/west direction of the W2 cap beam for pour 3.
- Resumed construction of pour 3 blockout formwork on the ground.

RPS

- Began to place 25L4L11 through 25L6L11 bar splices in the east quadrant of the W2 cap beam. See sheets 497S16R1, 497S17 and photo below for details.

Office Work:


- Attended weekly staff (Temp. Towers and Caps) meeting at 8:00am.
- Continued to review submittal 545 regarding the embedded items in the W2 cap beam.
- Wrote today's diary.

Inspector:

Matt Bruce *Matt Bruce* Transportation Engineer (D)

REC'D *08 SEP-06 #006511

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

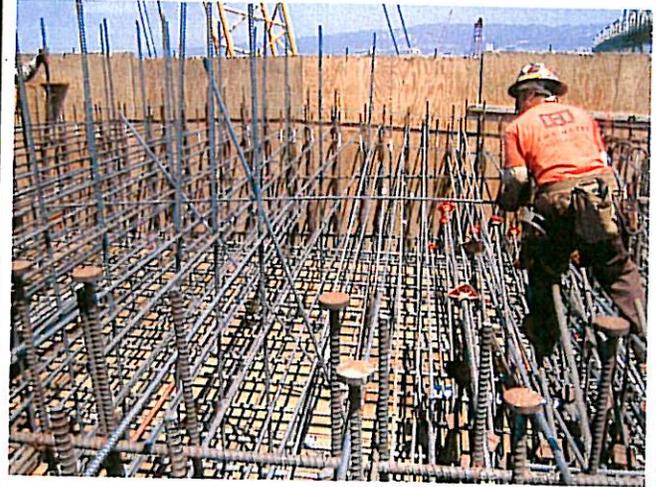

File Name:	Aug-4-2008 W2 Cap 002		
Date:	08-04-08	By Int:	M Bruce

Description: Tie rod installation going through the north manhole/access opening.

File Name:	Aug-4-2008 W2 Cap 006		
Date:	08-04-08	By Int:	M Bruce

Description: Placement of the 25L4L11 through 25L6L11 bar splices in the east quadrant of the W2 cap beam.
