

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – SAS
Larry Gustafson – Senior Scheduler

Week Ending 2008-08-29

Tuesday August 26, 2008 – Observation at approximately 11:00 AM: Clear, Calm, Warm – San Francisco “Summer” has arrived.


- TT “D’ Preparing to Erect Concrete Fender Panels



- E2 – Note that sandblasting shelter has been removed – Easterly Vertical Form continues



- TT "AW - BW" – Assembling Truss W1 – W3 (West Bound)

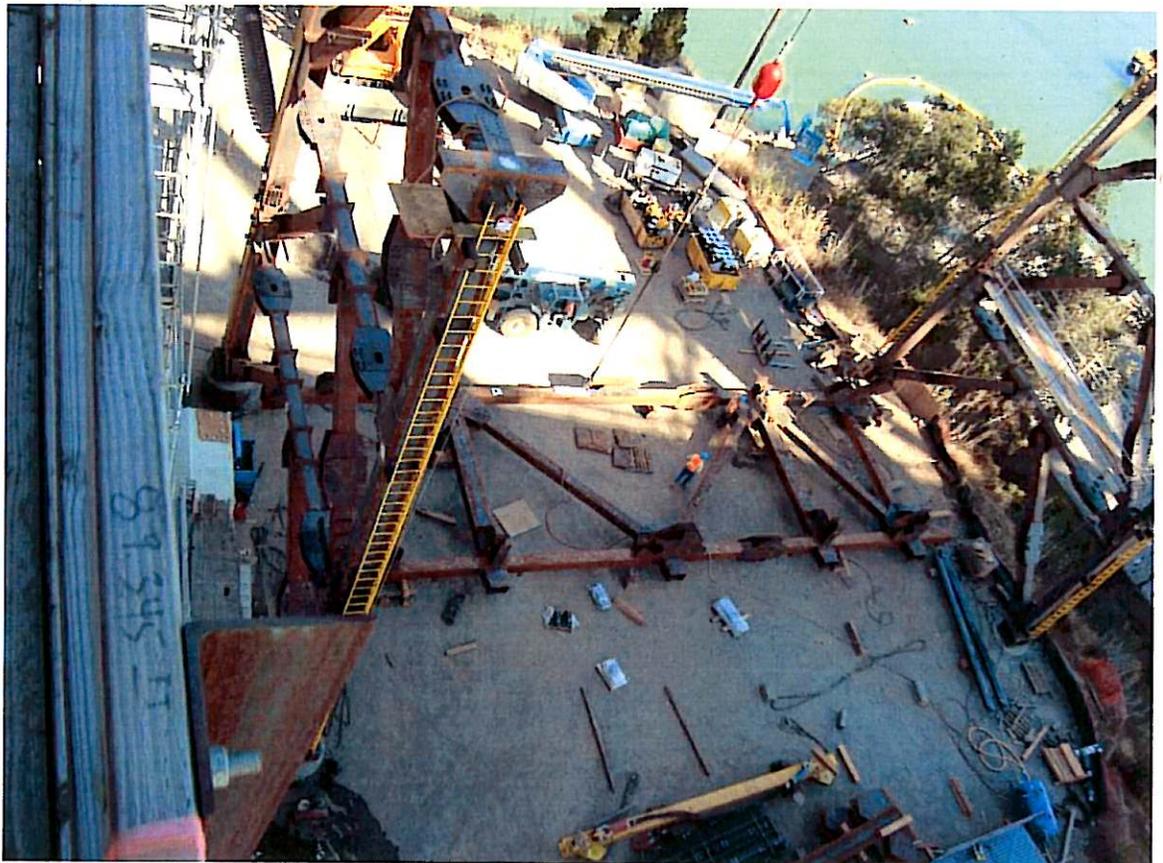

- W2 – Curing Pour 3 that was placed Thursday morning 21 August 2008



Extending walkway Northerly at top of Easterly form



• Temporary Tower Area "C" Work on tie-back wall at Southerly end



Corrugated Caissons cut to grade (filled with sand slurry) at Northerly end



**Thursday August 28, 2008 – Observation from West end of Skyway at approximately 11:00 AM:
Clear, Light Breeze, Warm**

- **E2 – Easterly Vertical Form continues**




Southerly (East Bound) Column Vertical Rebar – prepping for cross beam rebar



Northerly (West Bound) Column Vertical Rebar – prepping for cross beam rebar



Cross Beam Rebar staging area (on Service Barges)

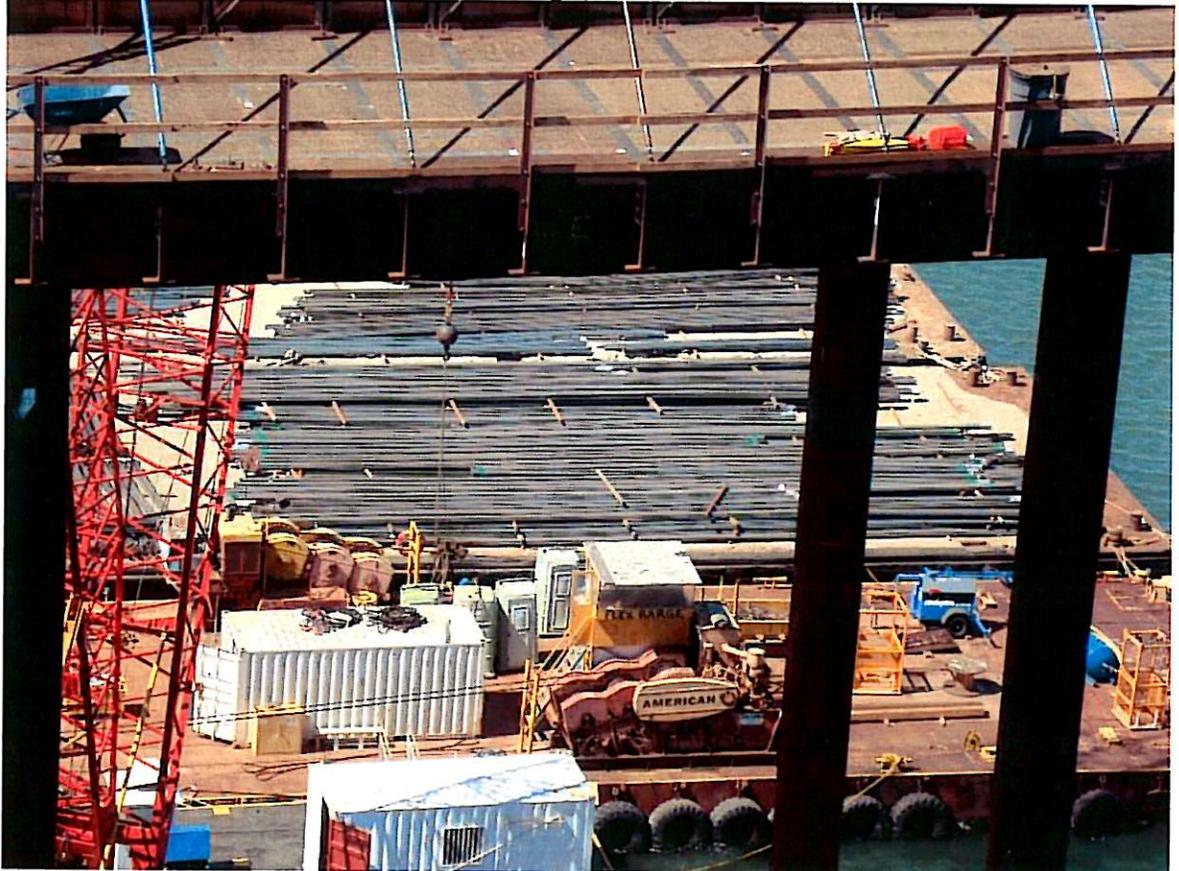

- **TT "D" View from E2 – Concrete Plank Fender operation**



- **View of W2 (from West end Skyway) Note that truss W1-W3 between A1W & B1W in place**



- **View of Area "C" is obscured from West end of Skyway, therefore no pictures today.**

Friday August 29, 2008 – Observation approximately 10:30 AM: Clear, Calm, Warm

- TT”D” Installing Concrete Fender Panels




- E2 – Prepping to hoist rebar



- TT "A1W" & "B1W" – Truss W1-W3 being bolted



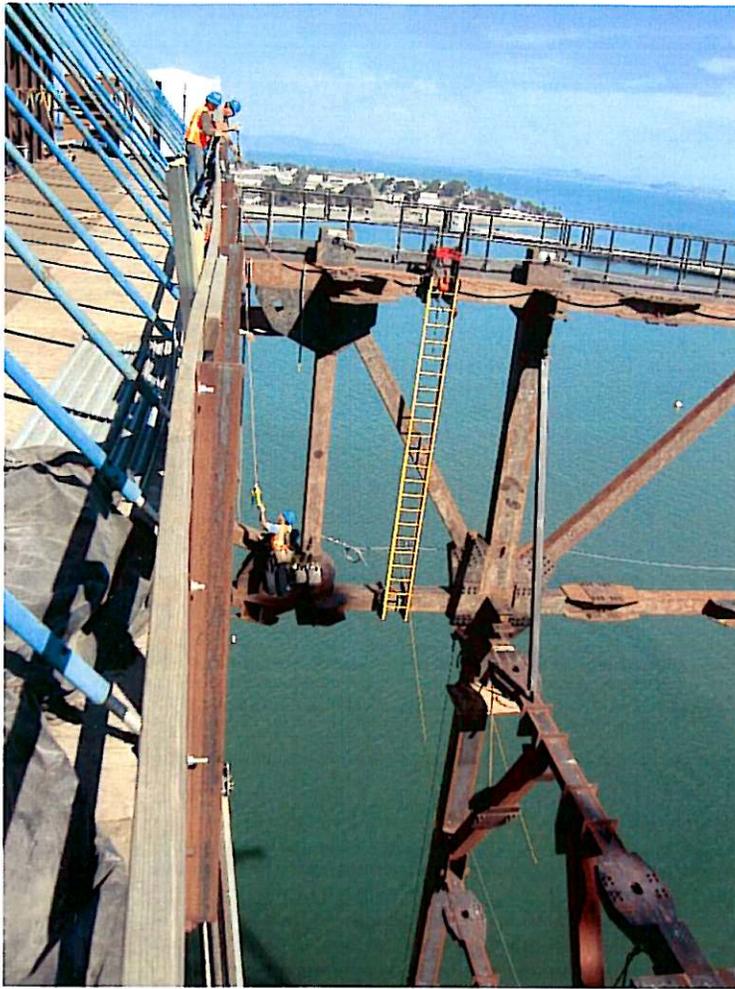

• Temporary Tower Area "C" – Southerly Tie-Back Wall



Northerly Tie-Back Wall



Prepping to start CIDH drilling at WB (Northerly area)



- **W2 – Curing and cooling of Pour 3 continues**



Extending Walkway Southerly on Easterly Form

