

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. **46.B**
Date the Shift Began: **8/14/08**
 NIGHTWORK **THURSDAY**
Shift Hrs Start **6:00** Stop **14:30**
Engineer's Hrs Start **7:30** Stop **18:00**

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT

Location: Pier E2	7-day const. cal.: 610	Weather: Sunny & Hot
Remark:	Project work day: 820	

Description of Operation: Falsework Erection

REV 08 SEP 27 #006743

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.					IDLE OR DOWN/ ELSEWHERE	REMARKS	Prime / Sub	
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	1	2	3	4	5				
At Pier E2											
		Pile Driver							Ben Neal	Foreman	p
		Pile Driver	8.00						Alan Briney	Journeyman	p
		Pile Driver	8.00						Luke Paulk	Journeyman	p
		Pile Driver	8.00						Jason Matlock	Journeyman	p
		Pile Driver	8.00						Edward Mendoza	Journeyman	p
		Deck Engineer	8.00						Ryan Oku	Journeyman	p
		Operator	8.00						Kevin Fitzgerald	Journeyman	p
		Oiler	8.00						David Bian	Journeyman	p
		Pile Driver	8.00						Garrieth Nelson	Journeyman	p
		Crane Ringer	8.00						Manitowac		
481-93-4002		Man-lift	8.00						Hertz Rental Genie S-125		
P185-R		Compressor	8.00						Ingersoll Rand		
		Welding Machine	8.00						Lincoln Vantage 500		
		Generator	8.00						MQ Power 25		
At Berth 7											
		Pile Driver	8.00						Harry Wheat	Journeyman	p
		Pile Driver	8.00						Richard Yambao	Journeyman	p
		Pile Driver	8.00						Carl Nisley	Foreman	p
		Pile Driver							Kenny Raynolds	Journeyman	p

At Pier E2, the work was comprised of sand blasing the South column, continue the setting of the panel forms on the East side, and laying out the bolts for the shear keys/bearings. A total of 5 forms have been placed thus far on the East side of the cross beam.

At Berth 7, ABF has employed one more worker to speed up the work at this location. Today, not only the crew continued to work on the pedestrian bridge, but also began work on the form panels. The electrical work concluded a couple days ago and after the placement of plywood, which is now underway, the concrete pipes will be installed here.

For details on the sand blasting work and more details on work at Berth 7, please refer to Massoud Modanlou's report.

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. **46.B**

Date the Shift Began: **8/14/08**

NIGHTWORK **THURSDAY**


Shift Hrs	Start	6:00	Stop	14:30
Engineer's Hrs	Start	7:30	Stop	18:00

ASSISTANT RESIDENT ENGINEER'S DAILY

BRIDGE

REPORT

Location: Pier E2	7-day const. cal.: 610	Weather: Sunny & Hot
Remark:	Project work day: 820	

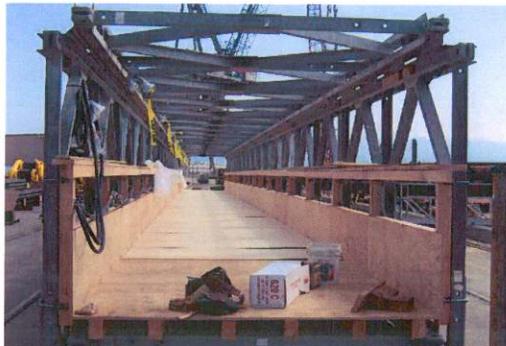

Materials:

Insp. Hrs.	
REG: 82	INTERMITTENT
OT:	INSPECTION

Saman Soheili
Saman Soheili

ASR/CT
Title
