

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. 7-day const. cal.: 621
Project work day: 831

Date the Shift Began: 8/25/08

NIGHTWORK MONDAY

Shift Hrs Start 6:30 Stop 15:00
Engineer's Hrs Start 6:45 Stop 15:15

TOLL PROGRAM/DIST. 4 CONSTR.

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT

Location: E2 Cross Beam
Remark: formwork/survey
Weather: warm
HI 95F/Lo 77F

Description of Operation:
ABF - continue to add to forms for cross beam
RPS - unload ironwork at Pier 7 (see Masoud Modanlou's Diary for names)

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.					CONTRACTORS		
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	38		133		IDLE OR DOWN/ ELSEWHERE	Prime	American Bridge / Fluor JV (P)	
			Structural Concrete, Bridge	Construction Surveying					Sub #1	
			RT	RT				Sub #2		(1)
								Sub #3		(2)
								Sub #4		(3)
								Sub #5		(4)
										(5)
								REMARKS		Prime / Sub
								Name	Classification	
	1	Foreman	8.00					Ben Neal	Pilebutt	P
	1	Journeyman	8.00					Allen Briney	Pilebutt	P
	1	Journeyman					8.00	Jason Matlock	Pilebutt	P
	1	Journeyman	8.00					Luke Paulk	Pilebutt	P
	1	Journeyman					8.00	Edward Mendoza	Pilebutt	P
	1	Apprentice	8.00					Garrieth Nelson	Pilebutt	P
	1	Journeyman	8.00					Kevin Fitzgerald	Operator	P
	1	Apprentice	8.00					David Bian	Oiler	P
	1		8.00					Byron Contreran	Laborer	P
	1						8.00	Ignacio Gil	Laborer	P
	1		8.00					Riyoberto Cancon	Laborer	P
	1	Apprentice		8.00				Chris Roberts	Surveyor	P
	1	Journeyman		8.00				Terry Dennis	Surveyor	P
	1	Ringer Barge					8.00	Manitowac Crane		P
002062	1	Lincoln Electric					8.00	Vantage 500	6008088	P
002083	1	Lincoln Electric					8.00	Vantage 500	6008091	P
002068	1	MQ Power Generator	8.00					Whisperwatt 25	6007939	P
002069	1	MQ Power Generator	8.00					Whisperwatt 25		P
	1	Honda 115 Horse Skiff					8.00			P
002045	1	Ingersoll Rand P185R					8.00			P
	1	Clemco Classic 150					8.00	Sand Bucket		P
674015	1	Sullair SF 375H					8.00	Compressor		P
679085002	1	Ditch Witch FX60					8.00	Vacuum		P
	1	Flex Anchor					8.00	Equipment Barge		P

Weekly internal staff meeting
Helped Matt (CT) load cylinders to be transported to Sacramento test lab
Ironwork has been continuously unloaded from truckbeds to a barge (DSC02257) since last Tuesday. Ironwork for the Cross beam will begin this Thursday 8/28. The concrete pour is scheduled for the 7th of November. This gives roughly 50 remaining working days.
ABF has placed rings at the locations of the high strength rods (DSC02261) and the survey crew continues to lay out remaining shear/bearing (DSC02262) where the tent was recently removed to Pier 7 (background of DSC02257).
ABF has placed drip grooves around the soffit (DSC02261) and continue to build railing at the top of the forms on the east face (DSC02258).

REC'D 08 OCT 01 #00506

XL

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
 04-SF-80-13.2/13.9 04-0120F4
 SFOBB SAS
 San Francisco Co. in San Francisco
 Fm 0.6 km to 1.3 km East of Yerba Buena
 Tunnel East Portal

Report No. 7-day const. cal.: 621
 Project work day: 831

Date the Shift Began: 8/25/08

NIGHTWORK MONDAY

Shift Hrs Start 6:30 Stop 15:00
 Engineer's Hrs Start 6:45 Stop 15:15

ASSISTANT RESIDENT ENGINEER'S DAILY

BRIDGE

REPORT


Location: E2 Cross Beam

Weather: warm

DSC02257.jpg



DSC02258.jpg

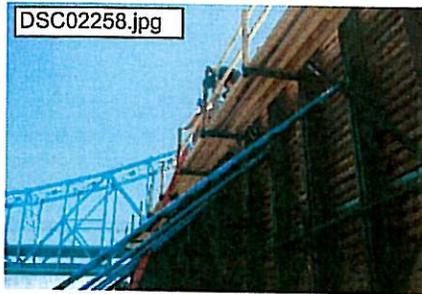

DSC02261.jpg



DSC02262.jpg



Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT:	INSPECTION

David Chung
 DAVID CHUNG

TE/CT
 Title
