

Job Stamp 04-0120F4 SFOBB SAS

Construction Calendar no.	673		
Project working days no.	883		
Date	10/16/2008		
Inspectors	Start	06:30	Stop 17:00
Hours			
Shift Hours	Start	06:30	Stop 15:00

Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower C foundation and A & B erections
Weather	HI: 75 F Low: 52 F Partly cloudy

Equipment and/or labor			Hours - ITEM no.							Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental			IDLE	
	C	Liebherr LR 1300	8							ABF
006-18-4293	C	Ingersoll Compressor	8							ABF
481-93-6013	R	Gnie Boom lift	4							ABF
544D-10	R	Gradall Forklift	8							ABF
	1	Manitowoc 2250	8							T.D.
L-269	1	Ingersoll-Rand Compressor	8							T.D.
	1	Ed Meyer	8							ABF Foreman
	1	Matt Chamberlain	8							ABF Iron worker
	1	James Sturgeon	8							ABF Iron worker
	1	Serina Lafleur	8							ABF Iron worker
	1	David Lucero	8							ABF Iron worker
	1	Jerry Kubala, Jr.	8							ABF Iron worker
	1	Mike Naday	8							ABF Iron worker
	1	Alex Bartlett	8							ABF Iron worker
	1	Randle Leslie	8							O.E. (T.D.)
	1	Don Adams	8							O.E. (T.D.)
	1	Levis	8							O.E. (T.D.)

Description of Operation:

- Daily activity of contractors
 - ABF continued to set up walkways (see Fig 1).
 - T.D. placed anchor bolts at C4 (see Fig 2).
 - See Art Pannu and Ali's diary for additional contractors' activities and comments.

- Note
 - Attend a safety meeting from 08:00
 - Spoke to Mark Vilcheck regarding the difference of aggregate size between the one approved (1inch) and one delivered to the site (3/4 inch). He communicated with Bill O'Sullivan.
 - Talked to T.D. foreman Randle regarding cleaning the area, which is soaked in sea water, with high-pressure washer.
 - Asked Victor Altamirano to deliver 8 concrete cylinders (which were sampled on Oct. 10) to Sacramento mat. Lab.
 - 2 hours O.T.



Fig 1

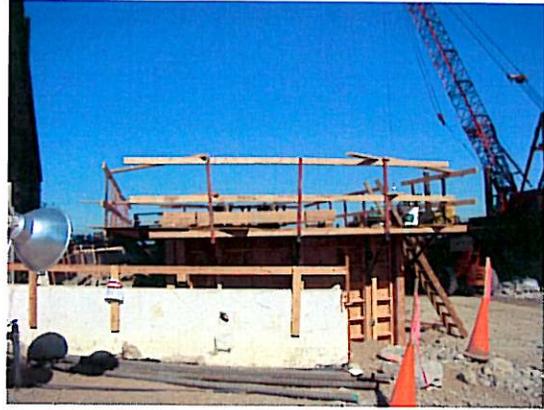


Fig 2

Inspector:

SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
