

Job Stamp  
**04-0120F4**  
**SFOBB SAS**

Construction Calendar no. 686  
Project working days no. 896  
Date 10/29/2008  
Inspectors Start 07:20 Stop 15:50  
Hours  
Shift Hours Start 06:30 Stop 15:00

### Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, A & B erections
Weather	HI: 65 F Low: 46 F Partly cloudy

Equipment and/or labor			Hours - ITEM no.							Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental			IDLE	
	C	Liebherr LR 1300	8							ABF
006-18-4293	C	Ingresoll Compressor	8							ABF
481-93-6013	R	Gnie Boom lift	8							ABF
544D-10	R	Gradall Forklift	8							ABF
	1	Ed Meyer	8							ABF Foreman
	1	Matt Chamberlain	8							ABF Iron worker
	1	James Sturgeon	8							ABF Iron worker
	1	Serina Lafleur	8							ABF Iron worker
	1	David Lucero	8							ABF Iron worker
	1	Mike Naday	8							ABF Iron worker
	1	Jerry Kubala, Jr.	8							ABF Iron worker
	1	Alex Bartlett	8							ABF Iron worker

**Description of Operation:**

- Daily activity of contractors
  - ABF continued to install walkways and pretension bolts (see Figs 1 and 2).
  - See Mark Vilcheck and Art Pannu's diary for additional contractors' activities and comments.
- Note
  - Was informed from Art that that Alex and Mike marked bolts after pretensioning. See the red rectangular mark of Fig 3 for the locations. In the location, the top chord bolt connections of web plate and plate facing down are the areas where contractor didn't follow the procedure.
  - Talked to Alex and Mike on the importance of following the turn-of-nut procedure mentioned in RCSC.

REC'D \*08 DEC-04 #007827



Fig 1



Fig 2

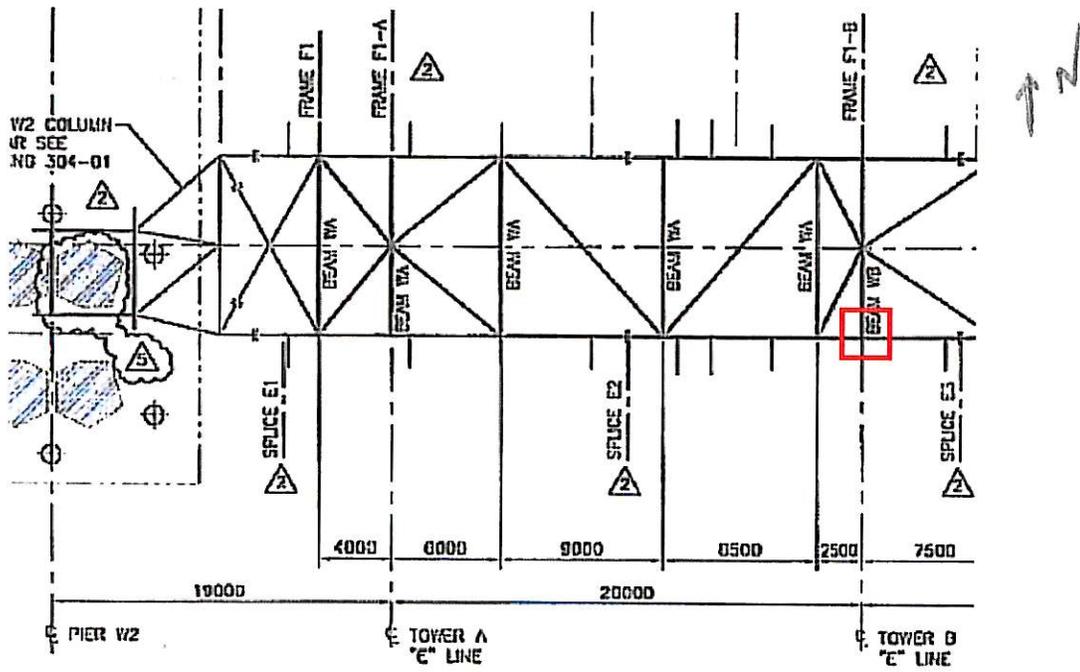


Fig 3

Inspector:  
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
