

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	727			
Project Work Day No.:	937			
Date	12/09/2008			
Inspectors	Start	09:10	Stop	11:30
Hours				
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Subs CMC-RS**

Weather: Sunny with cold temperatures – Hi 59°F Low 39°F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Continued to clean the pour 5 base slab.
- Resumed cleaning the pour 4 construction joint.
- Continued placing PVC pipes and the intake/outake pipes for the pour 5 thermal control. Also mobilized manifolds and hoses on the median or pour 3 surface.
- Surveyors assisted the ironworkers with layout for continuity tendon W-41B.

CMC-RS

- Began to place the duct for W-41B with the assistance of ABF surveyors.
- Continued to work on the punchlist items for PT and rebar (Pamela's).


Office work:

- Filled out paperwork for OSC training history and individual development plan.
- Reviewed stressing documents (Submittal 150) and plans.
- Wrote today's diary.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

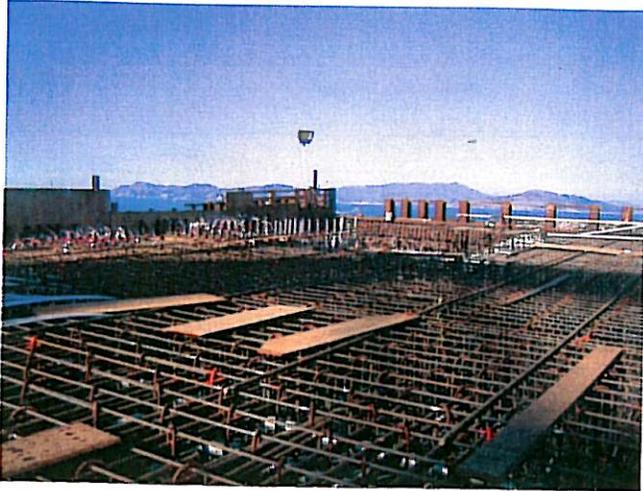

File Name:	Dec-09-2008 W2 Cap 003		
Date:	12-09-08	By Int:	M Bruce

Description: Pour 5 progress to date looking in the northwest direction.

File Name:	Dec-09-2008 W2 Cap 005		
Date:	12-09-08	By Int:	M Bruce

Description: Pour 5 progress to date looking south.
