

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

7-day Const. Cal.: 709
Project Work Day: 919
Date the Shift Began: 11/21/08
 NIGHTWORK FRIDAY
Shift Hrs Start 6:30 Stop 16:00
Engineer's Hrs Start 7:30 Stop 17:00

**ASSISTANT RESIDENT ENGINEER'S DAILY REPORT
BRIDGE**

Location: Temporary Tower F, Big Digger Barge Remark:			Report No. 46.B				Weather: Fog, 55° - 62°			
ITEM NO. >> 8			HOURS - ITEM NO.				Prime American Bridge / Fluor JV (P)			
							Sub #1 Traylor Dutra JV (1)			
							Sub #2 (2)			
							Sub #3 (3)			
							Sub #4 (4)			
							Sub #5 (5)			
EQUIPMENT AND/OR LABOR:			Furnish Temporary Towers				IDLE OR DOWN/ ELSEWHERE			
EQPT. NO.	NO. MEN	DESCRIPTION (Of Equipment or Labor)	RT	OT				REMARKS		
		Big Digger Manitowoc 2250 Crane	8.00	1.00				Name	Classification	Prime / Sub
#005		Lincoln Electric Welder	8.00	1.00						
#001		Lincoln Electric Welder	8.00	1.00						
L472		Power Generator	8.00	1.00						
L479		Multiquip Generator							IDLE	
L291		D185Q Sullivan Air Compressor							IDLE	
		PLDR	8.00	1.00				Lee Tacker	FOR	2
		PLDR	8.00	1.00				Danny Vega	JRNY	2
		PLDR	8.00	1.00				Ernest Hamilton	OPER	2
		PLDR	8.00	1.00				Gary Lewis	APPR	2
		PLDR	8.00	1.00				Jacob Lavish	JRNY	2
		PLDR	8.00	1.00				Phillip Baker	JRNY	2
		PLDR	8.00	1.00				Steven McGrew	JRNY	2
		PLDR	8.00	1.00				Steve Gordon	OPER	2

Description of Operation:

The workers continued fillet welding the plates for the non-PDA pile and installing access platforms for the exterior plate welds.

The following plates were welded then VT'd by the CWIs:
F116: A, B, C, D
F124: A, B, C
F125: H, G (no VT on G)
F107: F, E (E was only partially completed)
F126: H, G (No VT on H and G was only partially completed)

Lee Tacker informed me they want to finish all non-PDA plate welds by tomorrow so that the crew can return to Pier 7 on Monday and begin work on the jacking system for the north node.

Smith Emery CWIs present during the entire shift and overseeing welding operations were Michael Johnson (QC for ABF) and Gary Ehrsam (QA for TD). I asked Michael Johnson if he intended to MT the welds from yesterday and today that were only VT'd. He informed they did not MT any of the welds today so as not to interfere with the laborers work. He said they will probably MT first thing at tomorrow's shift.

See attached 4 photos for today's activities.

I received an email from Bill O'Sullivan regarding the Structural Bolting Plan for the remaining bolts on Tower F as well as those for Tower G. Traylor Dutra plans to use Squirter DTI's and will perform the pre-installation calibration and installation sequence in conformance with the manufacturer's recommendations. The pre-installation calibration is scheduled for Monday pending delivery of the DTI washers.


Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT: 0.0	INSPECTION

Gina Rizzardo
GINA RIZZARDO TE/CT
First Name Last Name Title

REC'D '09 JAN-02 #008031

46.02

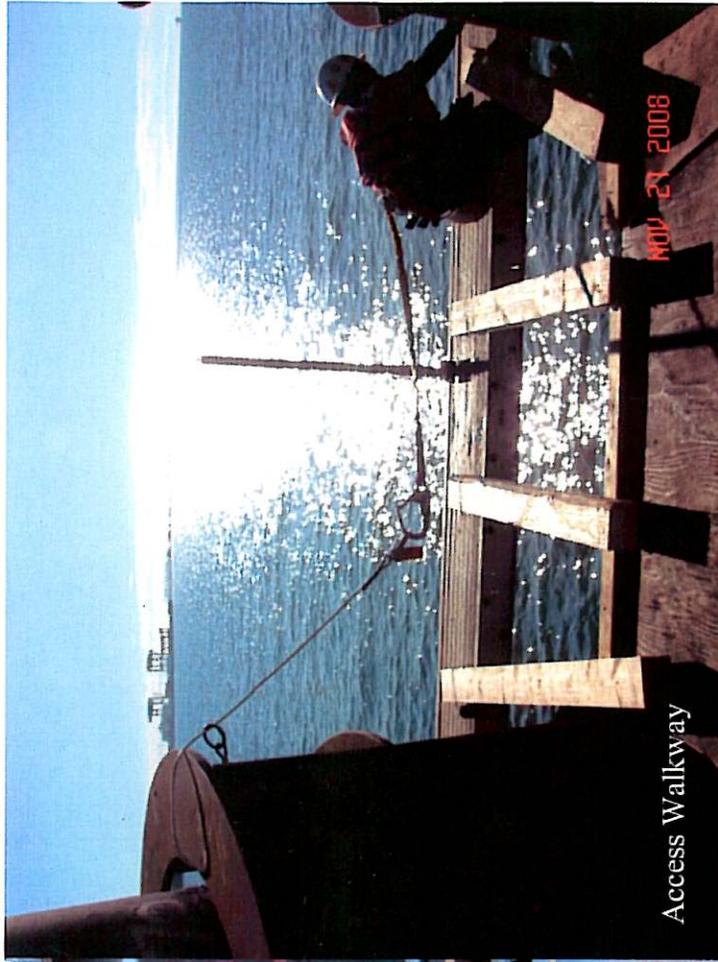


Access Walkway

NOV 21 2008



Weld Inspection

NOV 21 2008

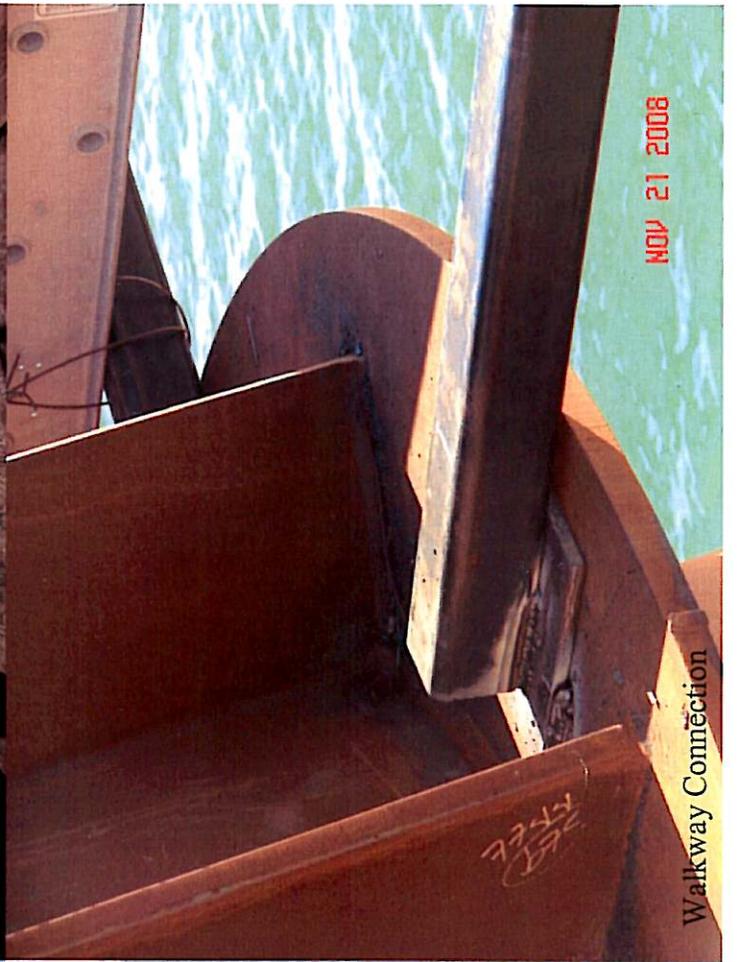

Walkway Connection

NOV 21 2008



Access Walkway

NOV 21 2008
