

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 706
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 916
Form HC-10A (Rev. 6/80)	04-0120F4	Date	11/18/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS	
Equip. #	N O M E N	DESCRIPTION (Of Equipment or Labor)	Regular	OT							IDLE OR DOWN	Name Contractor	
												Name	Contractor
		Big Digger	8										
		DB # 5 Marine barge	8										
		APE 600 Vibration hammer	0										
		Superintendant	0	0								Terry Murray	Traylor Dutra
		Pile driver Journeyman	0	0								Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0								Adams Price	Traylor Dutra
		Operator	0	0								Joe Boracci	Traylor Dutra
		Pile driver Journeyman	0	0								Ventura Ochoa	Traylor Dutra
		Operator	0	0								Theo Roth	Traylor Dutra
		Pile driver Journeyman	8	0								Phillip Baker	Traylor Dutra
		Pile driver Journeyman	0	0								Robert Utley	Traylor Dutra
		Pile driver Journeyman	0	0								Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	8	0								Lee Tacker	
		Pile driver Journeyman	8	0								Danny Vagas	Traylor Dutra
		Pile driver Journeyman	8	0								Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	0								Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	0								Gary Lewis	Traylor Dutra
		Operator	0	0								Bud Germany	Traylor Dutra
		Operator	8	0								Steve Gordon	Traylor Dutra
		Pile driver Journeyman	0	0								Travis Logsdon	Traylor Dutra
		Operator	0	0								Joe Boracci	Traylor Dutra
		Operator	8	0								Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	0	0								Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0								Todd Labarb	Traylor Dutra
		Pile driver Journeyman	0	0								Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	0	0								Randell Lesley	Traylor Dutra

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

Temporary Tower F – Connection Shear plates welding

46.02

Activities:

1. Office work:

- Review plans, special provisions, RFI and ABF submittals for TTF.


2. Field work:

- Big Digger crew continued connection shear plates welding (Inner face).
- Carpenter installed working platform outer face of the frame.
- Kent Chalabi and Gary Ehram from Smith Emery were present for QA/QC inspection.
- Welding operation was performed on non-PDA piles such as: F106, 107, 126, 124, 116, 114, 125, 113.
- Taken photos concrete fenders were damaged by moving barge at North West corner of TTD.

3. Overtime reason:

Thanh V Le

Trans Engineer (D)/Asst. Struct. Rep

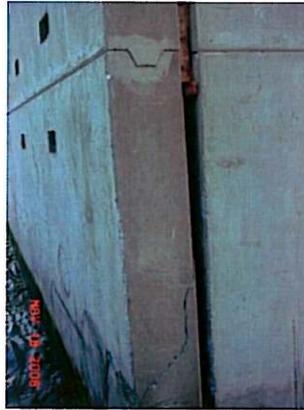

Damaged fenders North West TTD



Working platform installation
