

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 713
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 923
Form HC-10A (Rev. 6/80)	04-0120F4	Date	11/25/2008

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

HOURS - ITEM NO.												REMARKS	
EQUIPMENT AND/OR LABOR:			Regular	OT							IDLE OR DOWN	Name Contractor	
Equip. #	N O M E N	DESCRIPTION (Of Equipment or Labor)										Name	Contractor
		See Gina's diary for labor and equipment of the day											

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.


Description of Operation:

Temperary Tower F – North Node Assembly


Activities:

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTF.
  
2. Field work:
  - Pre installation bolt testing using Squirter DTI washer with the witness of QA inspector Michael Johnson.
  - BD 5 crew continued drilled and installation bolts for driving frame connections.
  - Carpenter crew continued installation working platform and safety handrail system for the driving frame.
  - Welder crew installed attachment for jacking systems.
  - See Gina's diary for more information.


3. Overtime reason:

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

46.02

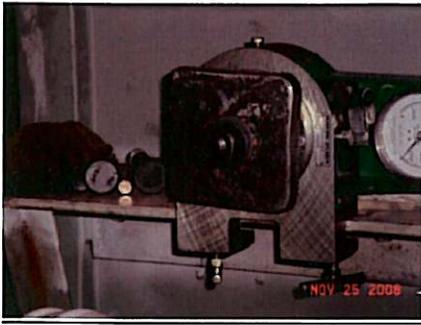

Squiter DTI washer preinstallation test

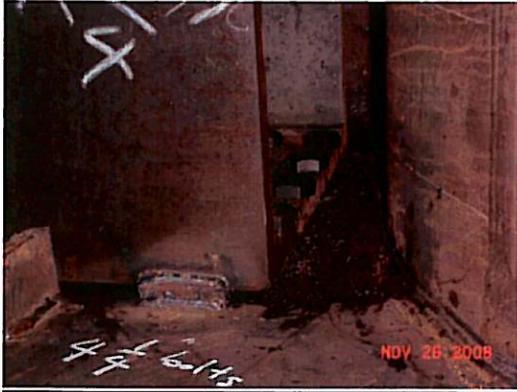

Bolts too close to the edge
