

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no.	726
Project working days no.	936
Date	12/08/2008
Inspectors	Start 07:00 Stop 12:00
Hours	
Shift Hours	Start 06:30 Stop 15:00

Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower A,B and C erections
Weather	HI: 64 F Low: 49 F Partly cloudy/ foggy

Equipment and/or labor			Hours – ITEM no.							Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental			IDLE	
	C	4100W crane	8							ABF
006-18-4293	C	Ingresoll Compressor	8							ABF
481-93-6013	R	Gnie Boom lift								ABF
	1	Jeff Scott	8							ABF crane operator
	1	Ed Meyer	8							ABF Foreman (erection)
	1	Carlos Valverde	8							ABF Foreman (bolt)
	1	Matt Chamberlain	8							ABF Iron worker
	1	James Sturgeon	8							ABF Foreman (erection)
	1	Serina Lafleur								ABF Iron worker
	1	David Lucero	8							ABF Iron worker
	1	Mike Naday	8							ABF Iron worker
	1	Jerry Kubala, Jr.	8							ABF Iron worker
	1	Alex Bartlett	8							ABF Iron worker
	1	Casey Lux	8							ABF Iron worker
	1	Ernesto Fresguez	8							ABF Iron worker
	1	Jason Kent	8							ABF Iron worker

Description of Operation:

- Daily activity of contractors
 - ABF erected the north panel of E4-E5 (see Figs 1 thru 4).
 - See Mark Vilcheck and Art Pannu's diaries for contractors' activities and comments.

- Note
 - Noticed that the erection ABF is currently performing is different from the one already approved. I informed the change to Mark Vilcheck. He told me that he got the revised submittal on December 5 and is going to work on it. Then, he asked me to write down their activities.
 - 3 hours personal leave.

46.02



Fig 1



Fig 2



Fig 3

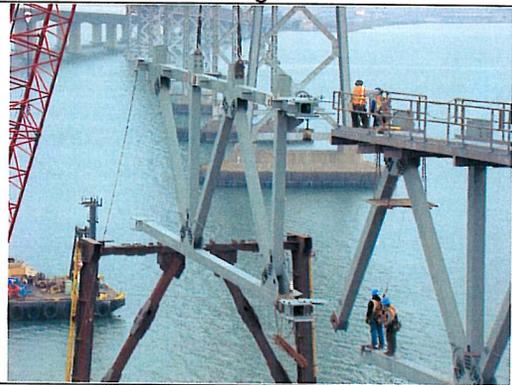


Fig 4

Inspector:
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
