

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no. 729
Project working days no. 939
Date 12/11/2008
Inspectors Start 07:00 Stop 17:30
Hours
Shift Hours Start 06:30 Stop 17:30

Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower A,B and C erections
Weather	HI: 59 F Low: 43 F Partly cloudy/ foggy

Equipment and/or labor			Hours – ITEM no.						Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental		IDLE	
	C	4100W crane	8						ABF
006-18-4293	C	Ingresoll Compressor	8						ABF
481-93-6013	R	Gnie Boom lift							ABF
	1	Jeff Scott	8						ABF crane operator
	1	Ed Meyer	8						ABF Foreman (erection)
	1	Carlos Valverde	8						ABF Foreman (bolt)
	1	Matt Chamberlain	8						ABF Iron worker
	1	James Sturgeon	8						ABF Foreman (erection)
	1	Serina Lafleur							ABF Iron worker
	1	David Lucero	8						ABF Iron worker
	1	Mike Naday	8						ABF Iron worker
	1	Jerry Kubala, Jr.	8						ABF Iron worker
	1	Alex Bartlett	8						ABF Iron worker
	1	Casey Lux	8						ABF Iron worker
	1	Ernesto Fresquez	8						ABF Iron worker
	1	Jason Kent	8						ABF Iron worker

Description of Operation:

- Daily activity of contractors
 - ABF erected the transverse member, which connects north and south panels of E4 and E5 (see Fig 1).
 - See Mark Vilcheck and Art Pannu's diaries for contractors' activities and comments.
- Note
 - Attend a safety meeting from 08:00 to 09:00 and a concrete pour meeting from 09:15 to 10:15.
 - Mentioned Mark regarding the need to have an internal meeting to come up with better access for inspection.
 - 2 hours O.T.

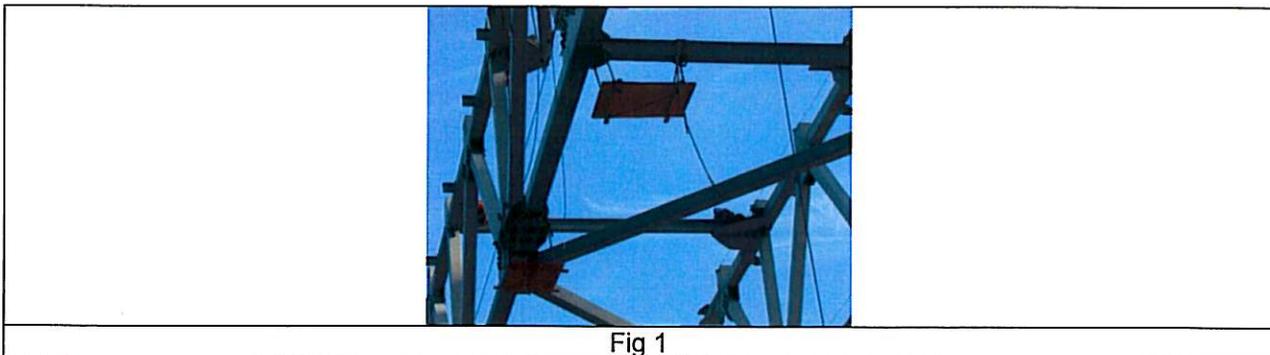


Fig 1

Inspector:
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep

46-02
