

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no. 733
Project working days no. 943
Date 12/15/2008
Inspectors Hours Start 09:00 Stop 17:30
Shift Hours Start 06:30 Stop 17:30

Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower A, B and C erections
Weather	HI: 52 F Low: 41 F Partly cloudy

Equipment and/or labor			Hours – ITEM no.						Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental		IDLE	
	C	4100W crane	8						ABF
006-18-4293	C	Ingresoll Compressor	8						ABF
481-93-6013	R	Gnie Boom lift							ABF
	1	Jeff Scott	8	2					ABF crane operator
	1	Ed Meyer	8	2					ABF Foreman (erection)
	1	Carlos Valverde	8	2					ABF Foreman (bolt)
	1	Matt Chamberlain	8	2					ABF Iron worker
	1	James Sturgeon	8	2					ABF Foreman (erection)
	1	David Lucero	8	2					ABF Iron worker
	1	Mike Naday	8	2					ABF Iron worker
	1	Jerry Kubala, Jr.	8	2					ABF Iron worker
	1	Alex Bartlett	8	2					ABF Iron worker
	1	Casey Lux	8	2					ABF Iron worker
	1	Ernesto Fresquez	8	2					ABF Iron worker
	1	Jason Kent	8	2					ABF Iron worker

Description of Operation:

- Daily activity of contractors
 - ABF continued to assemble CW (see Fig 1)
 - See Mark Vilcheck's diary for contractors' activities and comments.
- Note
 - Reported to Mark and Alex, a safety coordinator (CT), regarding the ABF activity on the top of boom (see Fig 2). See Alex's diary for the follow-ups.

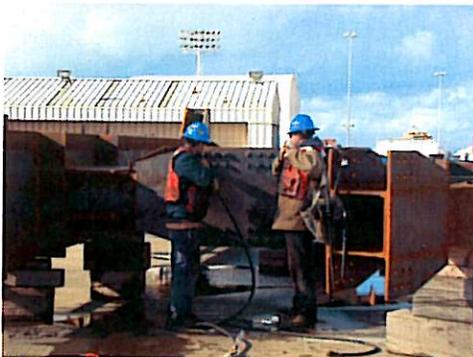


Fig 1



Fig 2

REC'D '09 JAN 28 #008444

Inspector:

SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
