

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no. 738
Project working days no. 948
Date 12/20/2008
Inspectors Hours Start 07:00 Stop 12:00
Shift Hours Start 06:30 Stop 15:30

Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower A, B and C erections
Weather	HI: 50 F Low: 34 F Partly cloudy/ foggy

Equipment and/or labor			Hours - ITEM no.						Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental		IDLE	
	C	4100W crane		8					ABF
006-18-4293	C	Ingresoll Compressor		8					ABF
481-93-6013	R	Gnie Boom lift							ABF
	1	Jeff Scott		8					ABF crane operator
	1	Ed Meyer		8					ABF Foreman (erection)
	1	Carlos Valverde		8					ABF Foreman (bolt)
	1	Matt Chamberlain		8					ABF Iron worker
	1	James Sturgeon		8					ABF Foreman (erection)
	1	David Lucero		8					ABF Iron worker
	1	Mike Naday		8					ABF Iron worker
	1	Jerry Kubala, Jr.		8					ABF Iron worker
	1	Alex Bartlett		8					ABF Iron worker
	1	Casey Lux		8					ABF Iron worker
	1	Ernesto Fresquez		8					ABF Iron worker
	1	Jason Kent		8					ABF Iron worker

Description of Operation:

- Daily activity of contractors
 - ABF continued to prepare the shipment from China (see Figs 1 and 2)
 - See Mark Vilcheck and Art Pannu's diary for contractors' activities and comments.
- Note
 - 5 hours O.T.
 - Dan told me that ABF is planning to pretension the bolts of Tower CW on either Monday or Tuesday.



Fig 1

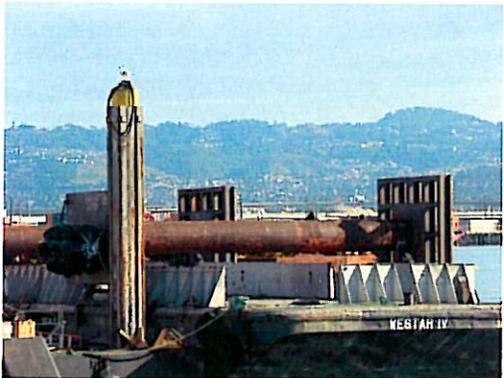


Fig 2

Inspector: SeongHyeok Song Trans Engineer (Civil) / Asst. Struct. Rep
