

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – Superstructure
Week ending 2009-01-30

Tuesday January 27, 2009: Observation via Engineer's Boat between 1000 and 1230 –
Clear, Cool, and Calm.

- E2 – West Elevation




E2 – North Elevation - PT layout




RECTD*09 FEB-06 #006500

E2- West Elevation –Patching & Finishing Vertical Concrete Face

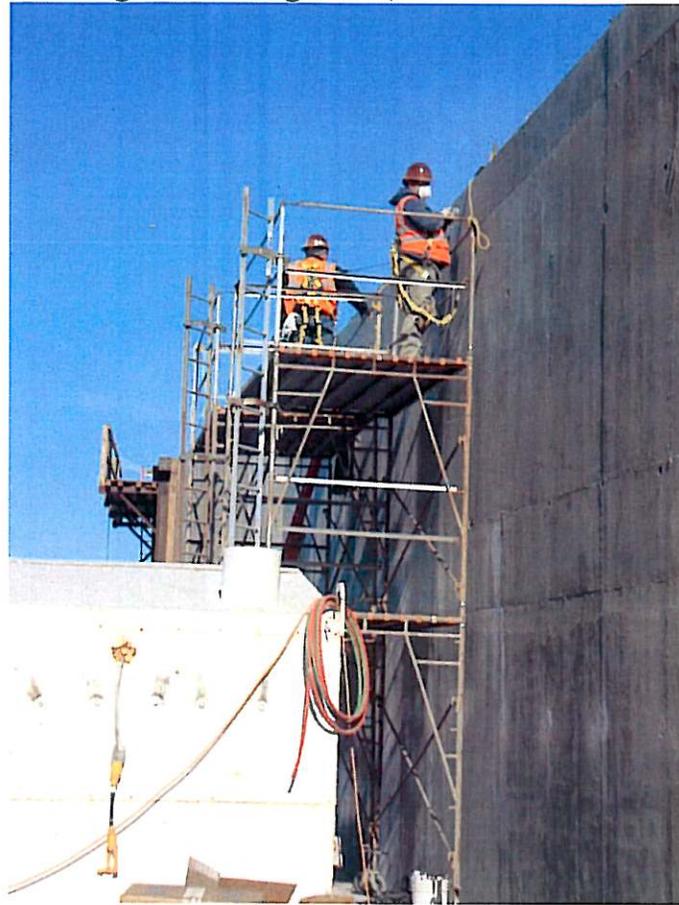


E2 – South Elevation - Drilling concrete from PT Duct

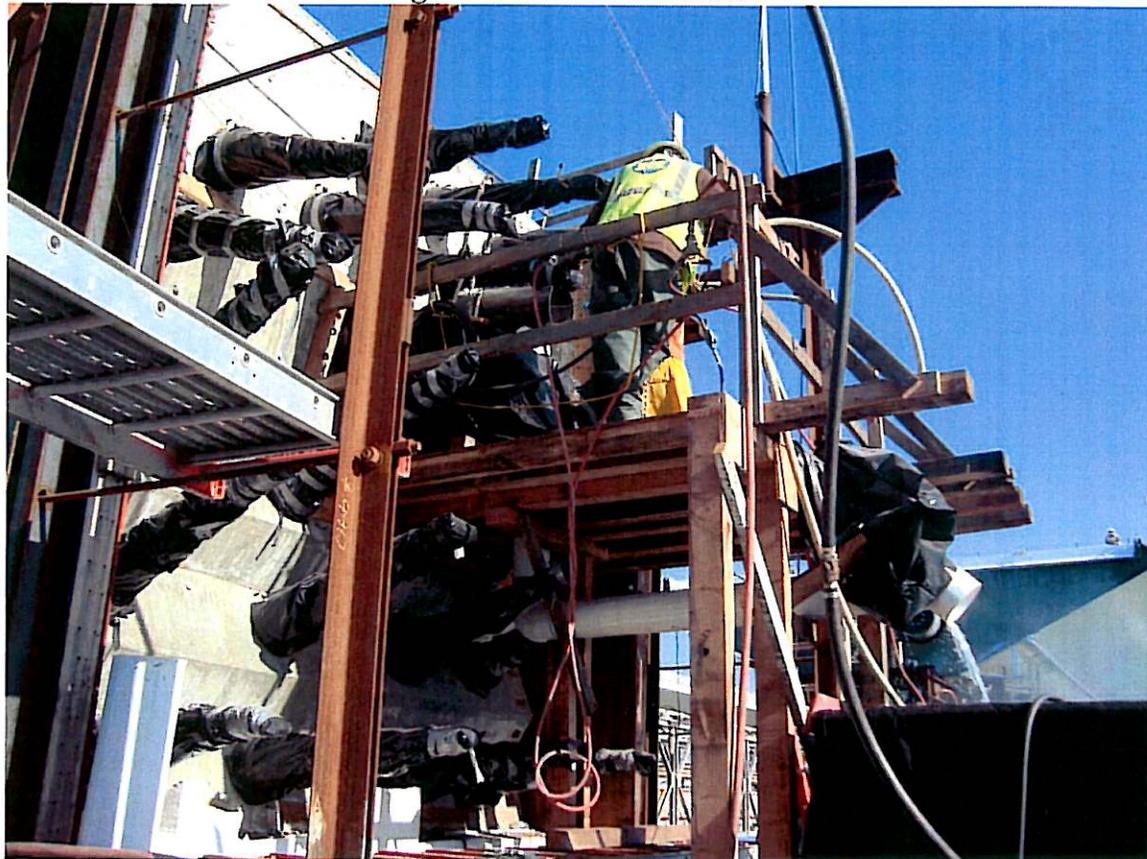


E2 – East Elevation - Patching & Finishing Vertical Concrete Face



E2 – View of Southerly portion of Top surface from Skyway

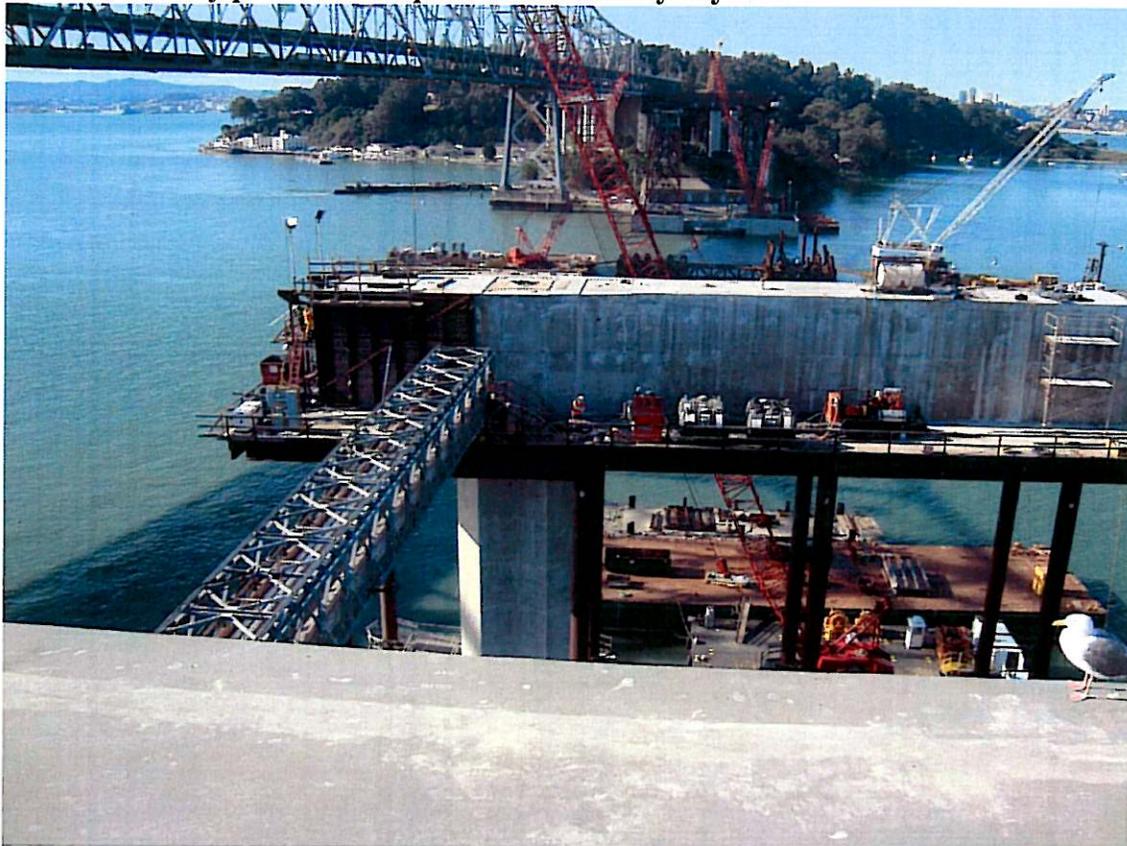

E2 – View of Northerly portion of top surface from Skyway (aka sea gulls at rest – got any crumbs?)

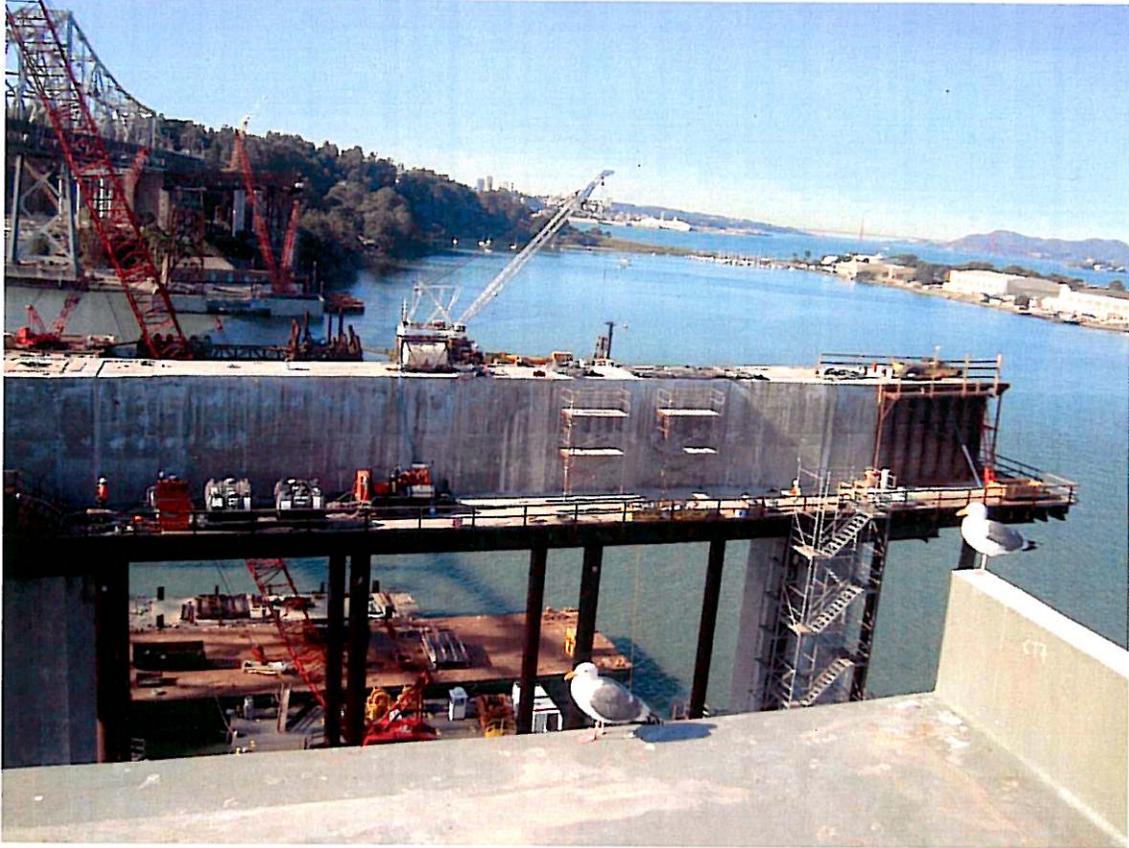

• Temporary Tower “F” – W-Line Foundation



TT "F" W-Line – State of progress – Some piles in Wait Period for re-tap, some have Plate Welding in process



E2 – Plate Welding



TT "F" – View of E-Line foundation from W-Line



TT – "F" – View of both W-Line & E-Line with adjoining structure




- Temporary Tower “D” – Tower “DWW” Line being erected



TT “D” – Bolting Temporary Tower “DWW”



TT "D" – E-Line Towers in foreground – W-Line in background

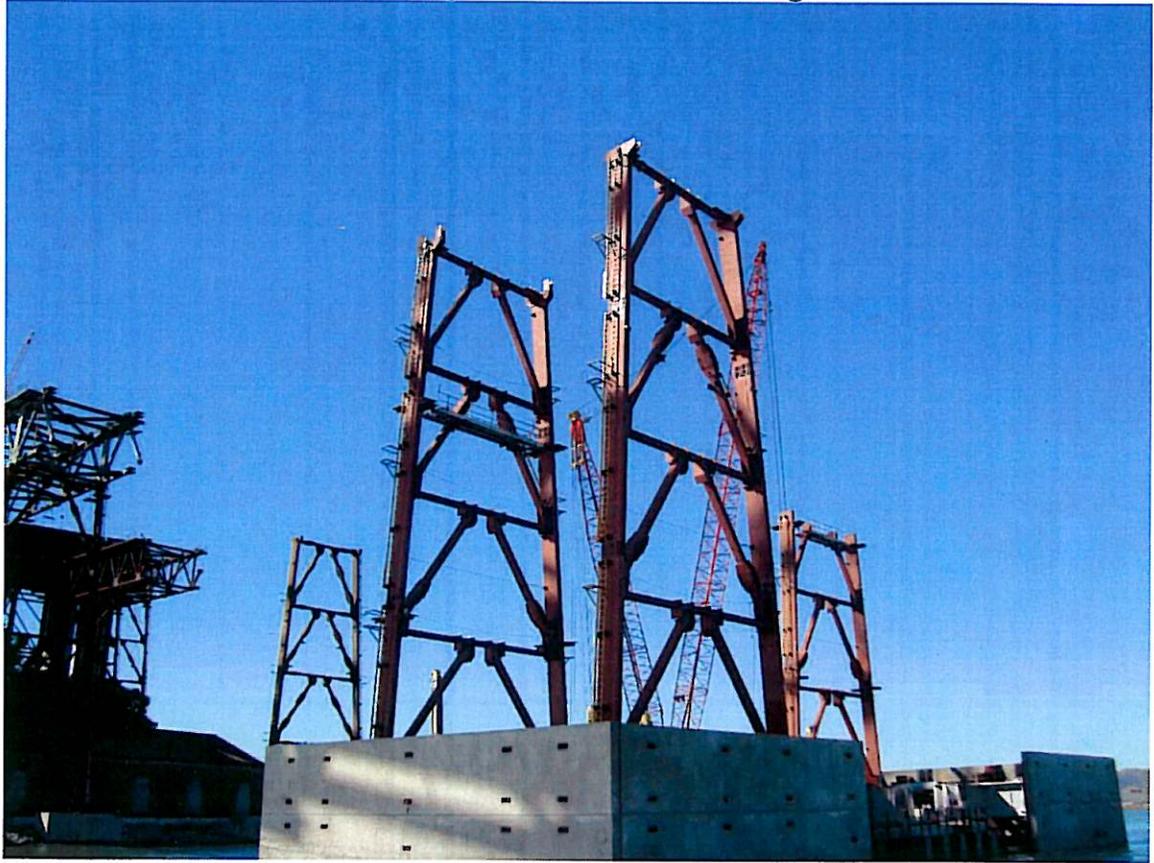

Temporary Trusses being moved by Tug @ Pier 7



Thursday January 29, 2009 : Observation from Yerba Buena Island between 1100 and 1200 – Clear, Cool and moderate Wind


- **Classical West Elevation View of E2**




- **Temporary Tower “FW” Foundation – Wait period for pile re-tap**



- Temporary Tower “DWW” – now full height “DWE” to be erected following erection of T1 Tower Lift 1 to allow access

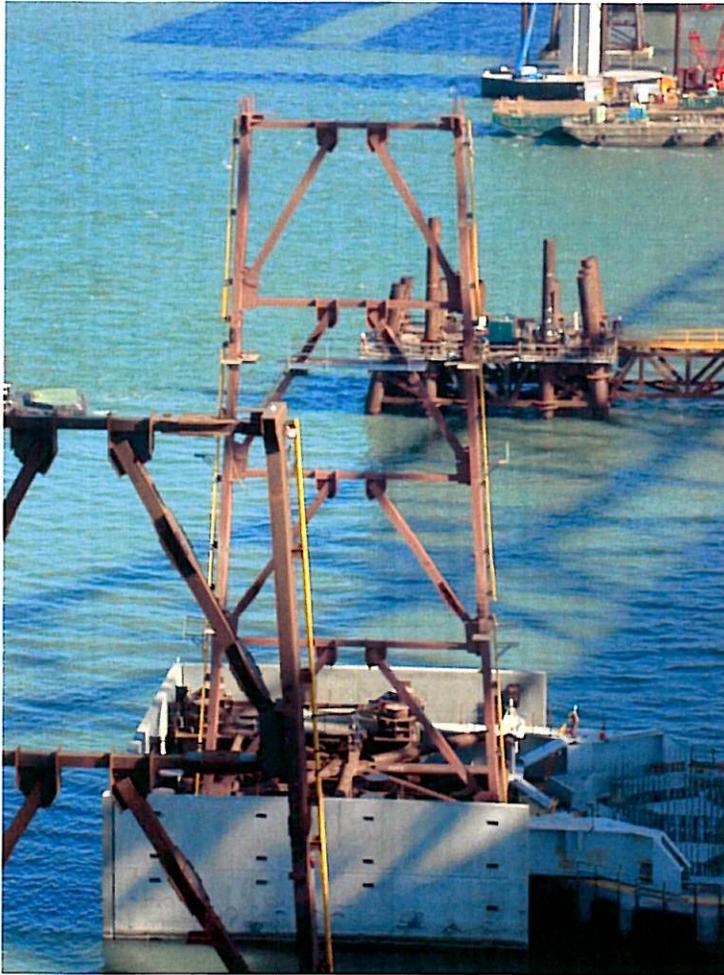


Temporary Truss W-line @ Temporary Tower “C” Area

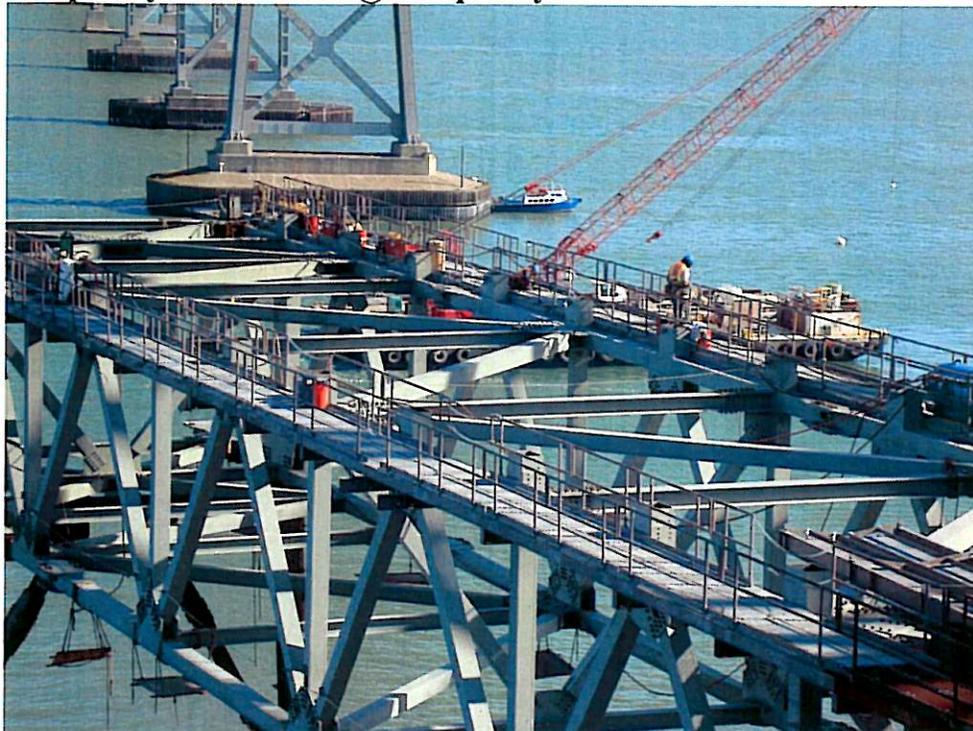


- **Temporary Truss E-Line and Temporary Towers “DEW & “DEE”**



Temporary Truss E-Line out to Temporary Tower “CE”

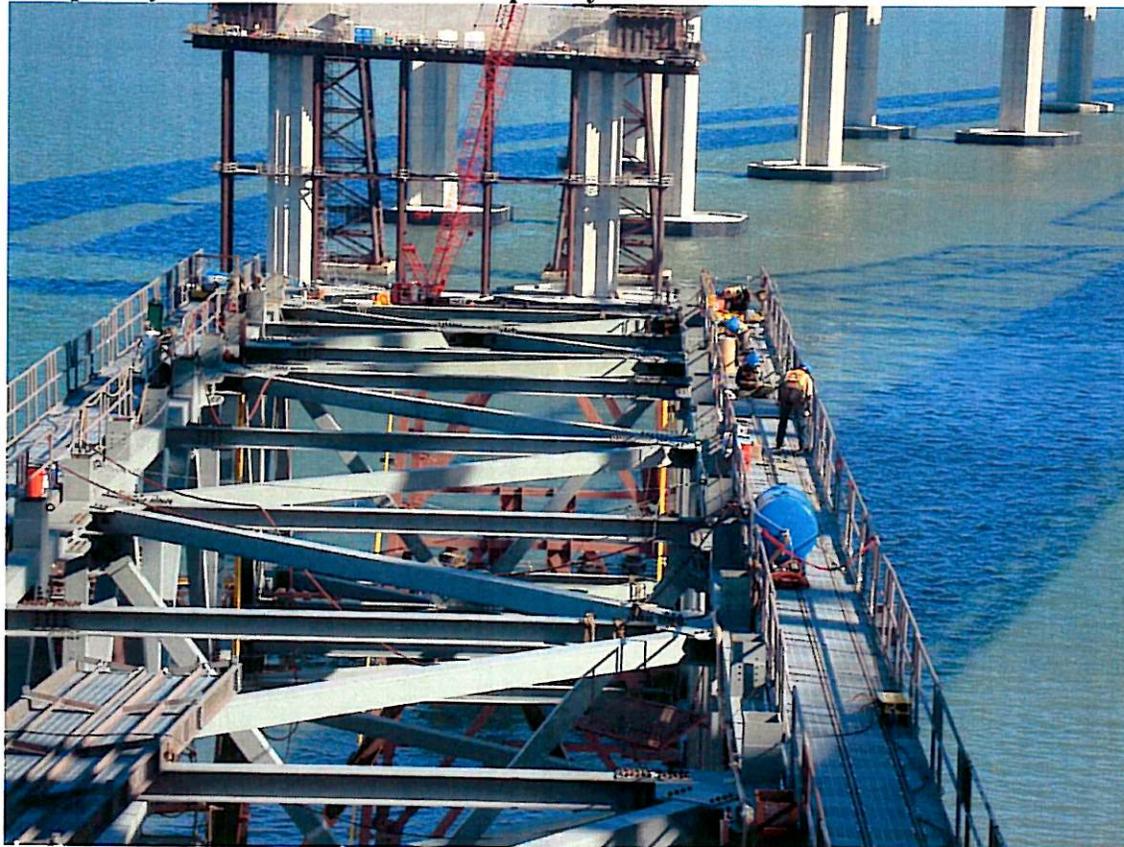

- **W2 – South Pour #6 – Concrete placement scheduled for Friday night 1-30-2009 (South East Area)**

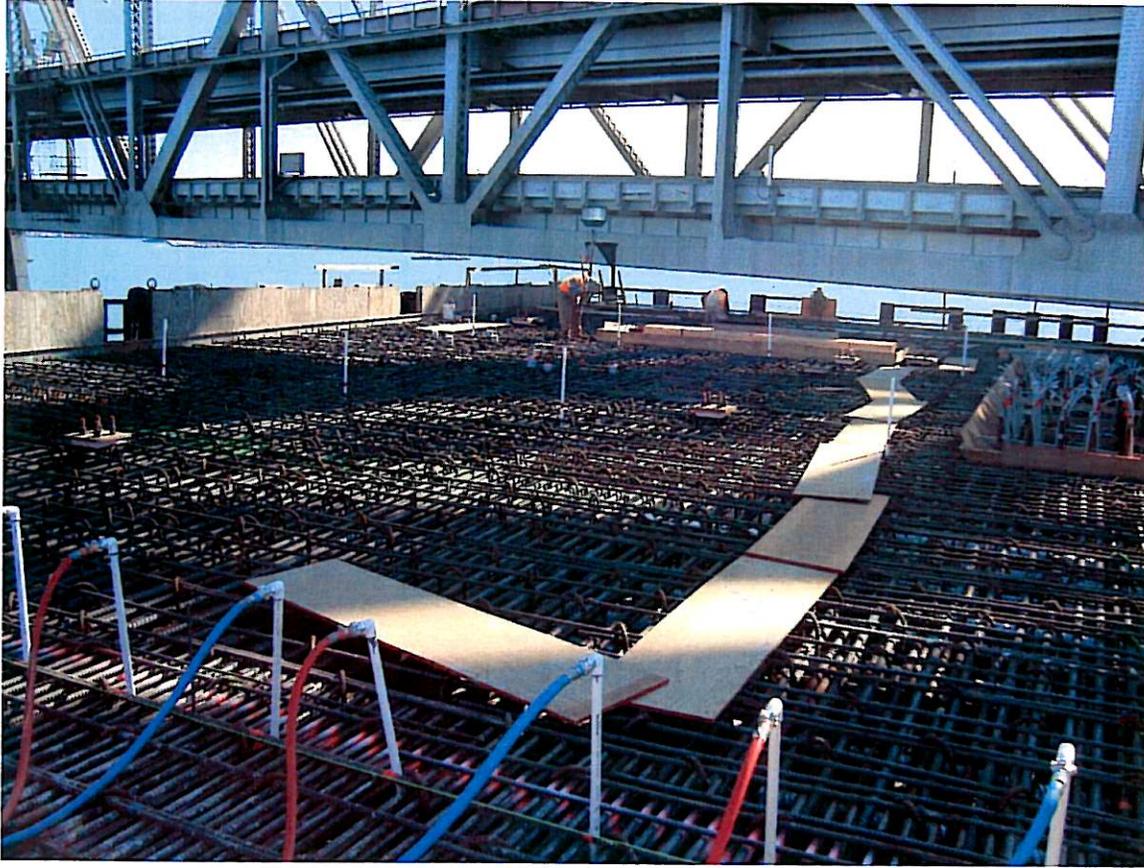


W2 – South Pour #6 Area (South West Area)



W2- Pour #6 South Area Anchor Bolts



W2 – Pour #6 North Area – Scheduled for concrete placement in approximately 2 Weeks – Flying Rebar

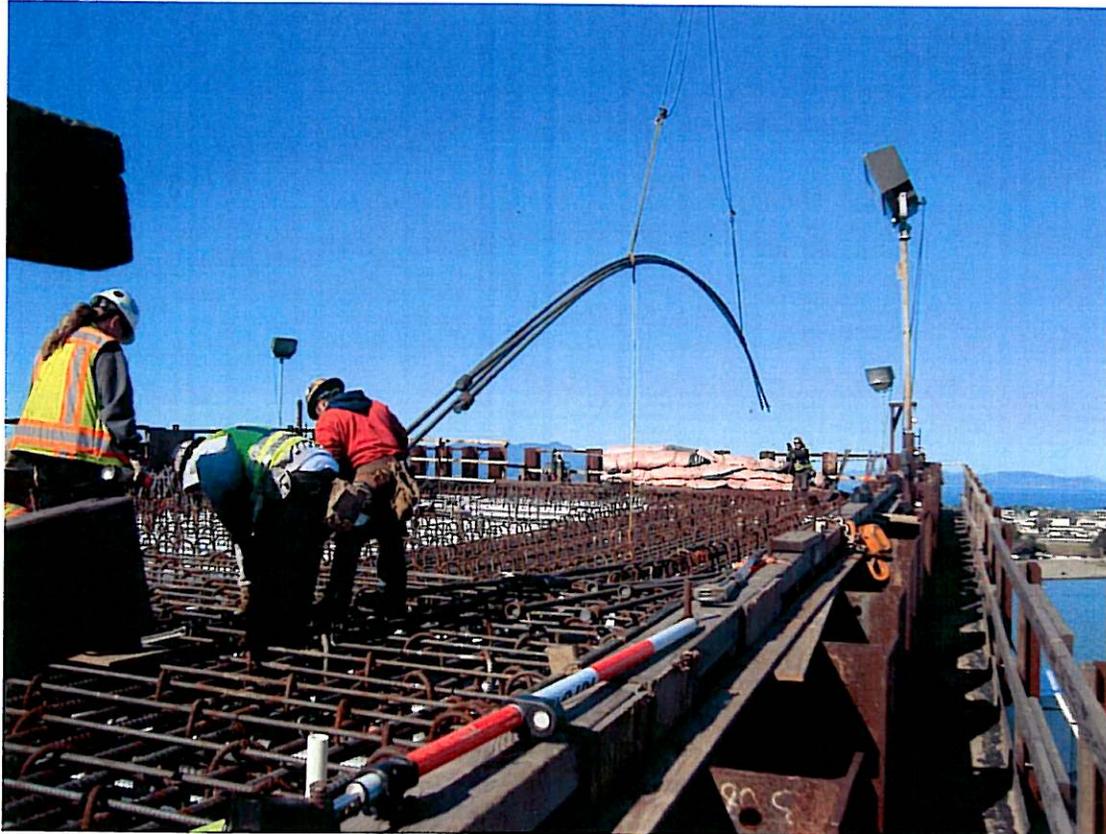

W2 – North Pour #6 Area

