


STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION  
Contract 0120F – SFOBB – Superstructure  
Week ending 2009-02-27

**Thursday February 26, 2009:** Observation from Yerba Buena Island between 1300 and 1430 – Partly Cloudy, Cool with moderate wind.

- West Elevation of E2 – Pedestrian Bridge removed a couple of weeks ago – preparing blockouts for concrete



- Temporary Tower “F” Foundation – West & East Bound - Erection of Tower “FE” commencing

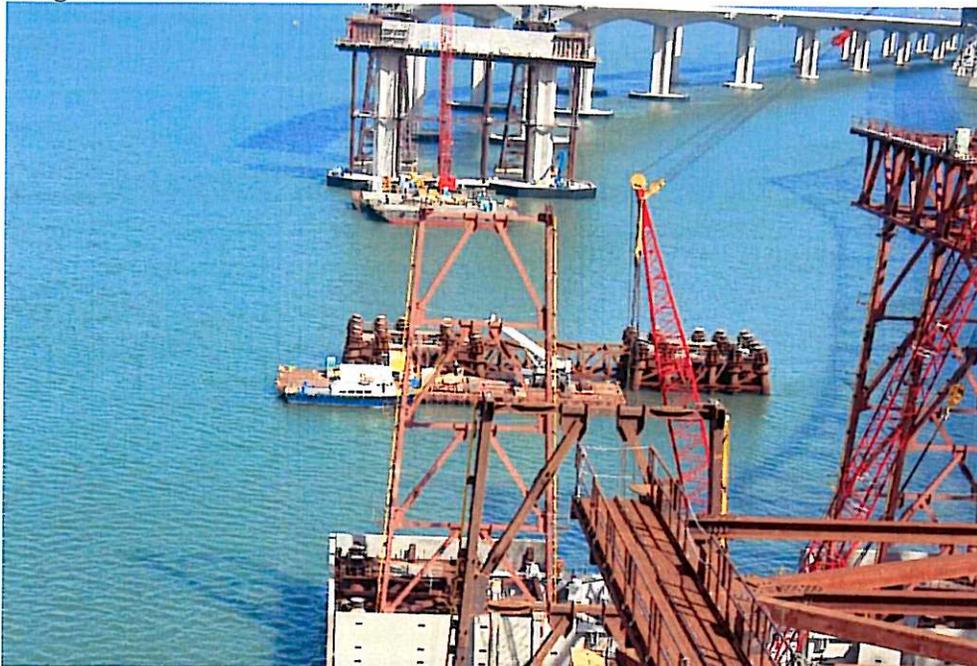

REC'D 09 MAR 02 #008872

- TT “GE” Driving Frame @ Pier 7 – Scheduled to be towed to location on Monday 3-2-2009



Another view of “GE” Driving Frame – “GW” Driving Frame scheduled to arrive late March.



- W Line – Truss @ TT “BW+”, TT “CW” & “DWW” – No progress this period




“E- Line” – Truss work progressing between “C” & “D”



- “E” Line – More distant view



E Line Truss – View form ground level

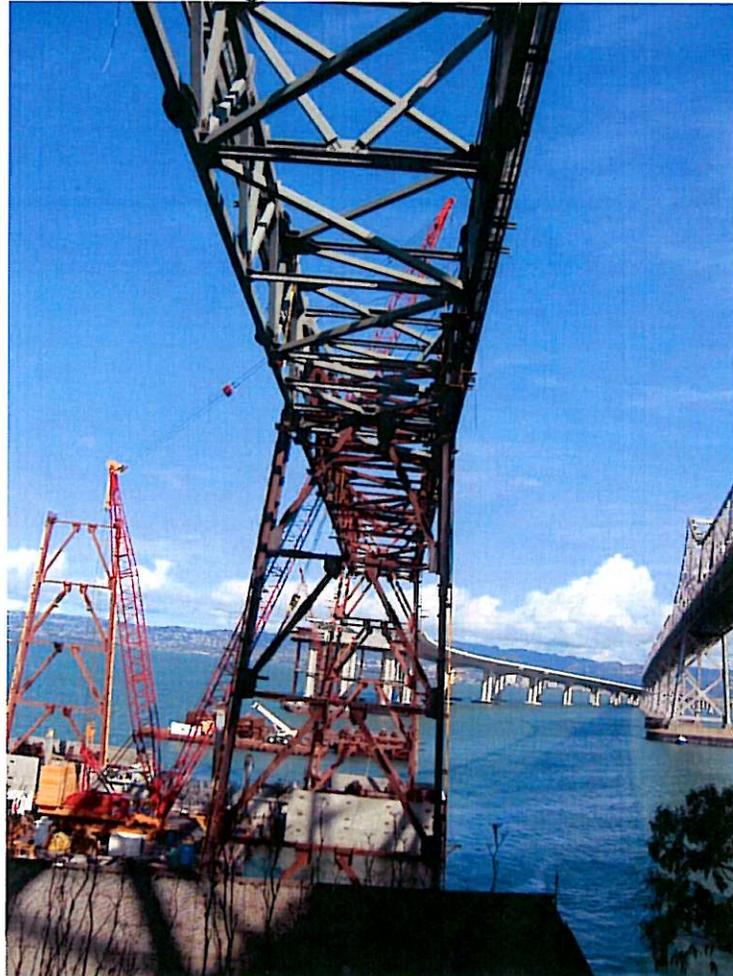

- **W2 – Removing Forms @ South West corner**



**W2 Form removal @ South East corner**



**W2 – Pour 6 North area – Placed Friday/Saturday 2-20/2-21-09 – Curing & Cooling in progress**



**W2 – Showing stripped area along South West Elevation**

