




STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 1020F - SFOBB - SAS - Superstructure
Larry Gustafson - Senior Scheduler
Week Ending 5-Jun-2009

Tuesday June 2, 2009: Observation from Engineer's Boat between 1330 and 1430 -
Mostly Sunny, Warm, Light Breeze

- E2 - Support barge has been removed



- Temp Tower Foundation "GE" - (Tower scheduled to be erected this week)

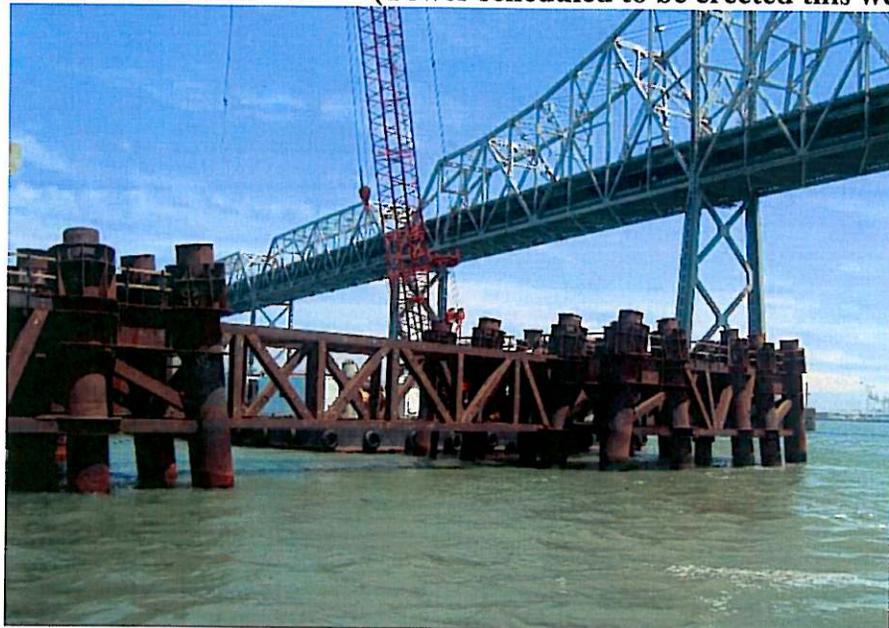

- **"E" Line Temporary Truss @ Temporary Tower "F"**



"E" Line Temporary Truss (Bolting-up Work in progress)



- **East Elevation of W2 from water level**



- **Shearleg crane at anchor (North of "W" Line Temp Truss)**



- **Traylor-Dutra Pile driving crane being removed from project**



- **Prep work continues on Temp Truss "W" (B.5 to D) at Pier 7 - (scheduled to be moved to site tomorrow Wednesday 3-Jun-2009)**



Thursday June 4, 2009 : Observation from Yerba Buena Island between 0930 and 1100 - Mostly Overcast, Warm, and Calm.

- **Temporary Truss "W" (B.5 to DWW) had been lifted and transported into location earlier in Morning**



Temporary Truss "W" (B.5 to DWW) from ground level




Bolting at B.5 connection



Connection at DWW Tower



Lifting harness

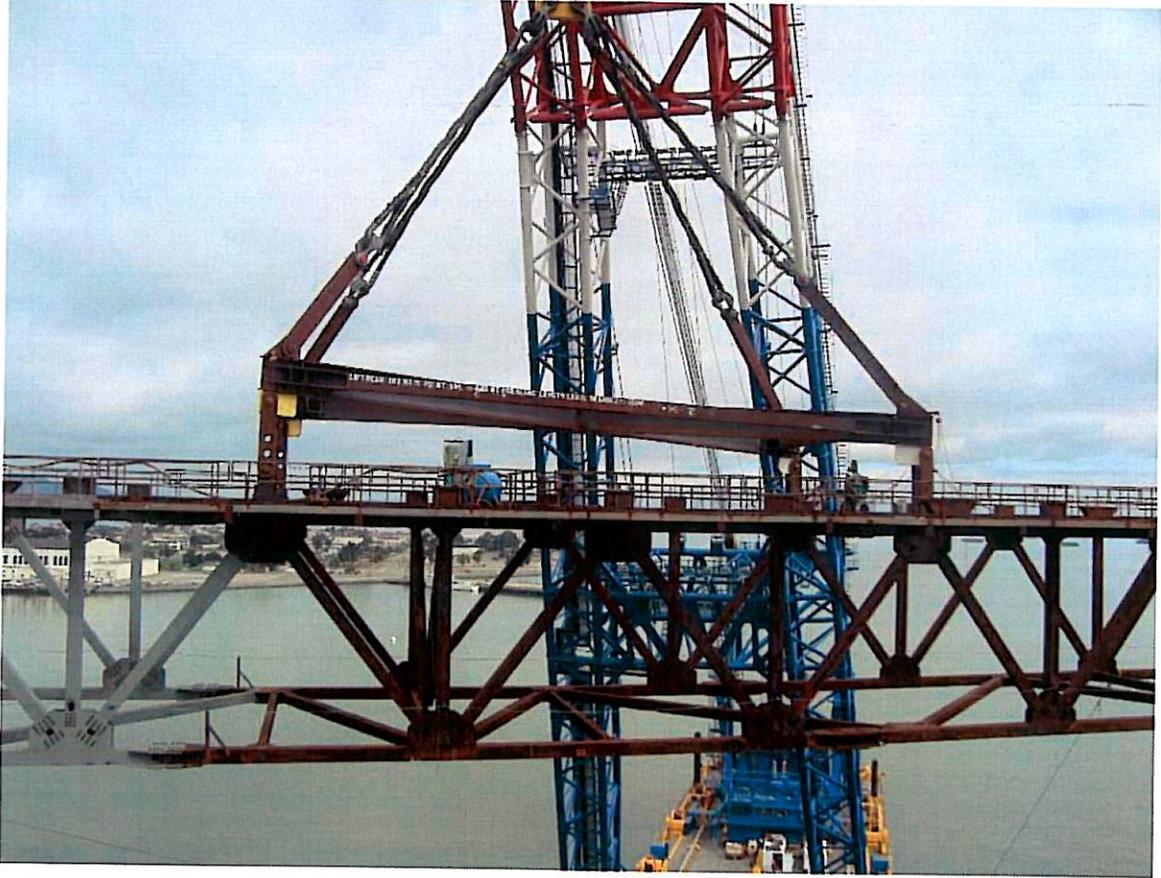

View of Shearleg Crane deck



View showing DWW termination looking toward W2



Temporary Truss DWW showing Temporary Tower DWW



Top view of Temporary Truss W (B.5 to DWW)



Another top view showing W Line to left, E Line to right, T1 Foundation (TTD) in foreground, then TT F, G Foundation and E2



- **W2 Northern portion of West Elevation**



W2 Southern portion of West Elevation



Strand Jack installation continues



Strand Jacks at South Elevation



Removal of Form Shores continues



Flying a removed Form Shore

