


Description of Operation:
Erect Temporary Towers: TTGS Pile Rehandling

All day the crew of the DB-5 worked on rehandling the piles that are to be used as the top portions of the piles for Temp Tower G, South. They were able to finish all of the piles they wanted to finish by mid afternoon

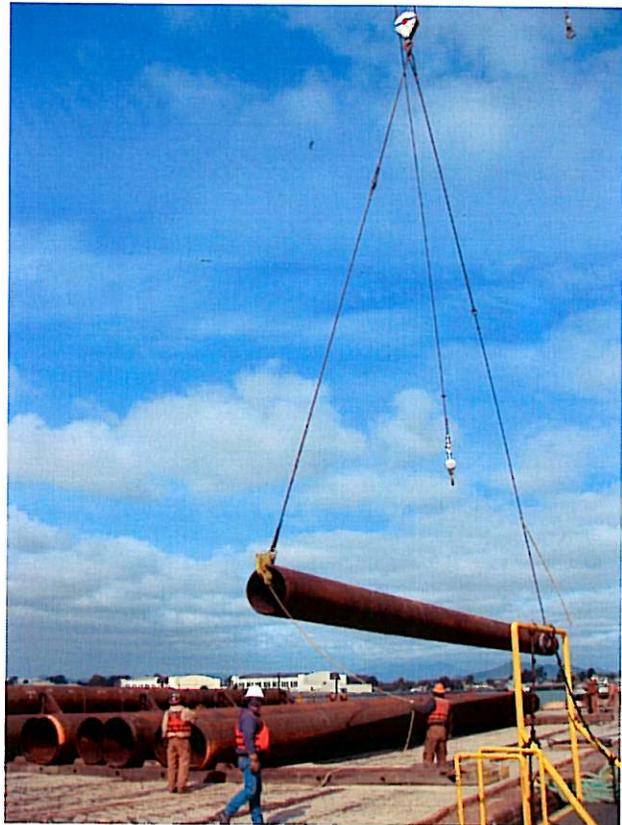

Once the piles were in place and secured, a couple workers began welding the seal welds between the backing bar and the bottom of the pile top. There is a gap between the two pieces of steel because of the imperfect fit up of the two different rolled pieces of steel.

A couple workers were on the frame preparing the ares for splice welding which will begin tomorrow. Some of the welding platforms were placed and the tops of the first couple pile bottoms were ground in preparation of the welding.

The last couple hours did not warrant continual inspection or documentation since they were just preparing items for work on Monday. I worked 8 hours but they worked 10 hours today.

OVERTIME: Due to this work being on a Saturday, all 8 hours worked are overtime hours.

Inspector:

Jason Wilcox



Transportation Engineer (D)/Asst. Structure Rep.
