

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 874
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1084
Form HC-10A (Rev. 6/80)	04-0120F4	Date	5/5/2009

Weather: Scattered showers and cool (AM)
Partly cloudy (PM)

Inspectors Hours Start 0630 Stop 1700

Shift Hours Start 0630 Stop 1700

ASSISTANT STRUCTURE REP.

CONTRACTOR – TRAYLOR DUTRA JV

JASON WILCOX

HOURS - ITEM NO. 8												
EQUIPMENT AND/OR LABOR:			REGULAR	OVERTIME	DOUBLE TIME	NIGHT PAY					IDLE OR DOWN	REMARKS
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor) Traylor Dutra										Name Contractor
		Foreman	8	2								Terry Murray Traylor-Dutra
		Foreman										Richard Hiebert Traylor-Dutra
		Welding Foreman	8	2								Lee Tacker Traylor-Dutra
		Operator	8	2								Joe Borraci Traylor-Dutra
		Operator	8	2								Todd Labar Traylor-Dutra
		Operator	8	2								Kurt Dillard Traylor-Dutra
		Pile Driver Journeyman	8	2								Danny Vega Traylor-Dutra
		Pile Driver Journeyman										Adam Price Traylor-Dutra
		Pile Driver Journeyman	8	2								Robert Utley Traylor-Dutra
		Pile Driver Journeyman										Richard Heibert Jr Traylor-Dutra
		Pile Driver Journeyman	8	2								Gilbert Moya Traylor-Dutra
		Pile Driver Journeyman	8	2								Ventura Ochoa Traylor-Dutra
		Pile Driver Journeyman										Travis Logsdon Traylor-Dutra
		Pile Driver Journeyman	8	2								Steve McGrew Traylor-Dutra
		Pile Driver Journeyman	8	2								Jake Lavash Traylor-Dutra
		Certified Welding Inspector	8	2								Andrew Erthum CWI
		Certified Welding Inspector	8	2								Michael Johnson Smith-Emery
DB-5		Derrick Barge crane	10									
Big Digger											IDLE	
Morty											IDLE	
217			10									
L437	1	Multiquip Generator	10									
L478	1	Multiquip Generator									IDLE	
L270	1	Sullivan-Palatek Air Compressor	10									

	2	Red-D-Arc DC600 Welding Machines	10											
P242	1	Manlift											IDLE	
L624	1	Light Station											IDLE	
L625	1	Light Station											IDLE	
L626	1	Light Station											IDLE	
L629	1	Light Station											IDLE	
	4	LN-25 Weld Machines	10											
	4	Red-D-Arc DC360 Welding Machines											IDLE	
	1	APE 600 Vibratory hammer											IDLE	
	1	Delmag D-100 diesel hammer											IDLE	

Description of Operation:

Erect Temporary Towers: Pile Splice Welding TTGN and Truss Erection at Segment 6E

FIELD WORK:

TTGN Splice Welding:

The rain in the morning delayed the beginning of splice welding this morning. Some of the workers laid out the tarp used to protect the welds from rain water and got them ready to attach to the pile tops. They started by picking up the pile top for G111. Once the root was run and MT'd and accepted the fill passes began until the splice was completed. The second pile top picked and placed was G109. The MT was accepted and filling continued until the end of the day, when there was enough material to remove the crane from it.




- Set pile top: G109 and G111
- UT G111 splice

Thanh Le is not in today because he is attending a class.

Truss Erection Segment 6E:

Ironworkers continued to erect Segment 6E on the E-Line of the Temp Towers. They installed one of the diagonal members that did not have the holes pre-drilled in it. In order to do this they had to use the jacking system to manipulate the frame so that the surveyors could verify position.

Masoud Modanlou is in a Confined Space training class this morning but he did get the diary for the truss assembly and erection at E-Line transition segment 6E.

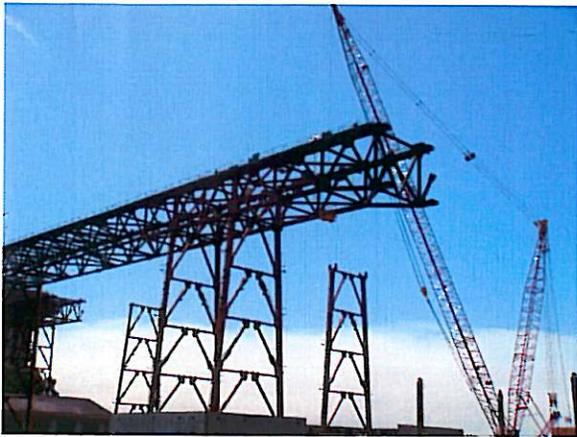

OFFICE WORK:

- Finished yesterdays diary
- Attended the 0800 hours Temp Tower staff meeting
- Reviewed diaries
- Reviewed Special Provisions and Plans
- Attended the 1330 hours Temp Tower construction meeting

OVERTIME: Accrued 2 hours of overtime covering the Contractors operations.

Inspector:

Jason Wilcox

Transportation Engineer (D)/Asst. Structure Rep.
