

Job Stamp

04-0120F4
SFOBB SAS

Const. Calendar Day No 889

Project Work Day No. 1099

Date 05/20/2009


Shift Hours Start 7:00 Stop 5:30

Inspector Shift 7:00 AM to 5:00 PM

ASSISTANT STRUCTURAL
REPRESENTATIVE.

CONTRACTOR - ABFJV


| EQUIPMENT AND/OR LABOR: | | HOURS - ITEM NO. | | | | | | | | | | REMARKS | | |
|-------------------------|---------|-------------------------------------|---------|-----------|-----------|--|--|--|--|--|--|--------------|-------------------|------------|
| Equip. # | NO. MEN | DESCRIPTION (Of Equipment or Labor) | Regular | Over Time | Surveying | | | | | | | IDLE OR DOWN | Name | Contractor |
| | 1 | Temp tower and trusses | | | | | | | | | | | | |
| | | Iron Worker Foreman | 8 | | | | | | | | | | Ed Meyer | ABF/ JV |
| | | Iron Worker App. | 8 | | | | | | | | | | Matthew Cochran | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Stanley Dalie | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Jerry Kubala | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Kevin Ratcliffe | ABF/ JV |
| | | Iron Worker Foreman | 8 | | | | | | | | | | Carlos Valverde | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Steven Batiste | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Josue Galvan | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Gabriel Rios | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Kelly Anderson | ABF/ JV |
| | | Iron Worker Foreman | 8 | | | | | | | | | | James Sturgeon | ABF/ JV |
| | | Iron Worker | 8 | | | | | | | | | | Troy Christianson | ABF/ JV |
| | | Iron Worker | 8 | | | | | | | | | | Matt Chamberlain | ABF/ JV |
| | | Iron Worker App. Mechanic | 8 | | | | | | | | | | Ronald Damerall | ABF/ JV |
| | | Iron Worker App. | 8 | | | | | | | | | | Ethan Kent | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Serina Lafleur | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Casey Lux | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Mike Maday | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Barry Rothman | ABF/ JV |
| | | Iron Worker Jrny | ----- | | | | | | | | | | Wes Woodring | ABF/ JV |
| | | Iron Worker Foreman | 8 | | | | | | | | | | David Lucero | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Brian Benson | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Aaron Kent | ABF/ JV |
| | | Iron Worker Jrny | 8 | | | | | | | | | | Jose Meza Amaya | ABF/ JV |
| | | Crane Operator | 8 | | | | | | | | | | Obra Paulk | ABF/ JV |
| | | Crane Operator | 8 | | | | | | | | | | Rodney Anderson | ABF/ JV |
| | | Crane Operator | 8 | | | | | | | | | | Ernie Hamilton | ABF/ JV |
| | | Oiler | 8 | | | | | | | | | | Mike Klein | ABF/ JV |
| | | Oiler | 8 | | | | | | | | | | Daniel Martinez | ABF/ JV |
| | | Oiler | 8 | | | | | | | | | | Chris Rayne | ABF/ JV |

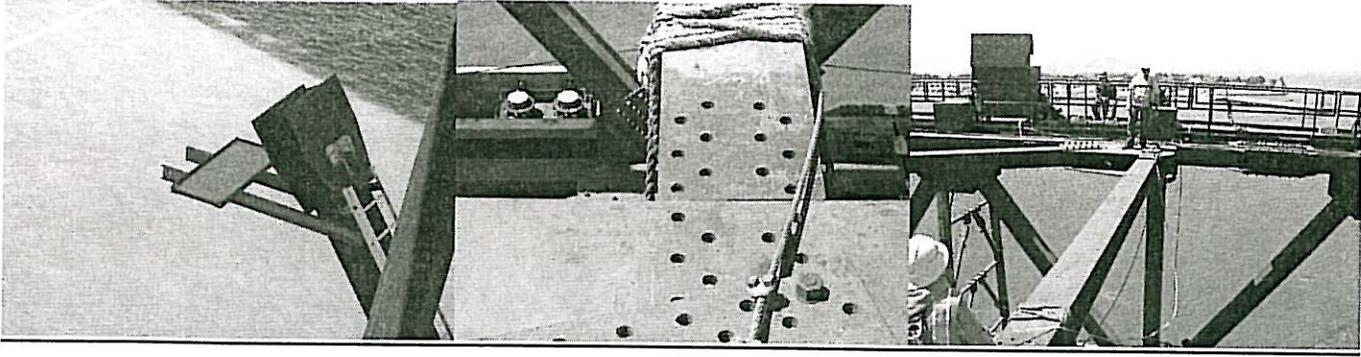

1. Running safety cables along the lower chords of truss segment from tower B to tower D of W line and from tower D to tower F of E line.
2. Grinding weld bead on cradle pedestal seats for easy installation of pedestals at W line.
3. Installing walkway across of the truss S6E.
4. Welding platform on diagonal member of truss S6E for SFE12 splicing.
5. Bolting splices of segment S6E is complete except a cross beam, WD at PPE40, at upper plane, which the connection plate's boltholes are not matching with the holes drilled at either end of the WD beam. ABF field engineer, Adam Roebuck and his assistant, checked and sketched the pattern and measurement of the boltholes on connection plats and on the beam for further study and correction. It seems the holes drilled on beam are not in the same line with the bolt holes drilled on upper chords.

Miscellaneous

Additional Work on/off site:

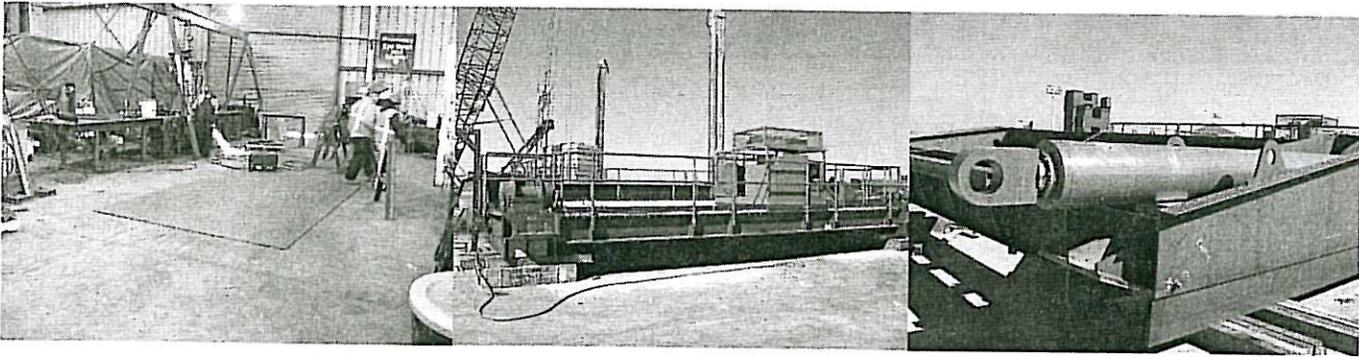

1. Cutting and carbon arc removal of the steel pedestal welded on the barge floor.
2. Assembling of a new flexi float at berth 7 is in progress..
3. Installing a pair of winches at one end and a pair of hydraulic jacks with hydraulic pump at the other end of assembled cradle pushing frame.
4. I worked 2.00 hours overtimes to cover contractor operation.

Inspector:

Masoud Modanlou

 Trans Engineer (C)/Asst. Struct. Rep

report day 889
Page 3 of 3
