

Job Stamp

04-0120F4
SFOBB SAS

Const. Calendar Day No 904

Project Work Day No. 1114

Date 06/04/2009


Shift Hours Start 5:00 Stop 9:30

Inspector Shift 5:30 AM to 6:00 PM

ASSISTANT STRUCTURAL
REPRESENTATIVE.

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	Over Time	Surveying							IDLE OR DOWN	Name	Contractor
		1 Temp tower and trusses												
		Iron Worker Foreman	8	4									Ed Meyer	ABF/ JV
		Iron Worker App.	8	4									Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8	4									Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8	4									Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8	4									Kevin Ratcliffe	ABF/ JV
		Iron Worker App.		4									Chris Biskner	ABF/ JV
		Iron Worker Foreman	8	2									Carlos Valverde	ABF/ JV
		Iron Worker Jrny	8	2									Steven Batiste	ABF/ JV
		Iron Worker App.	8	2									Jose Morales	ABF/ JV
		Iron Worker Jrny	8	2									James Wilkerson	ABF/ JV
		Iron Worker Jrny	8	2									Josue Galvan	ABF/ JV
		Iron Worker Jrny	8	2									Gabriel Rios	ABF/ JV
		Iron Worker Jrny	8	2									Kely Anderson	ABF/ JV
		Iron Worker Foreman	8	2									James Sturgeon	ABF/ JV
		Iron Worker											Troy Christianson	ABF/ JV
		Iron Worker	8	2									Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic											Ronald Damerl	ABF/ JV
		Iron Worker App.	8	2									Ethan Kent	ABF/ JV
		Iron Worker Jrny	8	2									Serina Lafleur	ABF/ JV
		Iron Worker Jrny	8	2									Casey Lux	ABF/ JV
		Iron Worker Jrny	8	2									Mike Maday	ABF/ JV
		Iron Worker Jrny	8	2									Barry Rothman	ABF/ JV
		Iron Worker Jrny	-----										Wes Woodring	ABF/ JV
		Iron Worker Foreman	8	2									David Lucero	ABF/ JV
		Iron Worker Jrny	8	2									Brian Benson	ABF/ JV
		Iron Worker Jrny	8	2									Aaron Kent	ABF/ JV
		Iron Worker Jrny	8	2									Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8	2									Obra Paulk	ABF/ JV
		Crane Operator	8										Rodney Anderson	ABF/ JV
		Crane Operator	8										Ernie Hamilton	ABF/ JV

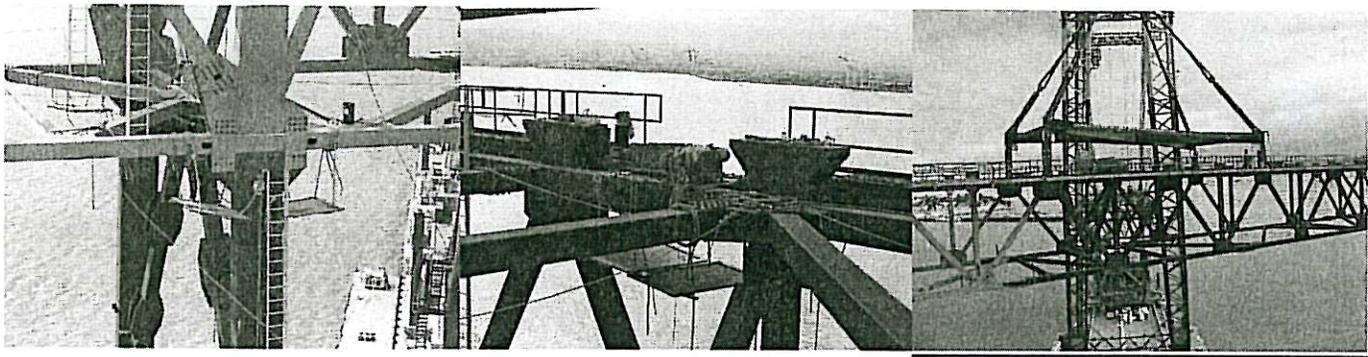

1. Erection of truss from tower B to tower D, W line, started at about 5:30 O'clock in the morning and continued till 5:00 o'clock in the afternoon. Jason Wilcox covered contractor operation from 5:30 to almost 9:30 in the morning and I covered since then because, I was hosting the safety meeting. The pick total weight was about 850 metric tons including the rigging. At about 10:00 am, positioning and alignment of truss with existing erected truss completed and bolting upper chords at field splice W4 started. At about 11.00 o'clock ironworkers started to jack the bottom chords of FS W4 for bolting, at the same time bolting started at vertical (diagonal) bracings. Alignment of connections at tower "C" took place simultaneously, drilling holes in tower connection plates for minimum fasteners required before the release of Shear Leg pick up assembly started, At 4:30 in the afternoon the minimum number of bolts required were installed, and the Shear Leg was released.
2. I was hosting safety meeting from 8:00 am.

Miscellaneous

Additional Work on/off site:



1. Ironworkers are welding forms for concrete pad f on San Clemente TSL barge for OBG's supporting frames.
2. Setting rebar inside of concrete pad form continued.
3. Preparation work on OBG cradles for installation continued.
4. Assembling of flexi-float continued today.

Inspector:

Masoud Modanlou

 Trans Engineer (C)/Asst. Struct. Rep
