

Job Stamp

04-0120F4
SFOBB SAS

Const. Calendar Day No 926

Project Work Day No. 1136

Date 06/26/2009

Shift Hours Start 6:30 Stop 3:30

Inspector Shift 7:00 AM to 3:30 PM

ASSISTANT STRUCTURAL
REPRESENTATIVE.

CONTRACTOR – ABFJV


EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEEN	DESCRIPTION (Of Equipment or Labor)	Regular	Over Time	Surveying							IDLE OR DOWN	Name	Contractor
		1 Temp tower and trusses												
		Iron Worker Foreman	8										Ed Meyer	ABF/ JV
		Iron Worker App.	8										Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8										Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8										Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8										Kevin Ratcliffe	ABF/ JV
		Iron Worker App.											Chris Biskner	ABF/ JV
		Iron Worker Foreman	8										Carlos Valverde	ABF/ JV
		Iron Worker Jrny	8										Steven Batiste	ABF/ JV
		Iron Worker App.	8										Jose Morales	ABF/ JV
		Iron Worker Jrny	8										James Wilkerson	ABF/ JV
		Iron Worker Jrny	8										Josue Galvan	ABF/ JV
		Iron Worker Jrny	8										Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8										James Sturgeon	ABF/ JV
		Iron Worker											Troy Christianson	ABF/ JV
		Iron Worker	8										Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic											Ronald Damerall	ABF/ JV
		Iron Worker App.	8										Ethan Kent	ABF/ JV
		Iron Worker Jrny	8										Serina Lafleur	ABF/ JV
		Iron Worker Jrny	8										Casey Lux	ABF/ JV
		Iron Worker Jrny	8										Mike Maday	ABF/ JV
		Iron Worker Jrny	8										Barry Rothman	ABF/ JV
		Iron Worker Jrny	-----										Wes Woodring	ABF/ JV
		Iron Worker Foreman	8										David Lucero	ABF/ JV
		Iron Worker Jrny	8										Brian Benson	ABF/ JV
		Iron Worker Jrny	8										Aaron Kent	ABF/ JV
		Iron Worker Jrny	8										Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8										Obra Paulk	ABF/ JV
		Crane Operator	8										Rodney Anderson	ABF/ JV
		Crane Operator	8										Ernie Hamilton	ABF/ JV
		Crane Operator	8										Mike Klein	ABF/ JV


		Oiler	8																		Daniel Martinez	ABF/ JV	
		Oiler	8																			Chris Rayne	ABF/ JV
		Deck Eng.	8																			Theo Rohr	ABF/ JV
		Deck Eng.	8																			Dick Shafer	
		Iron worker Foreman	8																			Frank Brajkovich	ABF/ JV
		Iron worker Jrny	8																			R. Clayborn	ABF/ JV
		Iron worker Jrny	8																			D. Bazewicz	ABF/ JV
		Iron worker Jrny	6																			Rory Hogan	ABF/ JV
		Iron worker Jrny	8																			Robert Johnson	ABF/ JV
		Iron worker Jrny	8																			Al McDaniel	ABF/ JV
		Iron worker Jrny																				Rick Royal	ABF/ JV
		Iron worker Jrny	8																			Salvador Sandoval	ABF/ JV
		Iron worker Jrny	8																			Harold W. Wheeler	ABF/ JV
		Iron worker Jrny	8																			James Zhen	ABF/ JV
		Iron worker App.																				Todd Jackson	ABF/ JV
		Iron worker App.																				Ryan Lockwood	ABF/ JV
		Iron worker App.																				Jeremy Dolman	ABF/ JV
240ft boom	1	Ringer barge I																					ABF/ JV
260ft boom	1	Ringer barge II																					ABF/ JV
481 93 5006 481 40 7013	2	Man lift																					ABF/ JV
	2	Welding machine																					ABF/ JV
58084	1	RT 160 crane																					ABF/ JV
6- 18-4293, 4217	2	IR Compressor																					ABF/ JV
549 07 5006	1	Generator																					ABF/ JV
412 10 7101 417 40 5029	1	Forklift																					ABF/ JV
Wetar I, II, XII	3	Barge																					ABF/ JV
KRS 180-8, 318	2	Barge																					ABF/ JV
TEC 35, 36, 27	3	Barge																					ABF/ JV
YC -1333	1	Barge																					ABF/ JV
OC 260, 261, 262, 265	4	Barge																					ABF/ JV

Weather: Sunny, 67 F

Description of Operation:

Trusses

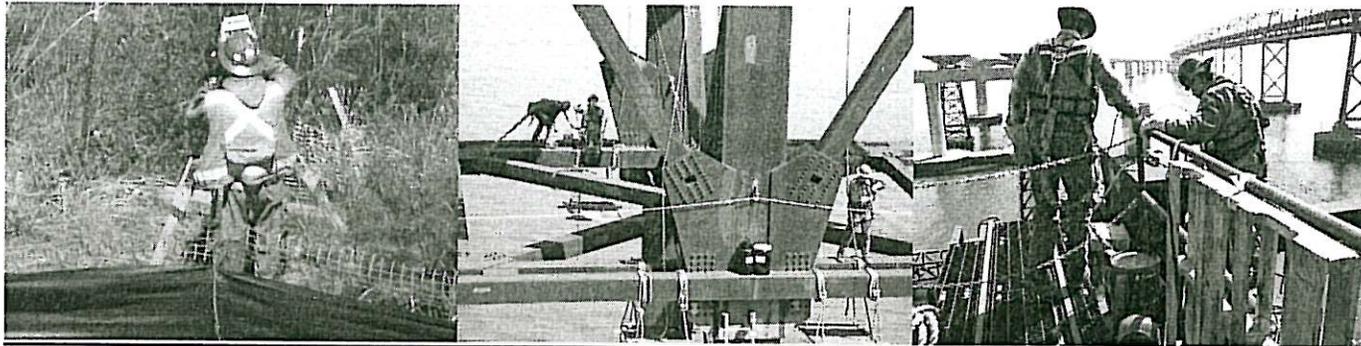

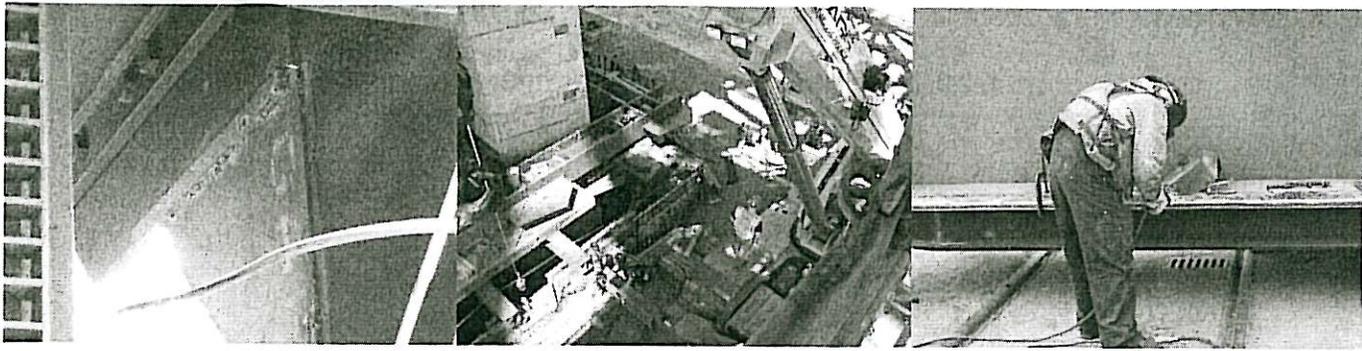

1. ABF surveyors are checking the alignment and level of erected truss at E line.
2. Bolting truss Gusset plates to lower D connection plate and sung tightening of the bolts, hammer head, W line.
3. Welding stiffener between gusset plates and truss vertical member at end of erected truss in E line. Neither WPS nor quality control personnel were present at job site for this welding. I report the case to Jason Wilcox and we both went to Gil Klebanov for further discussion, while discussing the welding on temporary towers and trusses, Rick Morrow joined the meeting and declared that because the work is temporary work and should be considered as false work no Caltrans inspection required and the work is the sole responsibility of the contractor and the contractor will furnish a certificate of compliance for all these temporary work before the erection of OBGs.
4. Preparation work for lifting collar frame to its position at W2 east pier column.
5. Welding stainless steel plates under the bottom flange of cradle assembly continued.

Miscellaneous

Additional Work on/off site:



1. Sorting and preparing bolts for using in towers and truss erection.
2. Installing cables to electro motors and running hoses between hydraulic pumps and jacks on the assembled Lift Center of Mass (LCM) frame is in progress at berth seven..
3. Welding pedestal on top of stringers of the frame built on barge to support OBG.
4. Assembling of flexi-float is in progress.

Inspector:

Masoud Modanlou

Trans Engineer (C)/Asst. Struct. Rep
