

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 89919
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1129
Form HC-10A (Rev. 6/80)	04-0120F4	Date	06/19/2009

Inspectors Hours	Start	0700	Stop	1530
Shift Hours	Start	0700	Stop	1530

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

HOURS - ITEM NO.

EQUIPMENT AND/OR LABOR:			Regular	OT						IDLE OR DOWN	REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)									Name	Contractor
		Iron worker Foreman	8	0							E.J Meyer III	ABF/JV
		Iron worker Jrny	8	0							Chris Biskner	ABF/JV
		Iron worker Jrny	8	0							Stanley Dalie	ABF/JV
		Iron worker Jrny	8	0							Kevin Ratcliffe	ABF/JV
		Iron worker Jrny	8	0							Mathew Cochran	ABF/JV
		Iron worker Jrny	8	0							Jerry Kubala	ABF/JV
		Labor	8	0							Froylan Ruiz	ABF/JV
		Labor	8	0							Ignacio Garcia	ABF/JV
		Labor	8	0							Jose Brado	ABF/JV
		Labor	8	0							Harmando	ABF/JV
		Labor	8	0							Carlos Garcia	ABF/JV
		OE	8	0							Mike Klein	ABF/JV
		OE	8	0							Daniel Martinez	ABF/JV
		OE	8	0							Dick Chafer	ABF/JV
1700 tons	1	Shear Leg barge										
240R boom	1	Ringer barge I										
260ft boom	1	Ringer barge II										
	2	Welding machine										
58084	1	RT 160 crane										
6 18 4293,4217	2	IR Compressor										
549 07 5006	1	Generator										
412 10 7101 417 40 5029	1	Forklift										
Wetar I,II,XII	3	Barge										
KRS 180 8 31B	2	Barge										
TEC 35,36,27	3	Barge										
YC 1333	1	Barge										
OC 260, 261, 262,265	4	Barge										

481 93 5006 481 40 7013	2	Man lift																		
----------------------------------	---	----------	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--


Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:


1. Temporary Tower G South: Tower erection.
2. Temporary Tower F : Tower base grouting.

Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TT trusses.
2. Field work:
 - ABF's iron worker crew continued bolting/tightening TTG South – West leg.
 - ABF's labor crew poured grout under tower base plates at TTF North and South with Sika grout 212.
 - Joel Nadler from Smith Emery was present to take one set of grout cubes of quality testing.
3. Conversation and discussion:
 - Tower pocket (TTF South@ North West conner pocket) gaps are > 12mm – Photos attached.
4. Overtime reason:

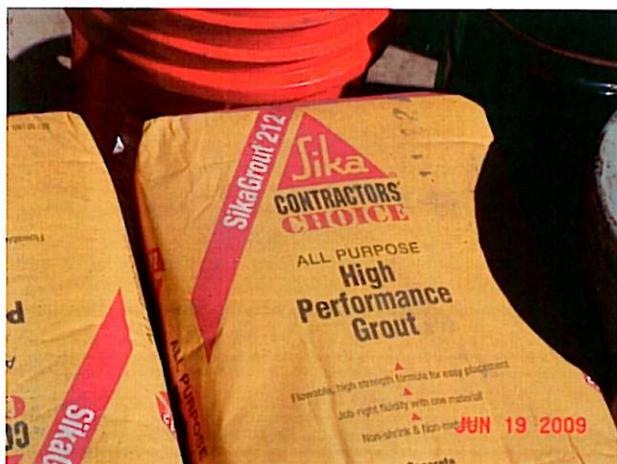


Sika Grout materials

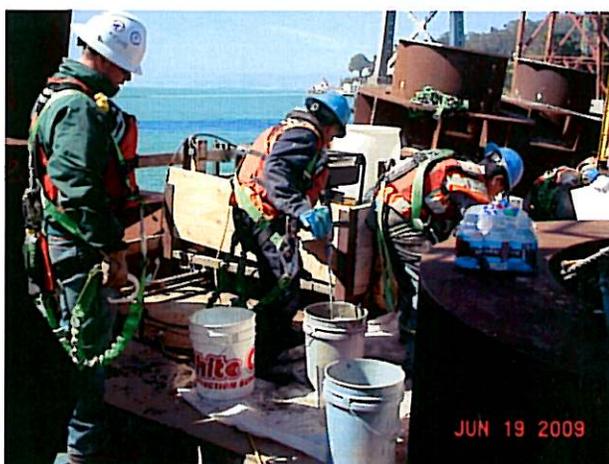

Grouting operation



North of North West conner pocket

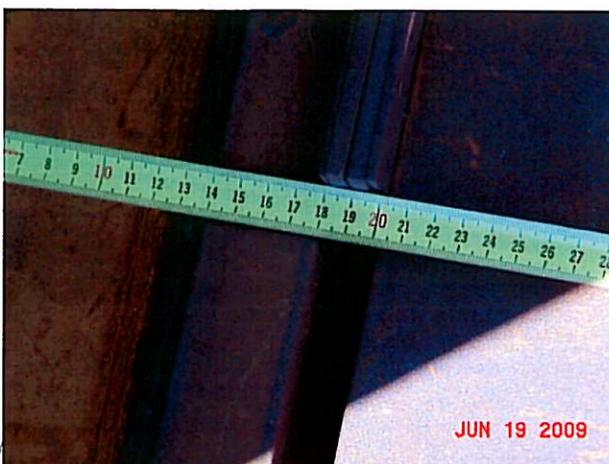

South of North West conner pocket

Thanh V Le

Trans Engineer (D)/Asst. Struct. Rep
