

Job Stamp

04-0120F4
SFOBB SAS

Const. Calendar Day No 993

Project Work Day No. 1203

Date 09/01/2009

Shift Hours Start 6:30 Stop 3:30


Inspector Shift 7:00 AM to 3:30 PM

ASSISTANT STRUCTURAL
REPRESENTATIVE.

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEEN	DESCRIPTION (Of Equipment or Labor)	Regular	Over Time	Surveying							IDLE OR DOWN	Name	Contractor
		1 Temp tower and trusses												
		Iron Worker Foreman	8										Ed Meyer	ABF/ JV
		Iron Worker App.	8										Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8										Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8										Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8										Kevin Ratcliffe	ABF/ JV
		Iron Worker App.	8										Chris Biskner	ABF/ JV
		Iron Worker Foreman											Carlos Valverde	ABF/ JV
		Iron Worker Jrny											Steven Batiste	ABF/ JV
		Iron Worker App.											Jose Morales	ABF/ JV
		Iron Worker Jrny											James Wilkerson	ABF/ JV
		Iron Worker Jrny											Josue Galvan	ABF/ JV
		Iron Worker Jrny											Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8										James Sturgeon	ABF/ JV
		Iron Worker	8										Troy Christianson	ABF/ JV
		Iron Worker	8										Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic	8										Ronald Damerl	ABF/ JV
		Iron Worker App.	8										Paul Good	ABF/ JV
			8										Eduardo Jimenez	
		Iron Worker Jrny	8										Serina Lafleur	ABF/ JV
		Iron Worker Jrny	8										Casey Lux	ABF/ JV
		Iron Worker Jrny	8										Mike Maday	ABF/ JV
		Iron Worker Jrny	8										Barry Rothman	ABF/ JV
		Iron Worker Jrny	8										Jaime Baragan	ABF/ JV
		Iron Worker Foreman	8										David Lucero	ABF/ JV
		Iron Worker Jrny	8										Matt Holt	ABF/ JV
		Iron Worker Jrny	8										James Laahs	ABF/ JV
		Iron Worker Jrny	8										Aaron Kent	ABF/ JV
		Iron Worker Jrny	8										Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8										Obra Paulk	ABF/ JV
		Crane Operator	8										Rodney Anderson	ABF/ JV


REC'D H31 OCT 05 #011083
Report day 955

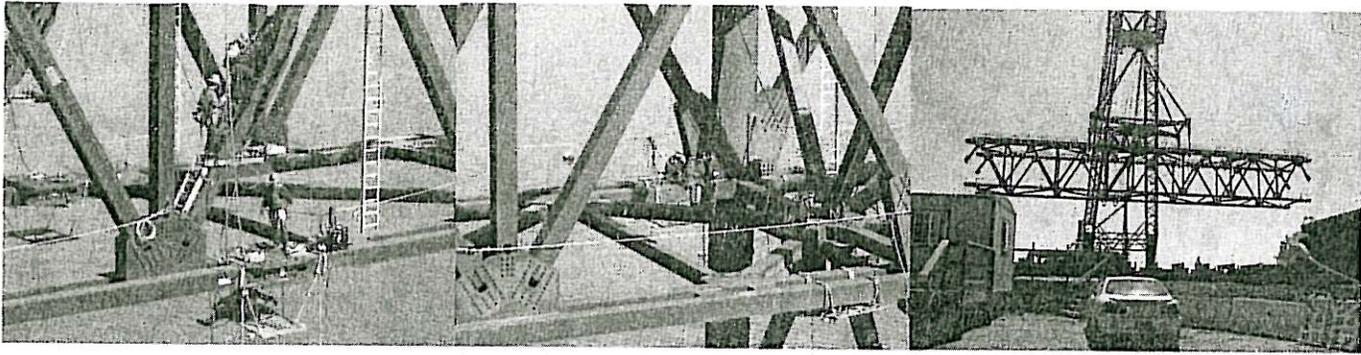

1. Installing stiffener plate at mid section of lower crosses bracing of truss connecting two gusset plates together over the tower C at W line.
2. Bolting, snug tightening and torquing of bolts on connection plates connecting truss with tower G.
3. Bolting, snug tightening of bolts and torquing of bolts in gusset plates at lower chords, diagonal members and upper chords of truss in field splice 13 at W line is in progress.
4. Installing new connection plates for upper chord cross beam WD at PP-E40 in E line truss, this cross beam's holes were not aligned with the original connection plate's pre-drilled holes. The holes in web of the beam were not matching with new connection plate therefore iron worker widened the holes in beam by torch cutting.
5. Jacking and setting shim for leveling pedestal hats at W line truss is in progress.
6. Welding angle iron 25 X 25 X 4mm on top of pedestals to hold the neoprene pad in W line.
7. Picking truss segment 12 from the berth 7 dockyard by Shear Leg and loading it on barge for splicing with segment 13.

Miscellaneous

Additional Work on/off site:

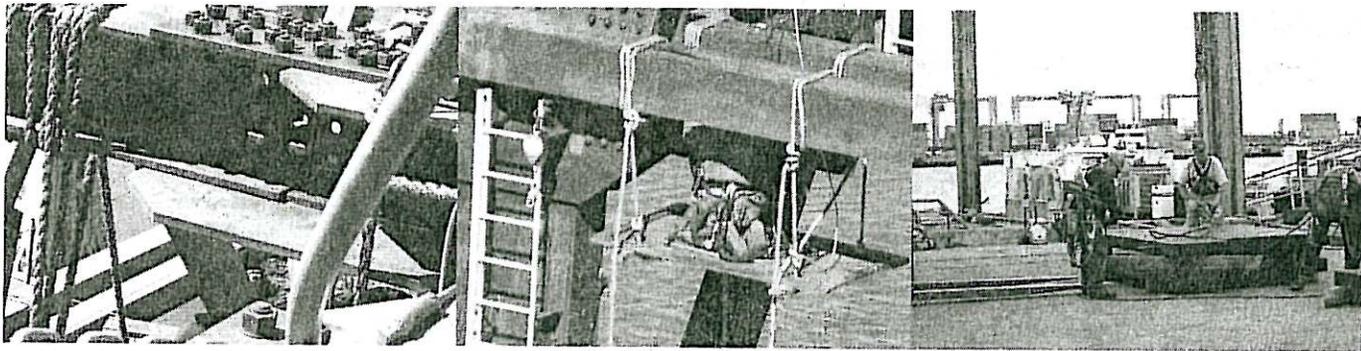

1. Sorting bolts to be used for splicing truss sections.
2. I attended staff meeting at 8.00 am.
3. Miscellaneous works.

Inspector:

Masoud Modanlou  Trans Engineer (C)/Asst. Struct. Rep
