

Job Stamp

04-0120F4  
SFOBB SAS

Const. Calendar Day No 1015

Project Work Day No. 1225

Date 09/23/2009

Shift Hours Start 6:30 Stop 3:30

Inspector Shift 7:00 AM to 3:30 PM


ASSISTANT STRUCTURAL  
REPRESENTATIVE.

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.								REMARKS		
Equip. #	NO. MEM.	DESCRIPTION (Of Equipment or Labor)	Regular	Over Time	Surveying					IDLE OR DOWN	Name	Contractor
	1	Temp tower and trusses										
		Iron Worker Foreman	8								Ed Meyer	ABF/ JV
		Iron Worker App.	8								Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8								Stanley Dalle	ABF/ JV
		Iron Worker Jrny	8								Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8								Kevin Ratcliffe	ABF/ JV
		Iron Worker App.	8								Chris Biskner	ABF/ JV
		Iron Worker Foreman									Carlos Valverde	ABF/ JV
		Iron Worker Jrny									Steven Batiste	ABF/ JV
		Iron Worker App.									Jose Morales	ABF/ JV
		Iron Worker Jrny									James Wilkerson	ABF/ JV
		Iron Worker Jrny									Josue Galvan	ABF/ JV
		Iron Worker Jrny									Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8								James Sturgeon	ABF/ JV
		Iron Worker	8								Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic	8								Ronald Damerall	ABF/ JV
		Iron Worker	8								Eduardo Jimenez	
		Iron Worker Jrny	8								Casey Lux	ABF/ JV
		Iron Worker Jrny	8								Mike Maday	ABF/ JV
		Iron Worker Jrny	8								Barry Rothman	ABF/ JV
		Iron Worker Jrny	8								Jaime Baragan	ABF/ JV
		Iron Worker Foreman	8								David Lucero	ABF/ JV
		Iron Worker Jrny	8								Matt Holt	ABF/ JV
		Iron Worker Jrny	8								James Laahs	ABF/ JV
		Iron Worker Jrny	8								Aaron Kent	ABF/ JV
		Iron Worker Jrny	8								Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8								Obra Paulk	ABF/ JV
		Crane Operator	8								Rodney Anderson	ABF/ JV
		Crane Operator	8								Ernie Hamilton	ABF/ JV
		Crane Operator	8								Mike Klein	ABF/ JV
		Oiler	8								Daniel Martinez	ABF/ JV

RECT H31 OCT-16 #011240




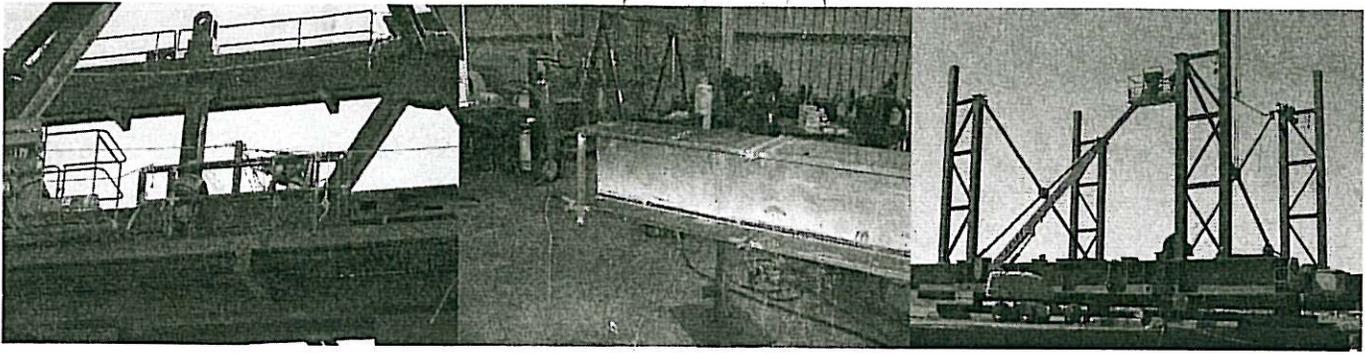

1. Swapping of bolts in field splice W 18 between truss segments 13 and 14 W line. These trusses were temporary spliced for shipment from China.
2. Running lifeline cable along the lower chords of assembled truss segments 12, 13, and 14.
3. Welding a new piece on built up cross beam PP – E40 is completed and Michael Janson ABF weld inspector (QA) preformed UT.
4. Welding angle iron 25 X 25 X 4 mm on top of OBG pedestals are in progress in E line and W line.
5. Erections of towers with cross bracing on top of OBG cradle L4 W. These towers are parts of a superstructure supporting OBG cross beam erection Gantry.

### Miscellaneous

#### Additional Work on/off site:

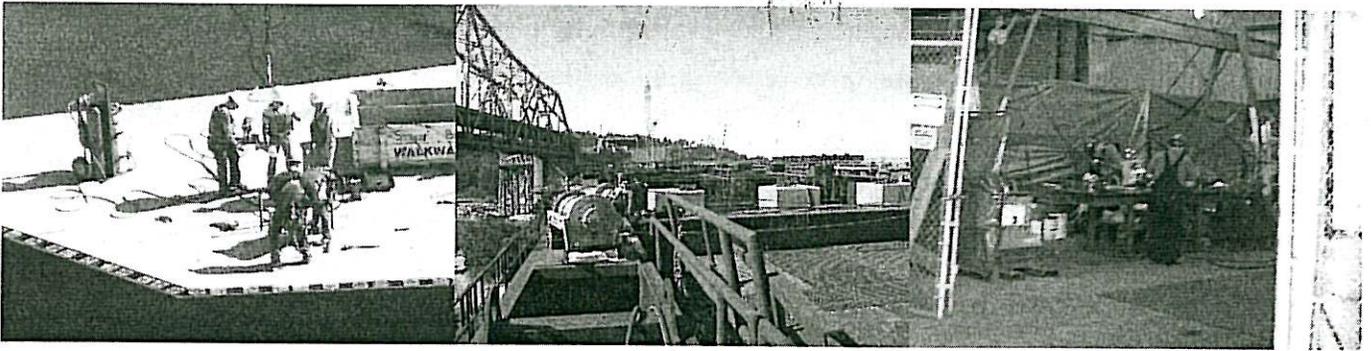

1. Sorting bolts to be used for splicing truss sections.
2. Removals of tower H anchor bolts at North footings of E2. About 10 anchor bolts were removed because of weak bonding.
3. Modifications and reparation works on pushing sled for pushing OBG cradle along the erected truss at E line.
4. Miscellaneous works.

#### Inspector:

Masoud Modanlou  Trans Engineer (C)/Asst. Struct. Rep
