

Job Stamp
04-0120F4
SFOBB SAS


Const. Calendar Day No 1017
Project Work Day No. 1227
Date 09/25/2009
Shift Hours Start 6:30 Stop 3:30
Inspector Shift 7:00 AM to 3:30 PM

ASSISTANT STRUCTURAL
REPRESENTATIVE.

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	Over Time	Surveying							IDLE OR DOWN	Name	Contractor
	1	Temp tower and trusses												
		Iron Worker Foreman	8										Ed Meyer	ABF/ JV
		Iron Worker App.	8										Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8										Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8										Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8										Kevin Ratcliffe	ABF/ JV
		Iron Worker App.	8										Chris Biskner	ABF/ JV
		Iron Worker Foreman											Carlos Valverde	ABF/ JV
		Iron Worker Jrny											Steven Batiste	ABF/ JV
		Iron Worker App.											Jose Morales	ABF/ JV
		Iron Worker Jrny											James Wilkerson	ABF/ JV
		Iron Worker Jrny											Josue Galvan	ABF/ JV
		Iron Worker Jrny											Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8										James Sturgeon	ABF/ JV
		Iron Worker	8										Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic	8										Ronald Damerai	ABF/ JV
		Iron Worker	8										Eduardo Jimenez	
		Iron Worker Jrny	8										Casey Lux	ABF/ JV
		Iron Worker Jrny	8										Mike Maday	ABF/ JV
		Iron Worker Jrny	8										Barry Rothman	ABF/ JV
		Iron Worker Jrny	8										Jaime Baragan	ABF/ JV
		Iron Worker Foreman	8										David Lucero	ABF/ JV
		Iron Worker Jrny	8										Matt Holt	ABF/ JV
		Iron Worker Jrny	8										James Laahs	ABF/ JV
		Iron Worker Jrny	8										Aaron Kent	ABF/ JV
		Iron Worker Jrny	8										Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8										Obra Paulk	ABF/ JV
		Crane Operator	8										Rodney Anderson	ABF/ JV
		Crane Operator	8										Ernie Hamilton	ABF/ JV
		Crane Operator	8										Mike Klein	ABF/ JV
		Oiler	8										Daniel Martinez	ABF/ JV

REC'D H31 OCT 16 #01124E

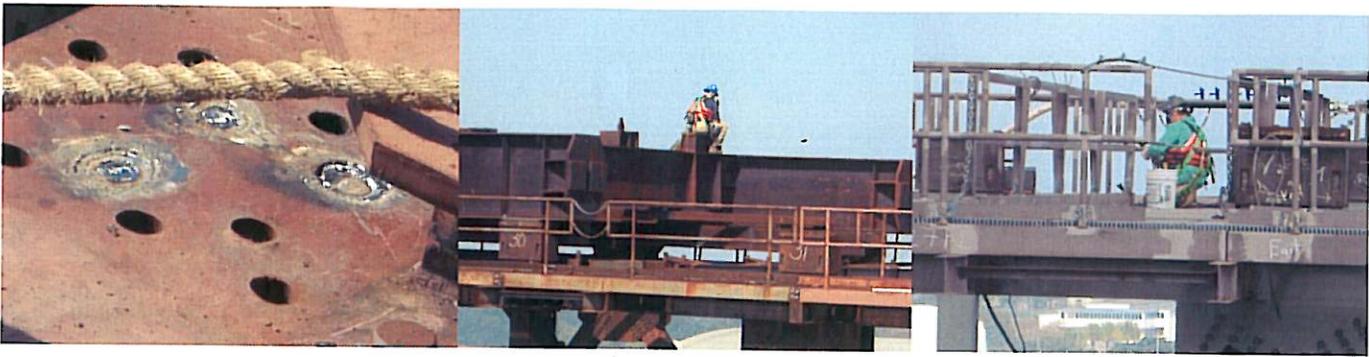

1. Swapping of bolts in field splice W 18 between truss segments 13 and 14 W line. These trusses were temporary spliced for shipment from China.
2. Repairing damaged holes on gusset plate at PP – E40. The holes on this gusset plate were enlarged by torch cut and were rejected.
3. Surveyors are checking the elevation and the alignment of newly installed OBG cradle at W line.
4. Welding angle iron 25 X 25 X 4 mm on top of OBG pedestals are in progress in E line and W line.
5. Welding steel brackets on tower H column for erection on ladder.
6. Rerouting power cables from the main generator at pier W 2 footing area to electric switch box installed on top of soffit deck for power distribution.

Miscellaneous

Additional Work on/off site:



1. Sorting bolts to be used for splicing truss sections.
2. Preparation for pushing cradle L1 E at E line.
3. Shipping gantry's superstructure beams to berth 7 dockyard for installation preparation work. This superstructure will be used for erection of main crossbeam between east and west OBG.
4. Miscellaneous works.

Inspector:

Masoud Modanlou  Trans Engineer (C)/Asst. Struct. Rep
