



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 022 Const Calendar Day: 182 Date: 09-Mar-2010 Tuesday
 Inspector Name: Wilcox, Jason Title: Transportation Engineer
 Inspection Type: Intermittent
 Shift Hours: 06:30 AM 17:00 PM Break: 00:30 Over Time: 02:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Liu, Tai-Lin Approved Date: 18-May-10 Status: Approved

Weather

Temperature 7 AM 40 - 50 12 PM 50 - 60 4PM 50 - 60
 Precipitation Condition Overcast, Windy

Working Day If no, explain:

<p>Diary:</p> <p>OBG Bolting & Welding</p> <p>FIELD WORK:</p> <p>Crossbeam 1 was picked and placed today. This took most of the workers away from production work on the splices in regards to bolting.</p> <p>E-Line:</p> <p>Splice 1: * Top Deck weld already completed. Grinding in preparation for U/T started and repairs needed. Repairs started as well. * Bottom Plate stiffeners completed. U/T testing of the stiffeners started yesterday and continue today. * Welding of the South Side Plates started today. They started at the center section and were able to place 6 passes by the end of the day. * Place permanent bolts in the North U-ribs.</p> <p>Splice 2: * First 14 U-ribs were torque tested going North to South. * Bottom Plate seal weld started on the 3E side. * Top Deck tack welding of the backing bar started today.</p> <p>Splice 3: * Measurements of the Longitudinal Diaphragm offsets taken and given to Tai-Lin Liu. Temporary splice plates fabricated on site so pins and bolts could be installed.</p> <p>Accrued 2 hours of overtime covering and documenting the Contractors operations.</p>	<p>Dispute</p> <p><input type="checkbox"/></p>
---	--

04-0120F4	Bid Item: 056	E-L02-ALB.056	E Line Lift 02 Align & Bolt
AMERICAN BRIDGE/FLUOR, A JV			

04-0120F4	Bid Item: 056	E-L02-WEL.056	E Line Lift 02 Weld
AMERICAN BRIDGE/FLUOR, A JV			

Diary: Dispute

Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Wilcox, Jason Diary #: 022 Date: 09-Mar-2010 Tuesday

OBG Bolting & Welding	056	E-L02-WEL.056	<input type="checkbox"/>
Welding of the Bottom Plate stiffeners continued today.			
Top Deck weld is complete. Grinding of the weld and the area around the weld for U/T throughout the day. Repairs also started today on the Top Deck weld.			
South Side Panel weld started this morning in the center section.			
04-0120F4	Bid Item: 056	X-L02-CBM.056	E-W Line Cross Over Lift 02 Cross Beam
AMERICAN BRIDGE/FLUOR, A JV			
Diary:			Dispute
OBG Bolting & Welding	056	X-L02-CBM.056	<input type="checkbox"/>
Crossbeam 1 was picked and placed today.			
04-0120F4	Bid Item: 056	E-L03-ALB.056	E Line Lift 03 Align & Bolt
AMERICAN BRIDGE/FLUOR, A JV			
Diary:			Dispute
OBG Bolting & Welding	056	E-L03-ALB.056	<input type="checkbox"/>
Torque testing of the U-Ribs continue today.			
04-0120F4	Bid Item: 056	E-L03-WEL.056	E Line Lift 03 Weld
AMERICAN BRIDGE/FLUOR, A JV			
Diary:			Dispute
OBG Bolting & Welding	056	E-L03-WEL.056	<input type="checkbox"/>
Welding of the backing bar to the bottom plate started this morning. This "sucks up" the backing bar to minimize the gap in the weld joint.			
The backing bar for the Top Deck was brought to within tolerance so welding could begin soon.			
04-0120F4	Bid Item: 056	E-L04-ALB.056	E Line Lift 04 Align & Bolt
AMERICAN BRIDGE/FLUOR, A JV			
Diary:			Dispute
General Comments	056	E-L04-ALB.056	<input type="checkbox"/>
Thanh Le and I took measurements of the 3E/4E Longitudinal Diaphragm offsets and gave the results to Tai-Lin Liu.			

Attachment

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Wilcox, Jason

Diary #: 022

Date: 09-Mar-2010


Tuesday



1E/2E South Side Panel welding



Crossbeam 1 erection

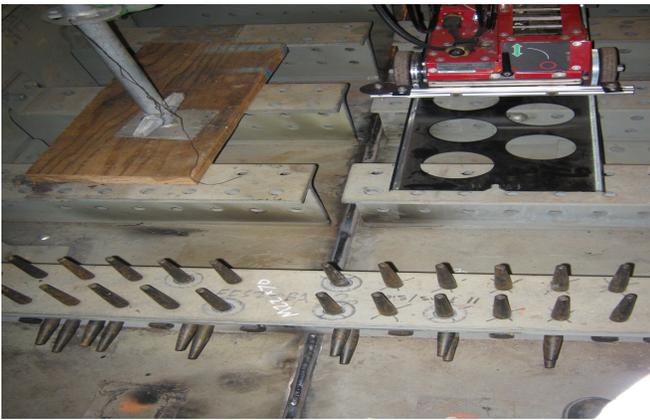

2E/3E Bottom Plate root weld started



Crossbeam 1 erected on the W-Line
