



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 057 Const Calendar Day: 513 Date: 03-Feb-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature	7 AM	12 PM	4 PM
Precipitation			Condition

Working Day If no, explain:

Diary:

Dispute

Work description.

SADDLE ADJUSTMENT

1. ABF crews completed eight West Saddle adjustment rods, and the carpenters are making secure access to the deck to facilitate future saddles adjustments. Most of the work was done on 02/02/2011 and the assembly completed at early time today.

- Ross, Scotty (Crane Op.)
- Rios, Gabriel (IWJ)
- Kubala, Jerry (IWF)
- Calzascia, Jonny (Laborer)

Equipment: G- GROVE ABF # 002363 crane

INSTALLMENT OF THE JACKING SADDLE GALLERY

2. The ABF crews started assembly of the jacking saddle gallery. And finish it at the end of the working hours. Please see the attached pictures.

- Alger, Bill (Crane Op.)
- Hernandez, Roberto (IWJ)
- Garcia, Richard (IWJ)
- Rios, Gabriel (IWJ)
- Kubala, Jerry (IWF)
- Calzascia, Jonny (Laborer)

Equipment: LIEBHERR LR 1300 crane

JACKING SADDLE

3. ABF crews had difficulty to taking out the one of the top bolts connecting the saddle to the frame (Please see the condition of the bolt). All the new bolts connecting the frame to the saddle are in place. ABF has decided to have the final bolt tightening after the load transfer.

4. ABF decided to make the hole slotted at both top and bottom back plate of the saddle frame as shown in the picture.

5. In the afternoon basting and paining of the jacking saddle frame started by the following ABF crews:

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 057

Date: 03-Feb-2011

Thursday

ABF Crews:

- Alcala, Javier
- Dougherty, Owen

SCAFOLDING AND HINGE K FRAMING

6. ABF crews continued working on the framing at Hinge K at the West side to make it ready for grouting. The water testing at west side is expected to be done on 02/04/2011.

ABF Crews

- Gary Pene
- Jasmin Goranyac

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 057

Date: 03-Feb-2011

Thursday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 057

Date: 03-Feb-2011

Thursday

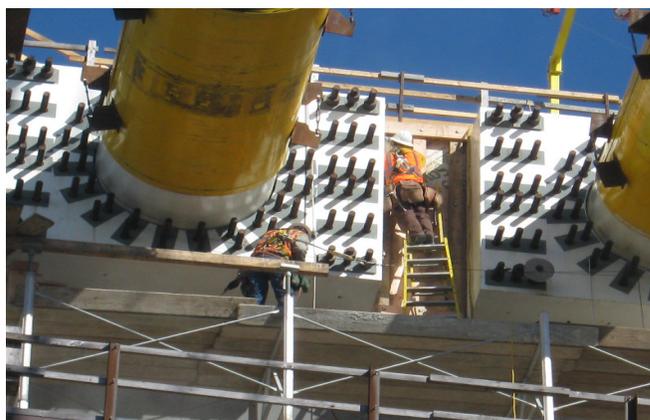

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 057

Date: 03-Feb-2011 Thursday

