



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 077 Const Calendar Day: 538 Date: 28-Feb-2011 Monday  
 Inspector Name: Khow, Sanny Title: Transportation Engineer  
 Inspection Type: Intermittent  
 Shift Hours: 07:00 AM 17:00 PM Break: 01:00 Over Time: 01:00  
 Federal ID:  
 Location:  
 Reviewer: Soheilifard, Saman Approved Date: 05-Mar-11 Status: Approved

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 12 PM 4PM  
 Precipitation Condition

Working Day  If no, explain:

04-0120F4 Bid Item: 053 T-L01-TNE.053 Tower Lift 01 Tower NE Erect structural steel (bridge tower)									
AMERICAN BRIDGE/FLUOR, A JV									
04-0120F4 Bid Item: 078 T-L02-ISW.078 Tower Lift 02 Internal Paint Tower SW									
CERTIFIED COATINGS COMPANY									
<b>Labor</b>									
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute	
Contractor: CERTIFIED COATINGS COMPANY									
Painter	FOR	MIKE GAYA	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Painter	FOR	TONY KATRONES	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
04-0120F4 Bid Item: 078 T-L02-ISW.078 Tower Lift 02 Internal Paint Tower SW									
AMERICAN BRIDGE/FLUOR, A JV									
CCO-096 Bid Item: 001 0-FSW-EFA.096 Field Site Work									
AMERICAN BRIDGE/FLUOR, A JV									
<b>Labor</b>									
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute	
Contractor: AMERICAN BRIDGE/FLUOR, A JV									
Ironworker	JNM	RICHARD GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
Ironworker	APP	IAN MURPHY	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
Ironworker	APP	TODD JACKSON	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
Ironworker	APP	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
Ironworker	JNM	ERIC SPARKS	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
Ironworker	APP	IAN MURPHY	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
Ironworker	JNM	RICHARD BAZEWICZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
Ironworker	FOR	FRANK BRAJKOVICH	8.00	2.00	0.00	10.00		<input type="checkbox"/>	
<b>Equipment</b>									
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Rental Company	Dispute	
Contractor: AMERICAN BRIDGE/FLUOR, A JV									

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Khow, Sanny

Diary #: 077

Date: 28-Feb-2011

Monday

002212	ALL TERRAIN VEHICLE, 4-WHEEL DRIVE	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>
002131	FORK LIFT TRUCKS	0.00	0.00	0.00	0.00	No	<input type="checkbox"/>

### Diary:

Dispute

#### General Comments 001 0-FSW-EFA.096

Caltrans and ABF hold a meeting to discuss the need for maintaining the minimum preheat temperature from beginning to three hours after the completion of the entire weld. The agreement from this meeting that the contractor will provide a cooling period for two hours after the completion of the weld.

ABF begins weld with two to three passes in the CJP joints and they will move to do two or three passes in the PJP joints.

Temperatures of skin plates are monitored with thermo gun and are found to be over 400 degree Fahrenheit.

The longitudinal and transverse plate temperatures are found to be over 200 degree Fahrenheit; these plates are heated manually with torch.


Mike Johnson is the QC inspector on the grillage welding.

ABF continues installing PTFE on Lift 4 facades.

Rick Clayborn and Gil Peralta names are not on the PMIV list.

Certified coating crew do some minor repair on the West shaft faying surface.

### Attachment

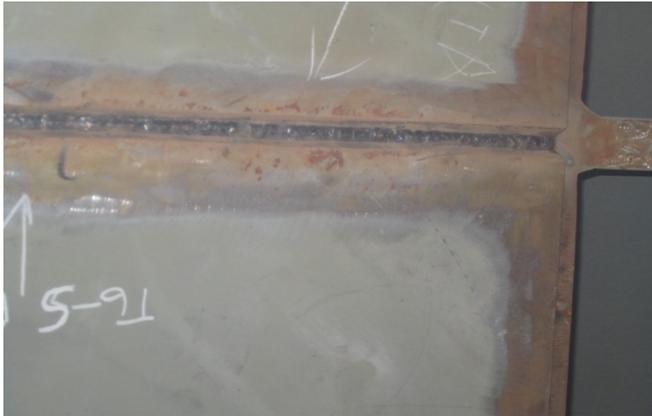

---

**Daily Diary Report by Bid Item**

**Job Name:** 04-0120F4

**Inspector Name:** Khow, Sanny

**Diary #:** 077

**Date:** 28-Feb-2011

**Monday**

---

