



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 253 Const Calendar Day: 543 Date: 05-Mar-2011 Saturday

Inspector Name: Bruce, Matt Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time: 08:00

Federal ID:

Location:

Reviewer: Mathur, Lalit Approved Date: 11-Apr-11 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 50 - 60 4PM 40 - 50
 Precipitation 0.29" Condition Partly cloudy to overcast

Working Day If no, explain:

Diary:


Dispute

Work description.

- See Lalit Mathur's diary for the erection of OBG lift 11W.
- Continued to gather, clean, and organize the grouting equipment that was used on Wednesday.
- Wrote outstanding diaries for the week including the diary for the Hinge K grouting operation on Wednesday March 2, 2011.
- Began to write the TL-502 forms related to the twelve sets (3 cubes in a set) taken during the Hinge K grout pad operation.
- Continued to observe and investigate the cradle offset for OBG lift 11W with the W-Line temporary truss pedestals.



Attachment

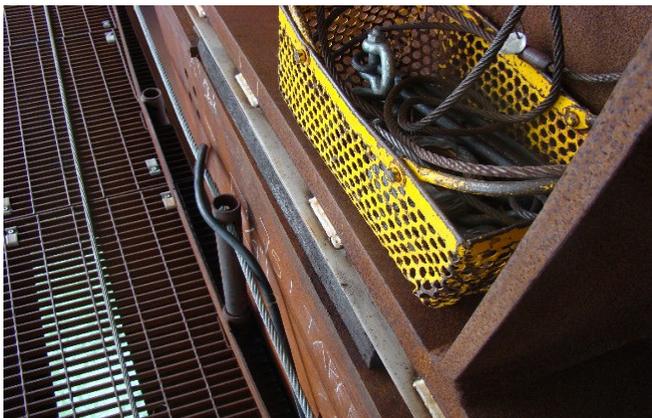

The edge of the cradle for OBG lift 4W was approximately even with a pedestal on the south side of the W-Line temporary truss.



The edge of the cradle for OBG lift 11W was approximately 65mm towards the north of a pedestal on the south side of the W-Line temporary truss.

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Bruce, Matt

Diary #: 253

Date: 05-Mar-2011

Saturday



ABF erecting OBG lift 11W onto the temporary truss.



The edge of the cradle for OBG lift 7W was approximately 35mm towards the north of a pedestal on the south side of the W-Line temporary truss.
