



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 11:37 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 326 Const Calendar Day: 643 Date: 13-Jun-2011 Monday
 Inspector Name: Bruce, Matt Title: Transportation Engineer
 Inspection Type: Intermittent
 Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:
 Federal ID:
 Location:
 Reviewer: Mathur, Lalit Approved Date: Status: Submit

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 60 - 70 4PM 60 - 70
 Precipitation 0.00" Condition Mostly sunny w/moderate winds

Working Day If no, explain:

Diary:

Dispute

Work description.

- Addressed miscellaneous surveying issues on the project related to OBG (bikepath) and cable works.
- Refer to Lalit's diary for more details regarding ABFs operation, labor, and equipment for preparations for the Shear Key and Bearing work at the E2 cap beam. See the photos below for additional details and comments.
- Refer to Abbas Iranmanesh, John Lyons, and Roman Granados's diaries for more details regarding the W-Line backspan catwalk erection operation, labor, and equipment. See the photos below for additional details and comments.

Attachment



ABF surveyors placing a pipe w/reflectors on one of the "U" frames of the W-Line backspan catwalk, which will be used to set the sag of the catwalk.



ABF in the process of erecting the W-Line backspan catwalk.



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Bruce, Matt

Diary #: 326

Date: 13-Jun-2011

Monday



The W-Line backspan catwalk pinned to the saddle bracket support.



ABF resuming placing bikepath panels on the brackets attached to the E-Line OBG.




Closeup photo of the free hanging pipe with reflectors.



Preparations are being made for the Shear Key and Bearing work at the E2 cap beam.



ABF in the process of erecting the W-Line backspan catwalk.

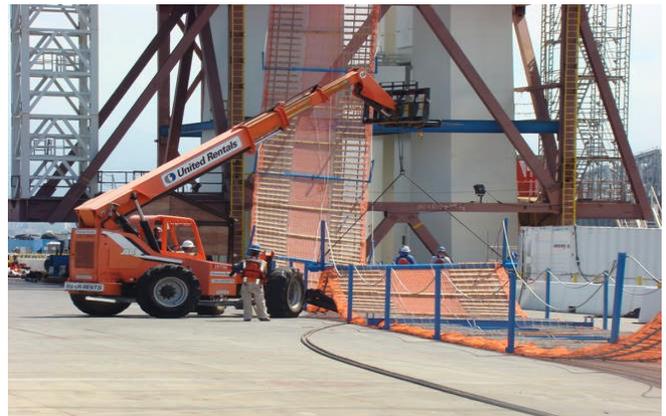

Kinks in the catwalk were observed while in the process of erecting the W-Line backspan catwalk.

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Bruce, Matt

Diary #: 326

Date: 13-Jun-2011

Monday



Kinks in the catwalk were observed while in the process of erecting the W-Line backspan catwalk.



Bikepath panel 9-11 where the north end near PP9 seen in the photo is still not bearing on the bracket after the panel was removed to place trav. Rail



ABF in the process of erecting the W-Line backspan catwalk.



Bikepath panels 9-11 and 11-13 were placed for a second time over the weekend after the traveler rail was placed.



Working platform mobilized at the new E2 pier in preparation for the upcoming Shear Key and Bearing work at the E2 cap beam.



ABF ironworkers getting ready to pin the W-Line backspan catwalk to the saddle bracket support.
