



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 167 Const Calendar Day: 720 Date: 29-Aug-2011 Monday
 Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer
 Inspection Type: Intermittent
 Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00
 Federal ID:
 Location:
 Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 70
 Precipitation None Condition partly

Working Day If no, explain:

Diary:

Dispute

Work description.

ABF Crews activities:



1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" as follows:

A) WELDING:

- With respect to drawings No. DE419PE, DE419QT (SECTION B & SECTION C) and DE419RT (DETAIL 27), the sheave bracket return part of the haul rope was welded on framing system connected to the pier 2 wall (Between saddles).
- More welding work was performed on a few Rail Beam connections to each other (previously bolted connection).

B)The chain holding the framing system to the pier 2 wall was released at a few locations. However, the deflections and its effect on the PWS hauling system have not been measured yet.

C) INSTALLATION:

- The Trolley removed and set up in the correct direction, shown in the picture.
- The ABF crew continued installment of the hanger rods, drawings No. DE419HT and DE419JT. The paint on the rods were removed, the rods covered with a thin touch of grease before installment. The pipes which were clogged by some steel particles or weld were cut at those location and if it was needed a piece of pipe was welded. The process has not been completed yet.
- The bracket of the jacking system, Drawings No. DE419HT (DETAIL 15), DE419KT (DETAIL 15) was repositioned.
- All the bolts of the framing system were tightened.

2- The attached pictures show the detail of the performed activities.

NOTES:

- Scott Smith has been present from the beginning of the construction of the Secondary Hauling System and Brackets of the Primary Hauling System.

ABF crews involved in Secondary hauling system

A) Installation crews:

- Jerry Kubala (FOR- Installation)
- Walter Hernandez

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Iranmanesh, Abbas **Diary #:** 167 **Date:** 29-Aug-2011 **Monday**

- Melgar Fleix
- John Power
- Rigoverto Garcia
- Patrick Oleary
- Scott Ross (Crane Operator)

- B) Welding Crews
- Salvador Sandoval
 - Michael Jimenez
 - Erick Sparks
 - Rick Clayborn
 - Paul Fambrini
 - Ian Murphy

ABF Equipments:
 Crane Terex RT160
 Miller welding machine (ABF002242)
 Miller Welding Machine (ABF002343)
 Miller Welding Machine (ABF002303)
 Lincoln Welding Machine (ABF002082)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)
 AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle
 AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	APP	IAN MURPHY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	PATRICK OLEARY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JOHN POWER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
		RICK CLAYBORN	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	PAUL FAMBRINI	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	ERIC SPARKS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	SALVADOR SANDOVAL	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELED	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW	5.00	0.00	0.00	0.00		No	<input type="checkbox"/>
*E0170406	WELDING EQUIPMENT	8.00	0.00	0.00	0.00		No	<input type="checkbox"/>
002243	WELDING EQUIPMENT	8.00	0.00	0.00	0.00		No	<input type="checkbox"/>
002154	Equipment, Crane, 60 Ton	8.00	2.00	0.00	0.00		No	<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Iranmanesh, Abbas **Diary #:** 167 **Date:** 29-Aug-2011 **Monday**

002242	WELDING EQUIPMENT				No	<input type="checkbox"/>
	8.00 0.00 0.00 0.00					
04-0120F4	Bid Item: 060	W-W2C-WDS.060	W Line W2 Cap West Deviation Saddle			
AMERICAN BRIDGE/FLUOR, A JV						
04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle			
AMERICAN BRIDGE/FLUOR, A JV						

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 167

Date: 29-Aug-2011

Monday

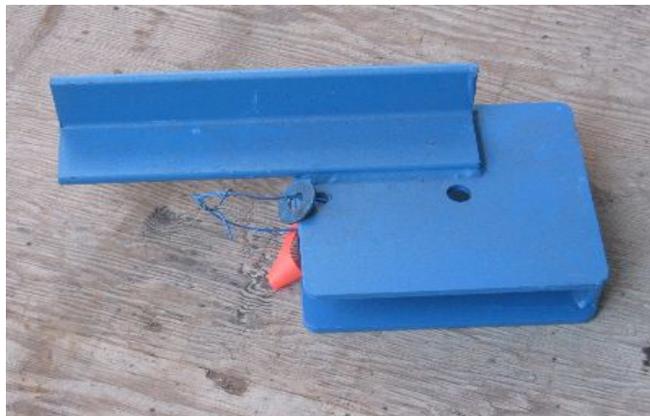

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 167

Date: 29-Aug-2011

Monday



Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 167

Date: 29-Aug-2011

Monday

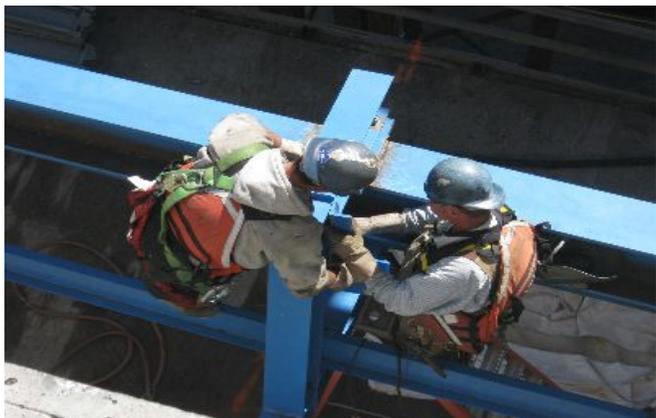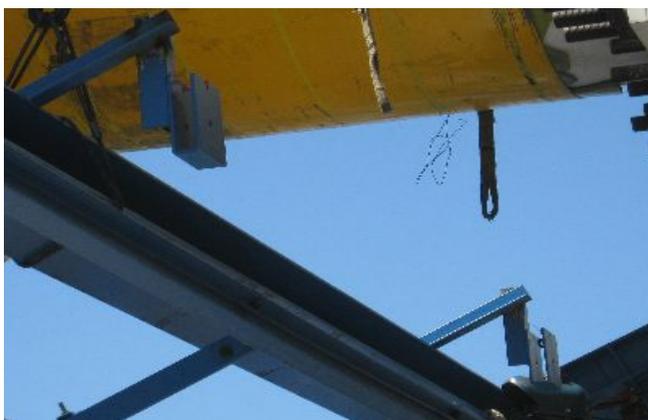

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 167

Date: 29-Aug-2011

Monday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 167

Date: 29-Aug-2011

Monday

