



**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:12 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 181 Const Calendar Day: 741 Date: 19-Sep-2011 Monday  
Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer  
Inspection Type: Intermittent  
Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:  
Federal ID:  
Location:  
Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

**Weather**

Temperature 7 AM 60 - 70 12 PM 4PM 70 - 80  
Precipitation None Condition Clear

Working Day  If no, explain:

<p><b>Diary:</b></p> <p><b>Work description.</b></p> <p>ABF Crews activities:</p> <p>1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and submittal ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System", as follows:</p> <p>INSTALLATION:</p> <ul style="list-style-type: none"> <li>•ABF crews continuing the installation of the UHMWP plates on the frames between the two saddles extending to the frames of the E-Line saddle per Detail 20 on the drawing sheets No. DE419OT of the submittal ABF-SUB-2171R01.</li> <li>•The ABF completed putting in place the machined tube (Bushing) inside the sheave shown in detail 15 and Section A of the sheet drawing No. DE419KT of The submittal ABF-SUB-2171R01. The bushing will help rotation of the sheave freely and is not as tight as before.</li> <li>•ABF crew trimmed partially the extra edges of the angle 3"x3"x1/4"which were welded to the steel channels to provide a truss type system to reduce the lateral deflection of the steel channels. The edges beyond the channel were trimmed as shown in the pictures.</li> <li>•The ABF crew added timbers at the required locations to provide safe use of the scaffolding.</li> <li>•ABF crew started putting in place the horizontal rollers at the E-Line saddle frames per Detail 3 and Section D of the sheet drawing No. DE419GT of the submittal ABF-SUB-2171R01.</li> <li>•The ABF crew started cleaning the added steel pieces which were added to stabilize the PWS framing system and the welds make it ready for painting.</li> </ul> <p>2- The attached pictures show the detail of the performed activities.</p> <p>ABF crew involved in the Secondary hauling system Installation crew: - Jerry Kubala (FOR. - Installation) - Walter Hernandez - Melgar Fleix - Rigovertto Garcia</p> <p>- PWS Frame trimmings:</p>	<p>Dispute</p> <p><input type="checkbox"/></p>
--	--



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Iranmanesh, Abbas    **Diary #:** 181    **Date:** 19-Sep-2011    **Monday**

-Ian Murphy  
-John Power

ABF crew involved in securing the use of scaffolding:  
-Rigoberto Campos(FOR.)  
-Victor Hernandez  
-Carlos Montejano

Equipments  
-Torch

**04-0120F4      Bid Item: 051      0-000-000.051      ERECT STRUCTURAL STEEL (BRIDGE)**  
AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      E-W2C-WDS.060      E Line W2 Cap West Deviation Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	VICTOR HERNANDEZ	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	RIGOBERTO CAMPOS	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	JOHN POWER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Equipment							Rental Company	
Equipment ID	Description		RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0220406	WELDING EQUIPMENT						No	
			0.00	0.00	0.00	0.00		<input type="checkbox"/>

**04-0120F4      Bid Item: 060      W-W2C-WDS.060      W Line W2 Cap West Deviation Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      X-W2C-JKS.060      E-W Line Cross Over W2 Cap Jacking Saddle**  
AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 181

Date: 19-Sep-2011

Monday



**Daily Diary Report by Bid Item**


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 181

Date: 19-Sep-2011

Monday

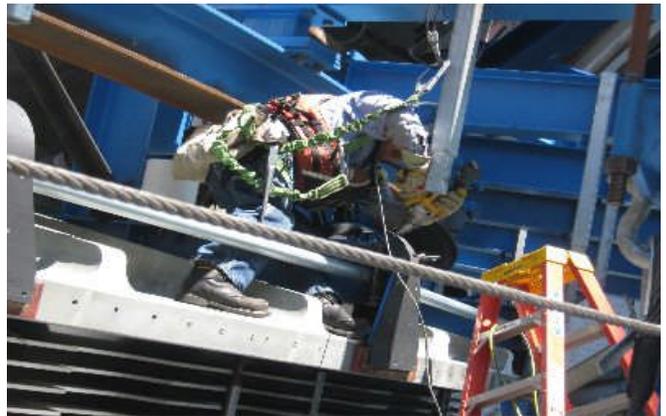

**Daily Diary Report by Bid Item**

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 181

Date: 19-Sep-2011

Monday



---

**Daily Diary Report by Bid Item**

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 181

Date: 19-Sep-2011 Monday

---

