



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 12:14 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 252 Const Calendar Day: 840 Date: 27-Dec-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 58

Precipitation None Condition Clear

Working Day If no, explain:

Diary:

Dispute

Work description.

INSTALLING THE FIRST PWS AT THE WEST LOOP

The ABF crew's activities are as follows:

- The ABF crews continued mostly forming the PWS at the last six feet of the upper portion of both the North and South Deviation Saddles. The ABF Engineer Mr. K. Baltzer was personally involved in forming the PWS at the upper portion of the North Deviation Saddle.
- The attached pictures are either showing the PWS at the Jacking Saddle in which the wires are in the correct position or the PWS at the South Deviation Saddle which shows wire crossing for the most length of the Deviation Saddle starting from the North End of the Saddle.
- Successive pictures were taken from the PWS wires position for both Deviation Saddles and submitted to Mr. Brian Boal for discussion with the designers.

Note: ABF Engineers, Mr. K. Baltezer, and Mr. A. Singh were present.

ABF Crews involved:

- Jerry Kubala
- Rigoverto Garcia
- Mike portillo
- Mike Draper
- Tony Miranda
- Ryan Nash
- Joseph Stone
- Luis Plancarte
- Lance Carlson
- Kevin Karber
- Ryan Evanchick
- Jim Benninghove

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV





Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Iranmanesh, Abbas Diary #: 252 Date: 27-Dec-2011 Tuesday

04-0120F4	Bid Item: 060	E-W2C-WDS.060	E Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 060	W-W2C-WDS.060	W Line W2 Cap West Deviation Saddle
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV			

Attachment

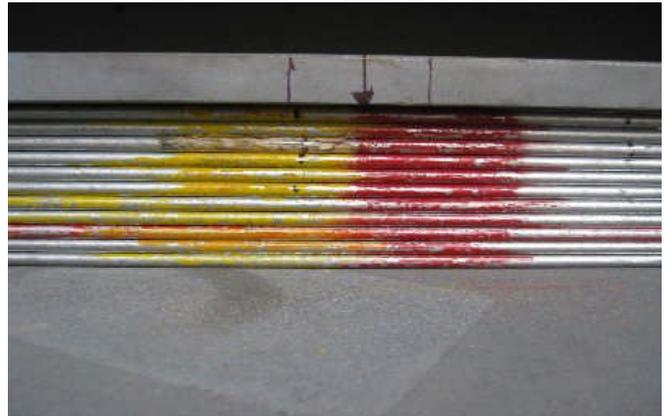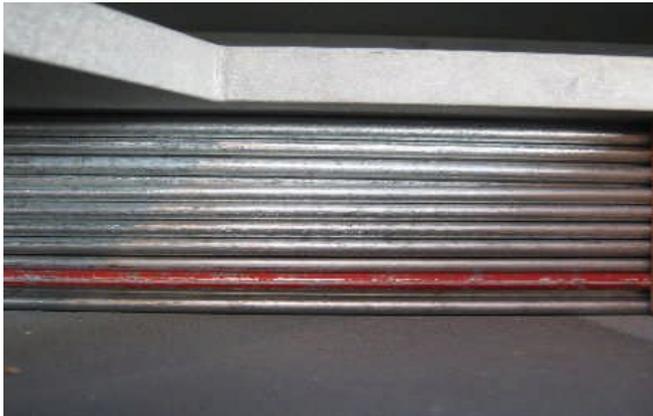

Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 252

Date: 27-Dec-2011

Tuesday

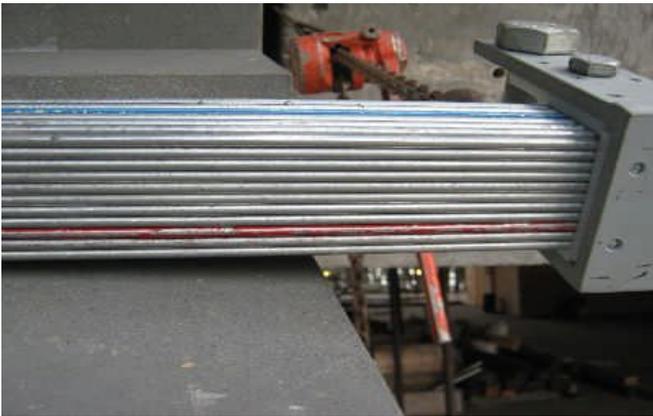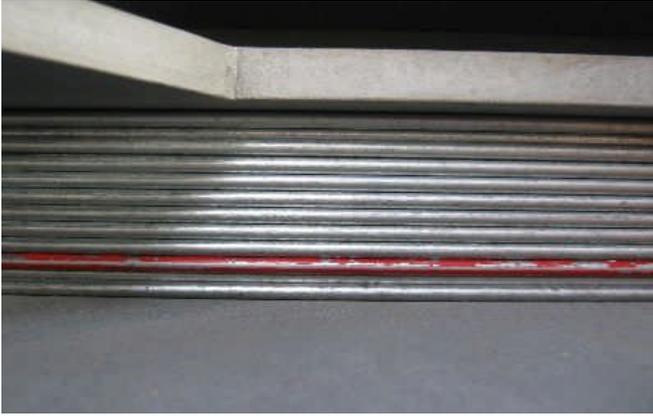

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 252

Date: 27-Dec-2011

Tuesday

