



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:04 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 257 Const Calendar Day: 862 Date: 18-Jan-2012 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 58
Precipitation None Condition Partly Cloudy

Working Day If no, explain:

Diary:

Dispute

Work description.

ABF Crews activities at Pier W2:

1. The PWS #3 is already inside the slot of the deviation saddles and the Jacking saddle. The ABF crews tried to pull the PWS by a few millimeters at the North Deviation saddle toward the tower in the North catwalk span by different alternatives in order to reduce the sag at the west loop and none of them were successful to overcome the friction force of PWS touching the saddle.

- The Hydraulic Arm is used to pull the PWS in the North direction.
- A pulley system and Come Along as shown in the picture was used.
- A Jacking system was set up at the East end of the North Saddle to push the PWS in the west direction.
- A jacking system was set up at the South end of the North deviation saddle to pull the PWS in the North direction.

2. The ABF crews started hauling the PWS # 5 by the Secondary Hauling system about 11.00 A.M. and connected the PWS socket to the Primary Hauling system about 11:50 A.M. The hauling of PWS # 5 was completed at 2:00 P.M.

3. The PWS # 4 which was installed to the Deviation Saddles on Jan. 17, 2012 has wire crossing in a length of about 7 feet at the South Deviation saddle. The issue has been reported by Mr. Victor Altamirano and Mr. Matt Bruce. No action is taken for correction by ABF so far.

ABF Crews involved at Pier W2:

- Jerry Kubala
- Rigoverto Garci
- Joseph Stone
- Ryan Nash
- Jonathan Canites
- Jim benninghove
- Tony Miranda
- Mike Draper
- Mike portillo
- Rick Sparks
- Paul Fambrini
- Ron Knarr

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 257 Date: 18-Jan-2012 Wednesday

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle

AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 257

Date: 18-Jan-2012

Wednesday

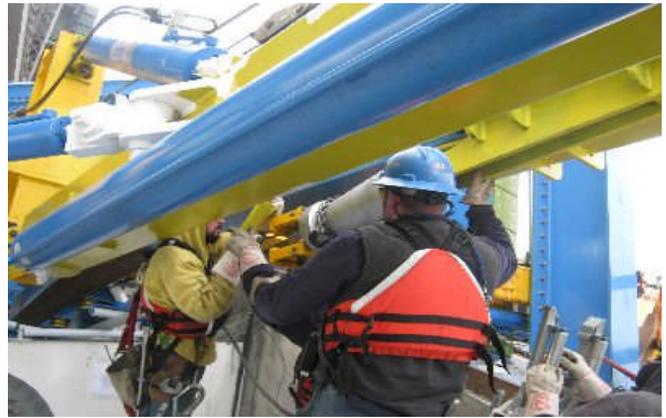

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 257

Date: 18-Jan-2012

Wednesday

