



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 12:49 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 285 Const Calendar Day: 914 Date: 10-Mar-2012 Saturday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 10:00

Federal ID:

Location:

Reviewer: Granados, Roman Approved Date: Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 4PM 50 - 66  
Precipitation None Condition Mostly cloudy

Working Day  If no, explain:

Diary:

Dispute

Work description.

MARCH 10, 2012 Diary

ABF Crews activities at the West Loop:

1.PWS HAULING, FLOATING, FORMING AND INSTALLATING:

•HAULING PWS # 91, PWS #92 and PWS # 93:

HAULING	START	TIME AT N.D.S.	TIME AT S.D.S.	END TIME
PWS # 91	Yesterday 6:34P.M.	7:25A.M.-7:36A.M.	7:52A.M.-8:01A.M.	9:38A.M.
PWS # 92	11:00A.M.	11:35A.M.-11:45A.M.	0:37P.M.-0:46P.M.	1:35P.M.
PWS # 93	3:19P.M.	4:07P.M.-4:46P.M.	4:31P.M.-4:41P.M.	Not

Completed

N.D.S.= North Deviation Saddle (Transfer of PWS from the Primary Hauling System to the Secondary Hauling System)

S.D.S. = South Deviation Saddle (Transfer of PWS from the Secondary Hauling System to the Primary Hauling System)

•FLOATING PWS # 91, PWS # 92 and PWS # 93:

FLOATING	CLAPM TO N.D.S.F.A	CLAPM TO S.D.S.F.A	FLOATING AT LOOP	FLOATING AT D.S.
PWS # 91	9:42A.M.-9:53A.M.	9:57A.M.-10:08A.M.	10:08A.M.	10:30A.M.
PWS # 92	1:45P.M-1:58P.M.	1:47P.M-2:16P.M.	2:25P.M.	2:40P.M.

N.D.S.F.A. = North Deviation Saddle Floating Arm

S.D.S.F.A. = South Deviation Saddle Floating Arm

•FORMING PWS # 90, PWS # 91 , PWS # 92 and PWS # 93:

FORMING	JACKING SADDLE	NORTH DEVIATIONSADDLE	SOUTH DEVIATION SADDLE
PWS # 90			7:00A.M.-



## Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 285 Date: 10-Mar-2012 Saturday

7:45A.M.  
PWS # 91 10:30A.M.-11:13 10:50A.M.-11:35A.M. 10:54A.M.-00:39P.M.  
PWS # 92 2:37P.M.-3:12P.M. 3:12P.M.-3:39P.M. 3:06P.M.-3:59P.M.

NOTE: For PWS #90 only the upper 20 feet remained from yesterday was completed

•INSTALLING PWS #90, PWS #91 , PWS #92 and PWS #93

INSTALLING	JACKING SADDLE	NORTH DEVIATIONSADDLE	SOUTH DEVIATION SADDLE
PWS # 90	7:00-A.M-7:44A.M.	7:15A.M.-7:45A.M.	7:46A.M.-8:26A.M.
PWS # 91	11:25A.M.-11:35A.M.	11:36A.M.-0:55P.M.	0:40P.M.-01:45P.M.
PWS # 92	3:13P.M.-3:38P.M.	3:40P.M.-4:20P.M.	4:00P.M.-4:36P.M.

•PWS # 90, PWS # 91, PWS # 92 and PWS # 93 SLACK ADJUSTMENTS:

SLACK ADJUSTMENT	SET UP HYDRAULIC PULLING SYSTEM	ADJUSTMENT TIME
PWS # 90 9:35A.M.	7:15A.M.	8:15A.M.-
PWS # 91 1:47P.M.	1:00P.M.	1:14P.M.-
PWS # 92 4:40P.M.	4:10P.M.	4:25P.M.-

SET UP AT LOWER END OF THE S.D.S.

### 2. NOTES:

- NOTE-1: PWS # 91 had a 90 degree twist at the S.D.S. which was removed by the Floating Arm clamp.
- NOTE-2: The ABF crew installed the 9th row of the N.D.S. and S.D.S. divider plates with respect to the bottom of the saddle.
- NOTE-3: The installed strands are checked for quality, PWS # 91 the second wire from the bottom is buried for 6 feet length at the N.D.S. (Attached picture)
- NOTE-4: ABF Engineer, Mr. Levi Gatsos and Superintendent Mr. Scott Smith were present.
- NOTE -5: 11 hours OT

ABF Crews involved at the West loop:

#### S.D.S.

-Jerry Kubala  
-Rigoverto Garcia  
-Ryan Nash  
-Jonathan Canites  
-Dario Loza

#### N.D.S.

-Ryan Evanchick  
-Jim Benninghove  
Tony Miranda  
-Mike Draper  
-Mike Portillo



## Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 285 Date: 10-Mar-2012 Saturday

J.S. and Slack Adjustment  
-Matthew Holt  
-Andy Zhen  
-Lonny Candelaria  
-Pablo Ramirez  
-Jonathon Biskner  
-Kevin Alger (OP. only 1/2 hour)


Equipment:  
Crane Grove (ABF002363, only 1/2 hour)

04-0120F4 Bid Item: 067 C-PWS-081.067 Install & Adjust PWS 81-85  
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-086.067 Install & Adjust PWS 86-90  
AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-091.067 Install & Adjust PWS 91-95  
AMERICAN BRIDGE/FLUOR, A JV

### Attachment

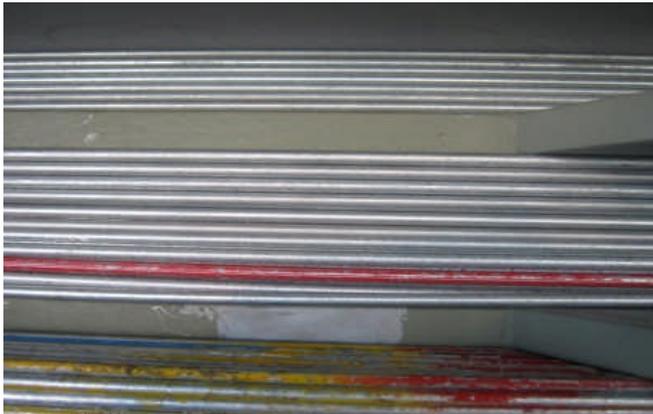

## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 285

Date: 10-Mar-2012

Saturday

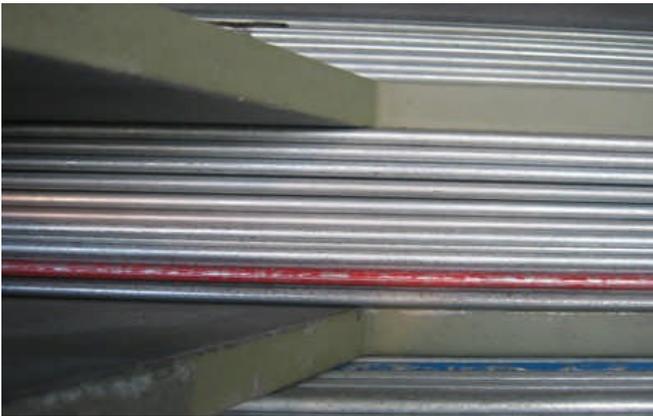

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 285

Date: 10-Mar-2012 Saturday

