



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 12:48 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 288 Const Calendar Day: 919 Date: 15-Mar-2012 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 11:00 am Break: Over Time:

Federal ID:

Location:

Reviewer: Granados, Roman Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 68
Precipitation None Condition Light Rain

Working Day If no, explain:

Diary:

Dispute

Work description.

MARCH 15, 2012 Diary

ABF Crews activities at the West Loop:

1. PWS HAULING, FLOATING, FORMING AND INSTALLATING:

•HAULING PWS # 98:

HAULING	START	TIME AT N.D.S.	TIME AT S.D.S.	END TIME
PWS # 98	8:20A.M.	9:48A.M.-9:59A.M.	Hauling stopped	Hauling stopped

N.D.S.= North Deviation Saddle (Transfer of PWS from the Primary Hauling System to the Secondary Hauling System)

S.D.S. = South Deviation Saddle (Transfer of PWS from the Secondary Hauling System to the Primary Hauling System)

•Floating PWS # 97:

FLOATING	CLAPM TO N.D.S.F.A	CLAPM TO S.D.S.F.A	FLOATING AT LOOP	FLOATING AT D.S.
PWS # 97	March 13	March 13	7:30A.M.	8:11A.M.

•Forming PWS 97:

FORMING	JACKING SADDLE	NORTH DEVIATIONSADDLE	SOUTH DEVIATION SADDLE
PWS # 97	8:05A.M.-8:35	8:26A.M.-9:17A.M.	8:23A.M.-10:06A.M.

•INSTALING PWS # 97

INSTALLING	JACKING SADDLE	NORTH DEVIATIONSADDLE	SOUTH DEVIATION SADDLE
PWS # 97	8:36-A.M-9:01A.M.	9:19A.M.-9:49A.M.	10:08A.M.-10:37A.M.



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 288 **Date:** 15-Mar-2012 **Thursday**

•PWS # 97 SLACK ADJUSTMENTS:

SLACK ADJUSTMENT	SET UP HYDRAULIC PULLING SYSTEM	ADJUSTMENT TIME
PWS # 97	9:25A.M.	9:32A.M.-
9:47A.M.		

SET UP AT LOWER END OF THE N.D.S.

2. NOTES:

- NOTE-1: The installed strand # 97 is checked for quality, and no issue was observed.
- NOTE-2: For the upper 8 feet at the S.D.S. either the first or the red wire of PWS # 97 are buried (Attached picture).
- NOTE-3: The work was stopped after installing PWS # 97 and hauling PWS 98 up to the jacking saddle at 11:00A.M.
- NOTE-4: ABF Engineer, Mr. Levi Gatsos and Superintendent Mr. Scott Smith were present.

ABF Crews involved at the West loop:

S.D.S.

- Jerry Kubala
- Rigovert Garcia
- Ryan Nash
- Jonathan Canites
- Joseph Stone
- Pablo Ramirez

N.D.S.

- Ryan Evanchick
- Jim Benninghove
- Tony Miranda
- Mike Draper
- Mike Portillo

J.S. and Slack Adjustment

- Matthew Holt
- Andy Zhen
- Lonny Candelaria
- Eduardo Jimenez Padilla
- Jonathon Biskner
- Carlos Alvarado
- Eduardo Jimenez Padilla

04-0120F4	Bid Item: 067	C-PWS-081.067	Install & Adjust PWS 81-85
AMERICAN BRIDGE/FLUOR, A JV			

04-0120F4	Bid Item: 067	C-PWS-086.067	Install & Adjust PWS 86-90
AMERICAN BRIDGE/FLUOR, A JV			

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 288 **Date:** 15-Mar-2012 **Thursday**


04-0120F4 Bid Item: 067 C-PWS-091.067 Install & Adjust PWS 91-95
 AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 067 C-PWS-096.067 Install & Adjust PWS 96-100
 AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	MICHAEL PORTILLO	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	RYAN NASH	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	RYAN EVANCHIK	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	FOR	JAMES BENNINGHOVE	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL DRAPER	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	CARLOS ALVERADO	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	FOR	MATTHEW HOLT	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	SHAOFEI ZHEN	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	LONNY CANDELARIA	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	PABLO RAMIREZ	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	JONATHON BISKNER	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	JNM	EDUARDO JIMENEZ-PADILLA	4.00	0.00	0.00	4.00		<input type="checkbox"/>
Ironworker	APP	Tony Miranda	4.00	0.00	0.00	4.00		<input type="checkbox"/>

Attachment

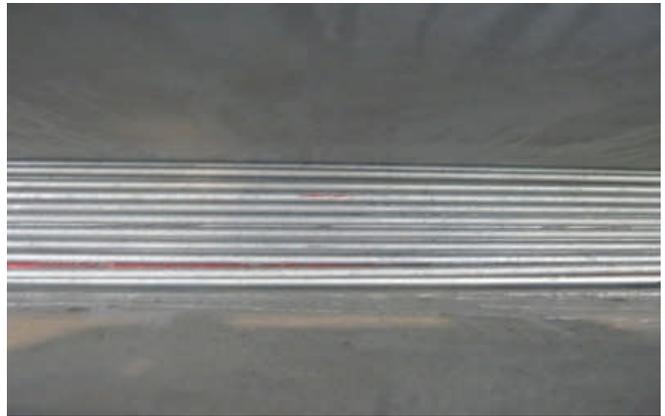

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 288

Date: 15-Mar-2012 Thursday

