



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 804 Const Calendar Day: 288 Date: 19-Mar-2013 Tuesday  
 Inspector Name: Bruce, Matt Title: Transportation Engineer  
 Inspection Type: Intermittent  
 Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:  
 Federal ID:  
 Location:  
 Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 40 - 50 12 PM 50 - 60 4PM 50 - 60  
 Precipitation 0.14" Condition Partly cloudy

Working Day  If no, explain:

**Diary:**


Dispute

**Work description.**

- Completed processing yesterdays surveying data performing a reciprocal trig-level from TWL270 and a point on the south tower head.
- Completed the surveying report for the T1 tower axial compression (shortening) and foundation settlement. Emailed the document to pertinent personnel within Caltrans.
- Checked on the status of the W2 cap beam Class 1 finish and crack repair before removal of the suspended platform. As of today these tasks have not been performed by ABF or their subcontractors.
- Prepared for future surveys including the SAS final AS-Built prior to opening the bridge to public traffic. Also informally observed the operation to remove the South Sidespan catwalks and went around the bridge looking for remaining work or punchlist items. See photos below for more details and additional comments.



**Attachment**

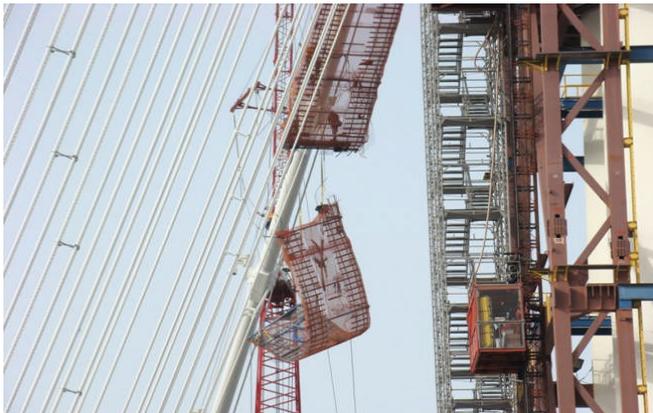

Lowering a section of the South Sidespan catwalk using the Manitowoc crane looking west.



Walking on the North Sidespan main cable looking east towards the South Sidespan catwalk removal operations.

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Bruce, Matt

Diary #: 804

Date: 19-Mar-2013 Tuesday



ABF laborers and ironworkers disassembling a removed section of the South Sidespan catwalk.



South Sidespan catwalk removal seen from the south tower head shaft.



Rebar placement for both the SAS and Skyway Hinge AE seismic joint blockouts.



Walking downhill on the South Sidespan main cable looking northeast towards the South Sidespan catwalk removal operations.



Hinge KW expansion joint construction looking south from the north edge of deck.



Completed concrete placement on the North end of the W2 cap beam for transverse tendon CBT1-15 blockouts.

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Bruce, Matt

Diary #: 804

Date: 19-Mar-2013


Tuesday



Removed anchor rods from one of the Shear Keys positioned over the E2 cap beam columns.



Walking downhill on the South Sidespan main cable looking northeast towards the South Sidespan catwalk removal operations.

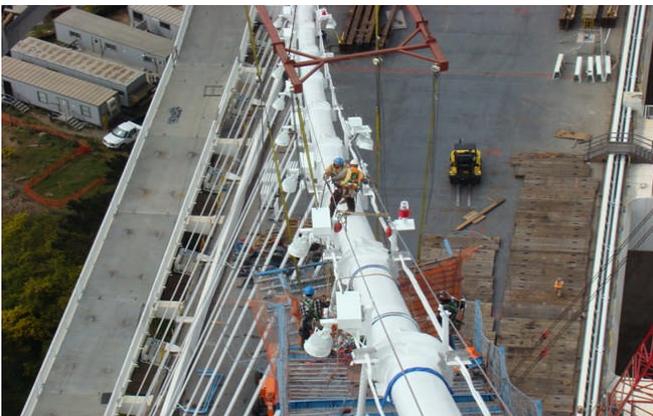

South Sidespan catwalk removal seen from the south tower head shaft.



West loop cable band and cable shrouds.



View of the remaining portion of the South Sidespan catwalk to be removed.
