



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:07 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 343 Const Calendar Day: 345 Date: 15-May-2013 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:00 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 66

Precipitation none Condition partly cloudy

Working Day If no, explain:

Diary:	Dispute
Work description.	<input type="checkbox"/>
05/15/2013	
Diary Wednesday May 15, 2013	
<p>The painters are continuing painting of the split collars after necessary washing and painting the suspender brackets after applying the anti rust paint before the final paint at the damaged spots. The painting is being completed from the west toward the East for both the W-line and E-line. The painters still have not completed the painting of the North side main cable at the West end.</p> <p>The Painters are painting the suspender cable separators and cable clamps at the top of the suspender cables by the help of a man lift.</p>	
<p>Other non- related cable work:</p> <p>The painters continued working on the barriers, removing stains, applying anti rust paint and making them ready for either complete or partial painting. The painting of the split collars and suspender brackets are being continued.</p> <p>The ABF crews are continuing installing the back plate of the barriers for both the E-Line and W-line. The ABF crew is continuing to disassemble the W2 falsework of the South side segment, and installing the lowering beam and jack assembly in order to lower the W2 falsework of the North side.</p> <p>The ABF crew was successful to cut one pipe pile of the erection tower at the South side and four on the North side and transfer them to pier 7 yesterday.</p> <p>Two ABF crews are involved in the disassembly of the erection tower and it is expected to remove most of the pieces up to deck level.</p> <p>The ABF subcontractor is continuing putting the polyester concrete overlay on the bike path.</p>	
Prepared by: Abbas Iranmanesh	

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 343

Date: 15-May-2013

Wednesday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 343

Date: 15-May-2013

Wednesday

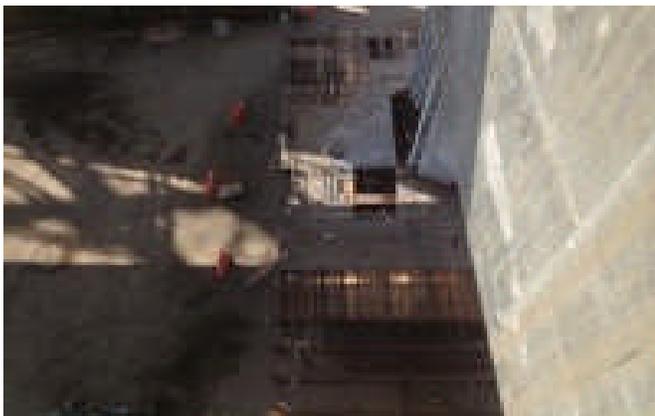

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 343

Date: 15-May-2013

Wednesday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 343

Date: 15-May-2013 **Wednesday**

